WAY4TECH SOLUTIONS


Live demo
construction.way4tech.com
w4demo / Demo2026 · Odoo 19

COMPLETE GUIDE · INTRODUCTION, SETUP AND EVERY SCREEN

Construction Management for Odoo 19

Projects, phases, bills of quantities, materials, labour, plant and subcontracts in the Base module, and the whole commercial side in Enterprise: tenders, measurement, RA bills and certificates, retention, variations, cost value reconciliation, site diary, QHSE, procurement and the client portal. Every screen and every step.

BASE ENTERPRISE

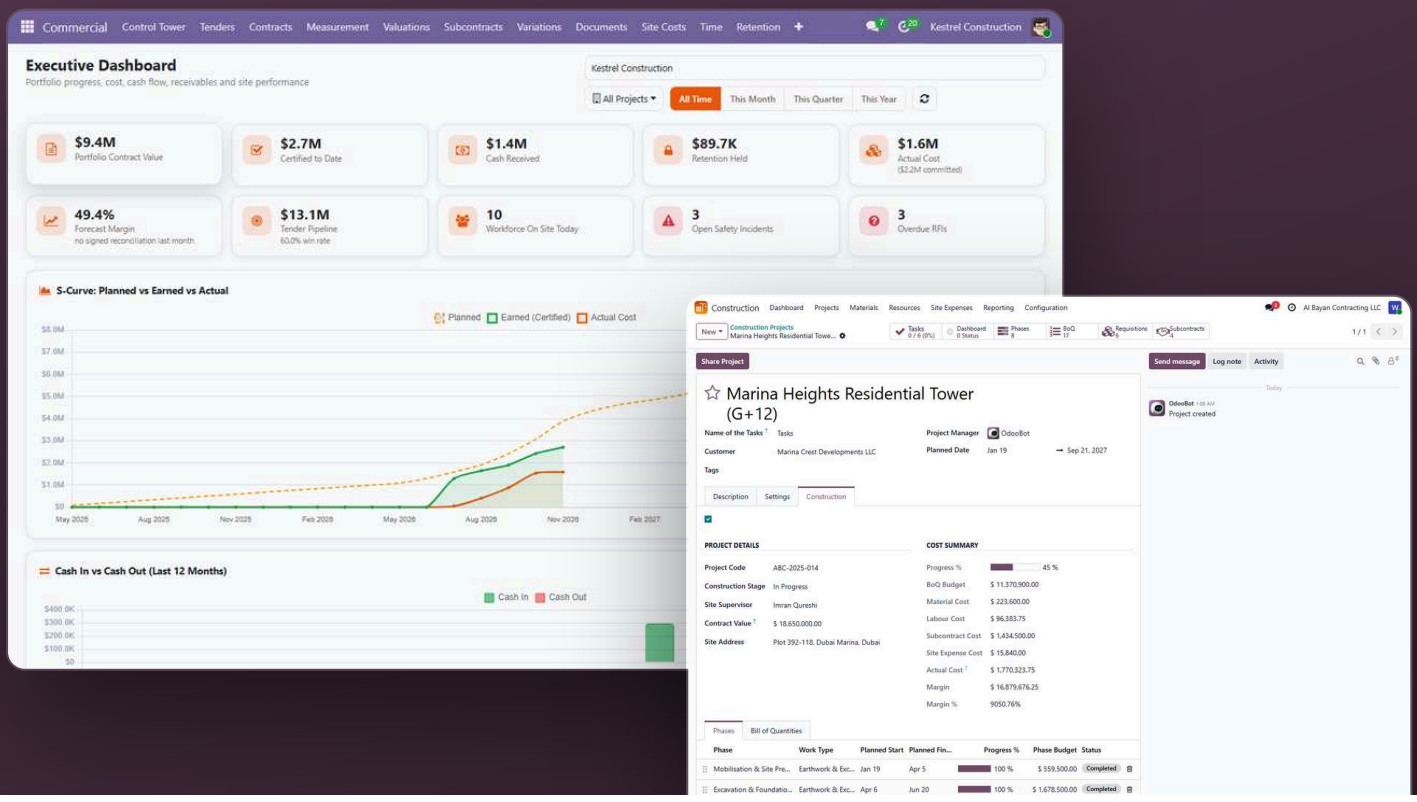

START

How to read this guide

This is one guide for one product: **Construction Management for Odoo 19** by Way4Tech. It comes as two modules that stack. The **Base** module turns an Odoo project into a costed construction job: phases, a bill of quantities, material requisitions, labour, equipment, subcontracts and site expenses. The **Enterprise** add-on sits on top and runs the commercial side and the site office: tenders, measurement, valuations and RA bills, retention, variations, cost value reconciliation, procurement, the site diary, QHSE, documents, the portal and the controls.

BASE

Construction Management, USD 10. Odoo 19 Community, needs Project, Employees and Invoicing.

ENTERPRISE

Construction Management Enterprise, USD 349 add-on. Needs the Base module installed first.

ODOO

A standard Odoo screen the modules build on, such as Purchase, Inventory or CRM.

Every part, section and step carries one of these tags, so you always know which module a screen comes from. Everything the Base module does is still there when Enterprise is added; Enterprise only adds.

> **Two sets of screenshots.** Screens tagged Base are taken on the live demo, **construction.way4tech.com**, where the worked example is a Dubai contractor with five jobs. Screens tagged Enterprise are taken on the Enterprise demo data that ships with the add-on, a contractor called Kestrel Construction with three jobs at different stages: a fit-out in the middle of the job, a civils job early on, and a residential block at final account. The figures in each set are invented demo data.

Who should read what

IF YOU ARE	READ
New to construction software	Part 1, how a contractor runs a job and gets paid, before anything else.
Choosing between Base and Enterprise	Part 2, the two editions side by side.
Setting the system up	Part 4, setup from zero, then Part 5 and Part 6 for the first job.
A site engineer or foreman	Parts 7 and 8 (Base), then 17, 19 and 22 (Enterprise).
A quantity surveyor or commercial manager	Parts 10 to 15.
A buyer or storekeeper	Part 16, procurement and site stores.
A director or owner	Part 15 (margin), Part 24 (controls) and Part 26 (dashboards).
Showing the product to someone	Part 29, the 15 minute demo, and Part 3 for the login.

What is in the guide

PART 1	How a contractor runs a job and gets paid	PART 2	The product at a glance
PART 3	Open the demo and sign in	PART 4	Set the company up from zero
PART 5	Construction projects	PART 6	Phases and the bill of quantities

PART 7 Materials and requisitions

PART 8 Labour, equipment, subcontracts and site expenses

PART 9 The Base dashboard and reports

PART 10 Tenders, CRM and client quotations

PART 11 Contracts, measurement and getting paid

PART 12 Variations, instructions, dayworks and provisional sums

PART 13 Retention and the final account

PART 14 Subcontract management

PART 15 Budget control, CVR and cash flow

PART 16 Procurement and site stores

PART 17 Work orders, job sheets, gangs and manpower

PART 18 Programme, schedule, delays and extension of time

PART 19 Site diary, weather and attendance

PART 20 Plant, tools, maintenance and petty cash

PART 21 Documents: RFIs, submittals, drawings and transmittals

PART 22 QHSE: permits, toolbox talks, incidents, inspections, NCRs and snags

PART 23 The client and subcontractor portal

PART 24 Control tower, approvals and month-end controls

PART 25 Roles and access control

PART 26 Dashboards

PART 27 Printed documents and Excel exports

PART 28 What runs by itself

PART 29 A 15 minute demo

PART 30 Questions people ask

PART 31 Menu map and feature index

PART 1 How a contractor runs a job and gets paid

A contracting job is won on a priced bill of quantities, built over months, and paid in monthly instalments for the work measured so far. The money is made or lost in the gap between what was built, what was certified and what it cost. This part explains that cycle in plain words, because every screen in the product is one step of it.

The bill of quantities is the job

Before a contractor builds anything, the work is written down as a **bill of quantities** (BoQ): every item of work with a unit, a quantity and a rate. "Excavate foundations, 1,240 m3 at 18.50" is one line. Added up, the bill is the price the client agreed to pay. It is also the budget: if the excavation was priced at 18.50 a cubic metre and it is costing 22, that line is losing money. Almost every record in this product points back to a bill item for that reason.

Measured, valued, certified, paid

A client does not pay the contract sum on day one. Each month the contractor **measures** what has been built against the bill, **values** it at the bill rates, adds agreed variations and dayworks, and **applies for payment**. The client's quantity surveyor checks it and issues a **payment certificate** for the amount they accept. In South Asia and the Gulf that monthly bill is often called a **running account (RA) bill**; in the UK and under FIDIC it is an interim valuation and an interim payment certificate. They are the same idea, and the product prints both.

The monthly money chain ENTERPRISE



Cumulative, not monthly

Every valuation is worked out **to date**: the total value of everything built since the start, less everything already certified. If last month over-measured a slab, this month measures the true quantity to date and the difference comes out by itself. A bill made from "this month only" carries every old mistake forward.

HOW IT WORKS

A worked example (figures are illustrative)

Gross value to date	400,000	everything built so far, at bill rates
Less retention 5%	20,000	held back by the client against defects
Less advance recovery	40,000	the mobilisation advance, paid back a slice each month
Net value to date	340,000	
Less previously certified	212,500	what earlier certificates already paid
Due this month	**127,500**	


Retention, advances and variations

Retention is a percentage the client keeps from every certificate, usually up to a cap, and gives back in two halves (moieties): one at practical completion and one after the defects period. Retention nobody chases is retention never collected. A **mobilisation advance** is paid up front and recovered from each certificate until it is cleared. A **variation** is any change to the work the client instructs: extra, less or different. A verbal instruction that is never confirmed in writing is the most common way contractors lose money, which is why the product puts a clock on it.

Committed, accrued and actual cost

Cost runs on a different clock from value. When a subcontract is let, the money is **committed** but not spent. When the subcontractor has done a month's work and not invoiced it yet, the cost is **accrued**. Only when the invoice is posted is it **actual**. A monthly **cost value reconciliation** (CVR) sets value earned against all three, which is the only honest margin a contractor has while the job is still running.

The whole job in one picture

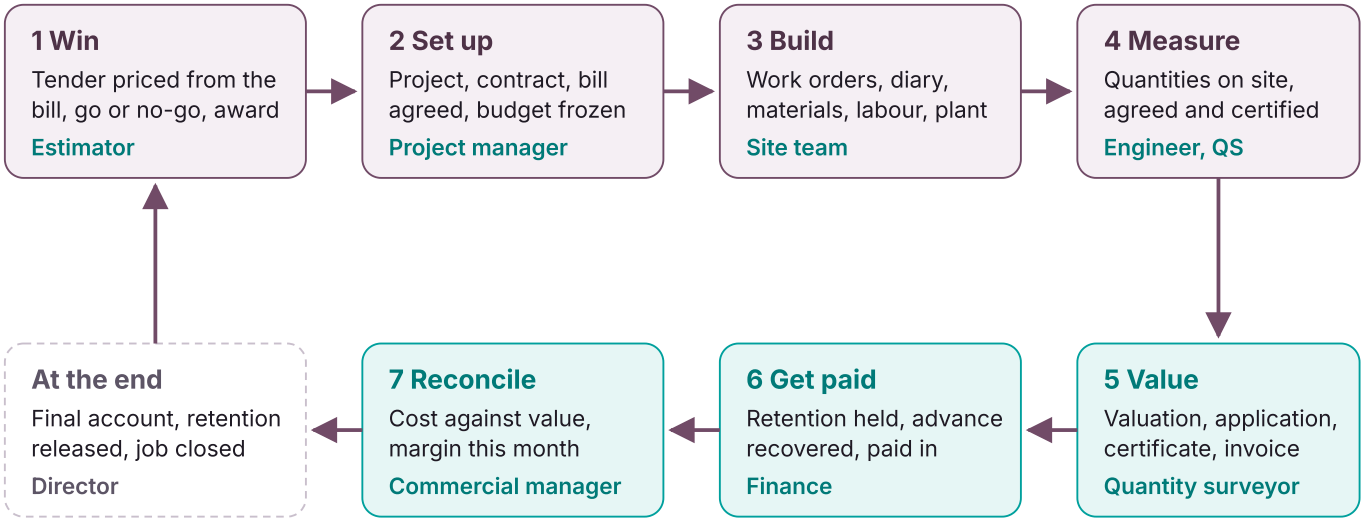

The Base module covers steps 2 and 3 with simple costing: what the job was budgeted at, and what it has cost. The Enterprise add-on covers every step, from the tender to the final account.

PART 2 The product at a glance


Two modules, two apps in the Odoo menu, and a set of roles that decide who sees what. This part is the map; every later part is one area in full.

Base and Enterprise side by side

Area	Base	Enterprise adds
Projects	Construction projects on Odoo Project: code, stage, supervisor, contract value, site address, live cost summary	Project team and team restriction, geofence, site store, templates, quality and safety counters
Bill of quantities	One flat list per job: work type, item, unit, quantity, rate, amount	Bills as documents with sections, revisions, cost rates, margin, templates, Excel import and export, rate library
Budget	BoQ total against actual cost, margin on the project	Budget, committed, actual and remaining per bill item, with a warn, block or approval policy
Materials	Requisitions: request, approve, issue, costed	Requests for quotation, quote comparison, purchase orders, goods received, three-way match, site stores
Labour	Daily labour logs by trade	Gangs, allocations against bill items, productivity norms, geofenced attendance, roll call
Plant	Equipment register with status	Plant hire with daily sheets, idle checks, maintenance by hours, custody, small tools
Subcontracts	Order with billed and paid figures	Packages and quote levelling, valuations, order variations, contra charges, bills
Getting paid	-	Contracts, measurement book, valuations, applications, certificates, RA bill, invoices, retention
Site office	-	Site diary, weather, delays, extension of time, RFIs, submittals, drawings, transmittals, QHSE
Controls	Three roles	Eleven roles, approval matrix, delegation, month lock, audit trail, alerts, portal, dashboards

Two apps in the menu

The Base module adds the **Construction** app. Enterprise adds menus inside it (Site Diary, Site Attendance, QHSE, Work Orders, Petty Cash, Procurement, Dashboards and the Executive Dashboard) and a second app, **Commercial**, for the quantity surveyors and the commercial office: Control Tower, Tenders, Contracts, Measurement, Valuations, Subcontracts, Variations, Documents, Site Costs, Time, Retention, Final Account, Cost Value Reconciliation, Reporting and Configuration.

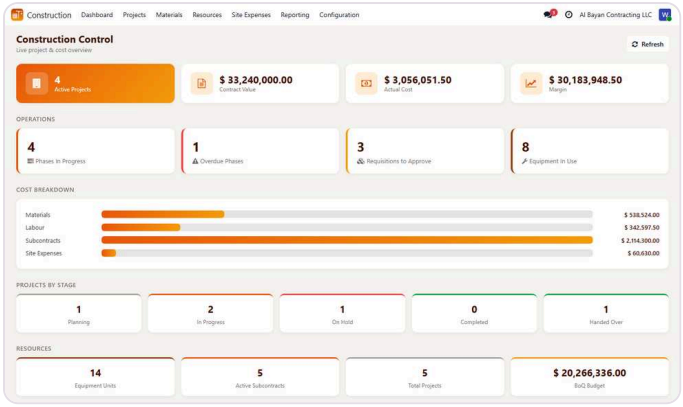

BASE The Construction app on the Base module: the Construction Control dashboard.



ENTERPRISE The Commercial app that Enterprise adds, here on the contract register.

Who sees what

The Base module ships three roles: Site Engineer, Project Manager and Administrator. Enterprise extends the same ladder to seven (Site Worker, Site Engineer, Site User, Project Manager, Commercial Manager, Director, Administrator), where each role includes the one below it, and adds four specialist roles beside the ladder.

Role	Edition	What they do
Site Worker	ENTERPRISE	Checks in and out from a phone, sees only their own attendance, and records their own claims if they hold a petty cash float.
Site Engineer	BASE	Records site facts: requisitions, labour logs, site expenses, phase progress. With Enterprise also measurement, job sheets, goods received, plant sheets, inspections, permits and snags, without seeing rates or margins.
Site User	ENTERPRISE	Everything a site engineer does, plus the site diary, weather, delays, dayworks, site instructions, RFIs, submittals, drawings, custody and roll calls.
Project Manager	BASE	Runs the job: phases, the bill, subcontracts, plant and labour. Approves requisitions and expenses. Sees cost, budget and margin.
Commercial Manager	ENTERPRISE	Owns the money chain: contracts, variations, valuations, certificates, retention, final accounts, CVR and cash flow. Awards tenders.
Director	ENTERPRISE	Reads every project, every figure and every dashboard, and approves at the top level.
Construction Administrator	BASE	Configures construction: settings, libraries, cost codes, templates, approval and alert rules. Holds every other role.
Estimator	ENTERPRISE	Tenders, the go or no-go checklist, competitor bids, estimates and rate build-ups. Marks a tender lost; the award stays with commercial.
Procurement and Stores	ENTERPRISE	Requisitions, quotes, goods received, plant hire, custody, small tools and the material reconciliation. Sees budget, not margin.
QHSE Officer	ENTERPRISE	Permits, incidents, corrective actions, inspections and hold points, NCRs, snags and toolbox talks. Sees no cost.
Finance	ENTERPRISE	Raises invoices from certificates and bills from subcontract valuations, releases retention, approves petty cash, owns the cash flow.

> With Enterprise, costs and margins are hidden from the site roles at the database level, not only on the screen, and users can be limited to the projects whose team they are on. Part 25 covers both.

The menus

Construction

Dashboard Base	Construction Control
Projects Base	Projects, Phases, Bill of Quantities, Bills of Quantities
Materials Base	Material Requisitions, Materials, Site Stores, Issue to Work
Resources Base	Equipment, Labour Logs, Subcontracts, Tools, Custody, Plant Maintenance
Site Expenses Base	Every site spend
Reporting Base	Cost Analysis, Labour Analysis, Bill Analysis
Site Diary Enterprise	Today, Diaries, Weather, Delays, Manpower, Plant
Site Attendance Enterprise	Check-In, Roll Call, All, To Approve, Exceptions, By Site
QHSE Enterprise	Permits, Board, Toolbox, Incidents, Inspections, Holds, NCRs, Snags, Locations
Work Orders Enterprise	Work Orders, Job Sheets, Manpower, Delayed, Generate, Schedule
Petty Cash Enterprise	Floats, Transactions, To Approve, Needing Top-Up
Procurement Enterprise	Requisitions, RFQs, Comparison, POs, Goods Received, Bills to Review, Stores, Transfers, Issue, Consumption
Dashboards Enterprise	Site, Commercial, Tender, QHSE, Procurement, Finance
Executive Dashboard Enterprise	The portfolio
Configuration Base	Settings, Work Types, Labour Types, Expense Categories
Configuration (Enterprise) Enterprise	Rate Library, Bill Templates, Cost Codes, Permit Types, Toolbox Topics, ITPs, Access Control

Commercial

Control Tower Enterprise	Executive Dashboard, Alerts, Waiting on Me, Cash, Retention, Exposure, Margin, Live Margin
Tenders Enterprise	Pipeline, Bid Bonds, Competitor Analysis, Opportunities, Quotations
Contracts Enterprise	Contracts
Measurement Enterprise	Measurement Book, Measured Quantities
Valuations Enterprise	Raise a Valuation, Interim Valuations, Applications, Certificates, Client Invoices
Subcontracts Enterprise	Packages, Valuations, Order Variations, Contra Charges, Subcontractor Bills
Variations Enterprise	Site Instructions, Variations, Exposure, Daywork Sheets, Provisional Sums, Approvals
Documents Enterprise	RFIs, Outstanding, Submittals, At Risk, Drawings, Revisions, Transmittals, Who Had What
Site Costs Enterprise	Plant Hire, Daily Plant Sheet, Goods Received, Material Reconciliation, Gangs, Labour Allocations
Time Enterprise	Programmes, Schedule, Delay Events, EOT Claims, Site Diaries
Retention Enterprise	Retention Ledger, Nobody Chased This, Snags Holding Retention
Final Account Enterprise	Final Accounts, Everything Holding a Job Open, Loss and Expense
Cost Value Reconciliation Enterprise	Reconciliations, Accruals, Accruals to Reverse, Cash Flow, Cost by Code
Reporting Enterprise	Budget vs Actual, Over Budget, Unconfirmed Instructions, Unsigned Dayworks, RFIs Holding Up Work, Idle Plant, Waste, Gangs Below Norm, Notices Due, Claimed vs Agreed, Losing Money, Cash Movements, Job Cost Sheet
Controls Enterprise	Approval Matrix, Waiting on Me, Delegations, Close Month, Audit Trail
Configuration Enterprise	Forms of Contract, Valuation Methods, document, plant, delay, weather and tender libraries, Templates, Approval and Alert Rules


PART 3 Open the demo and sign in

BASE

Everything tagged Base in this guide can be followed on the live demo. It is a real Odoo 19 database with the Construction Management module installed and five jobs already on it, from a school extension still in planning to a villa renovation that has been handed over.

TRY IT YOURSELF ON THE DEMO

1. Open construction.way4tech.com/web/login
2. Sign in with w4demo and Demo2026
3. Open Construction, then Projects, then Projects
4. Open Marina Heights Residential Tower and click the Construction tab

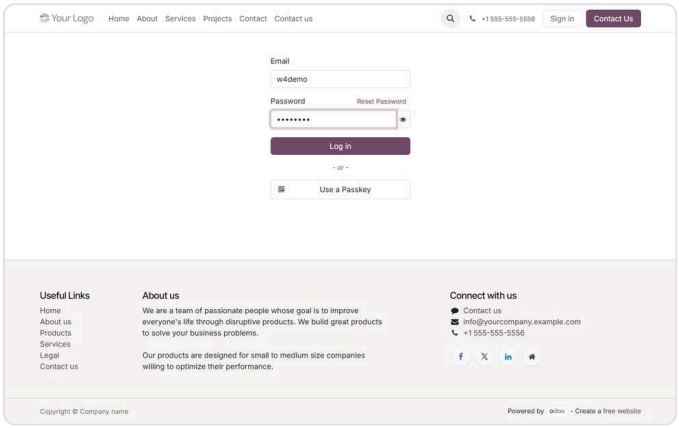


1 BASE

Go to the demo

Open **construction.way4tech.com/web/login** in any browser. The home page is a sample contractor website; the sign-in screen is the standard Odoo one.

The address works on a phone, a tablet or a computer. The office screens are built for a desktop.



2 BASE

Sign in and open Construction

User `w4demo`, password `Demo2026`. The **Construction** app opens from the app menu. This login sees every job so you can follow the whole guide.

The demo is shared and resets from time to time. Anything you change may be put back or seen by the next visitor, so treat it as a site to walk round rather than your own books.

What is on the demo BASE

Job	Client	Stage	Contract value
Marina Heights Residential Tower (G+12)	Marina Crest Developments LLC	In progress	18,650,000
Al Quoz Logistics Warehouse and Office Block	Desert Link Logistics FZE	In progress	4,280,000
Mirdif Gate Retail Plaza, Shell and Core	Mirdif Gate Properties LLC	On hold	2,350,000
Al Noor School Extension, Block B (G+2)	Al Noor Private School LLC	Planning	6,820,000
Villa 27, Full Renovation and Extension	A private client	Handed over	1,140,000

Every job has eight phases and seventeen bill items. The live jobs carry requisitions at every status, daily labour logs, subcontracts and site expenses, so each workflow in Parts 5 to 9 has a record you can open in the state the guide describes.

> The live demo runs the Base module only. Enterprise screens in this guide were taken on the demo data that ships with the Enterprise add-on. Ask us for an Enterprise walkthrough and we open it on a demo database for you.

PART 4 Set the company up from zero

What a contractor does on day one, before the first job: install the modules, set the company rules, and check the libraries that every job draws on. On the demo all of this is done, so read it to understand what each setting means and where it lives.

4.1 Install

1 BASE

Install Construction Management

Apps, search **Construction Management**, Install. It brings Project, Employees and Invoicing with it if they are not there yet. A **Construction** app appears in the menu with Dashboard, Projects, Materials, Resources, Site Expenses, Reporting and Configuration.

The module runs on Odoo 19 Community and on Enterprise.

2 ENTERPRISE

Add Construction Management Enterprise

Install it after the Base module. It brings Purchase, Inventory, Sales, CRM, Maintenance and the Portal with it, adds new menus inside Construction and a second app called **Commercial**. On install it gives every bill item that already exists a starting budget, so a company that has run the Base module for a year keeps its history and its jobs.

Uninstalling Enterprise puts the Base module back exactly as it was, including the rule that a bill line needs a project.

3 BASE


Give people their roles


Settings, Users, open a user, and pick a level under **Construction**. The Base module offers Site Engineer, Project Manager and Administrator. Enterprise adds Site Worker, Site User, Commercial Manager and Director on the same ladder, and separate choices for Estimating, Procurement and Stores, QHSE and Finance.

Part 25 shows the Access Matrix, which lists for every role what it can read, change, create and delete.

4.2 Company settings

Construction, Configuration, Settings. The page is the standard Odoo settings page, opened on the Construction section. The Base module adds two settings; Enterprise adds blocks for access, budget, invoicing, the certificate print, maintenance, procurement, materials and the period lock.

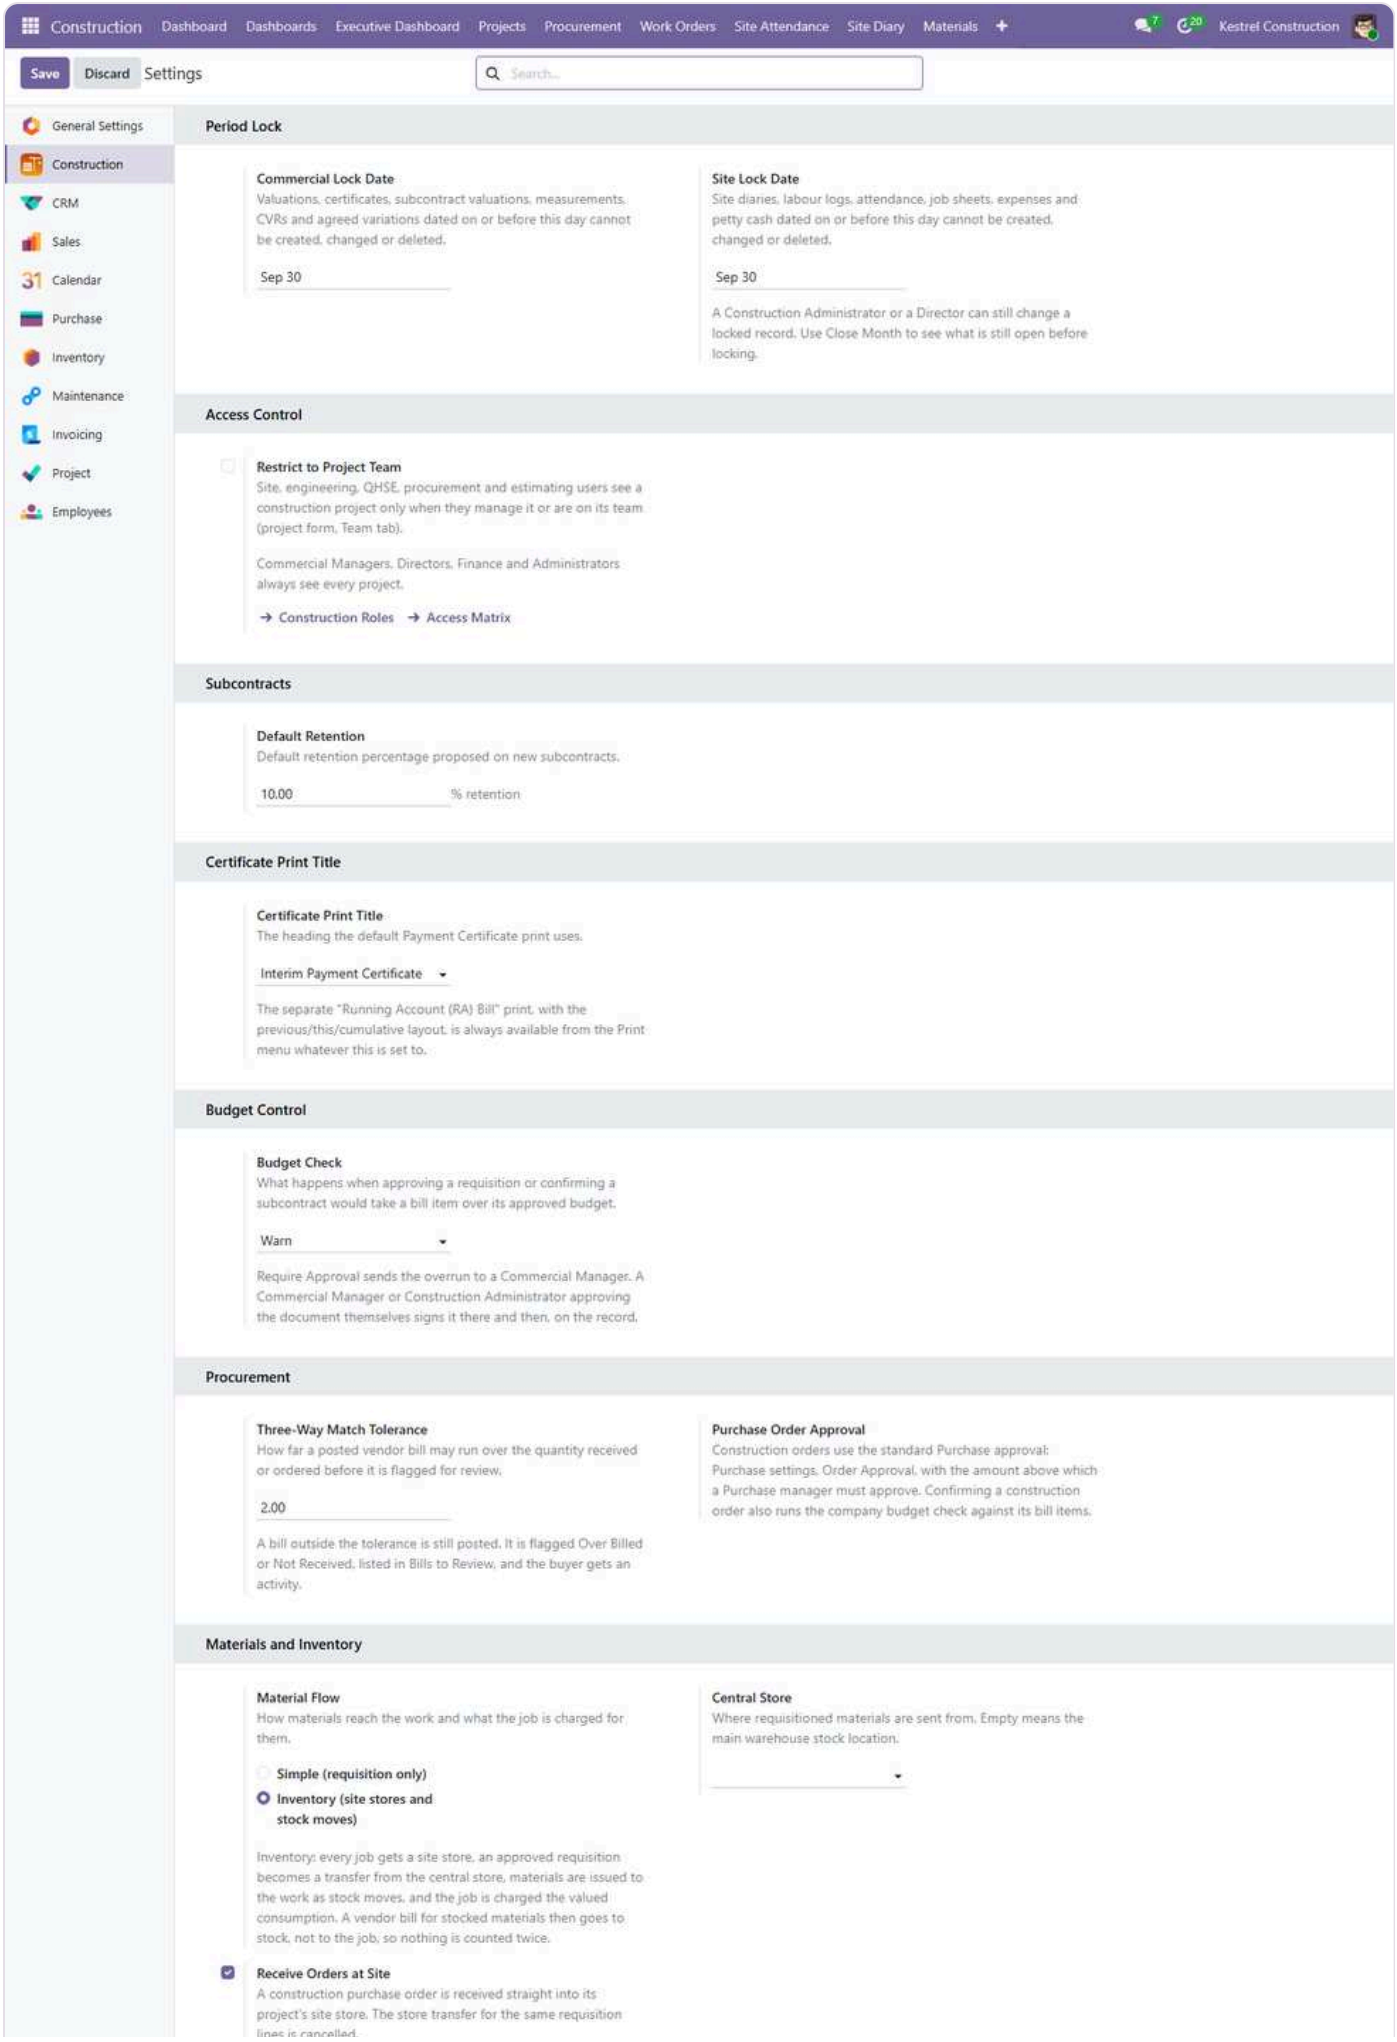
Construction
Dashboard
Dashboards
Executive Dashboard
Projects
Procurement
Work Orders
Site Attendance
Site Diary
Materials
Kestrel Construction
Save
Discard
Settings
Search...
General Settings
Construction
CRM
Sales
Calendar
Purchase
Inventory
Maintenance
Invoicing
Project
Employees
Period Lock
Commercial Lock Date
Valuations, certificates, subcontract valuations, measurements, CVRs and agreed variations dated on or before this day cannot be created, changed or deleted.
Sep 30
Site Lock Date
Site diaries, labour logs, attendance, job sheets, expenses and petty cash dated on or before this day cannot be created, changed or deleted.
Sep 30
A Construction Administrator or a Director can still change a locked record. Use Close Month to see what is still open before locking.
Access Control
Restrict to Project Team
Site, engineering, QHSE, procurement and estimating users see a construction project only when they manage it or are on its team (project form, Team tab).
Commercial Managers, Directors, Finance and Administrators always see every project.
→ Construction Roles → Access Matrix
Subcontracts
Default Retention
Default retention percentage proposed on new subcontracts.
10.00
% retention
Certificate Print Title
Certificate Print Title
The heading the default Payment Certificate print uses.
Interim Payment Certificate
The separate "Running Account (RA) Bill" print, with the previous/this/cumulative layout, is always available from the Print menu whatever this is set to.
Budget Control
Budget Check
What happens when approving a requisition or confirming a subcontract would take a bill item over its approved budget.
Warn
Require Approval sends the overrun to a Commercial Manager. A Commercial Manager or Construction Administrator approving the document themselves signs it there and then, on the record.
Procurement
Three-Way Match Tolerance
How far a posted vendor bill may run over the quantity received or ordered before it is flagged for review.
2.00
A bill outside the tolerance is still posted. It is flagged Over Billed or Not Received, listed in Bills to Review, and the buyer gets an activity.
Purchase Order Approval
Construction orders use the standard Purchase approval: Purchase settings, Order Approval, with the amount above which a Purchase manager must approve. Confirming a construction order also runs the company budget check against its bill items.
Materials and Inventory
Material Flow
How materials reach the work and what the job is charged for them.
Simple (requisition only)
Inventory (site stores and stock moves)
Inventory: every job gets a site store, an approved requisition becomes a transfer from the central store, materials are issued to the work as stock moves, and the job is charged the valued consumption. A vendor bill for stocked materials then goes to stock, not to the job, so nothing is counted twice.
Central Store
Where requisitioned materials are sent from. Empty means the main warehouse stock location.
Receive Orders at Site
A construction purchase order is received straight into its project's site store. The store transfer for the same requisition lines is cancelled.

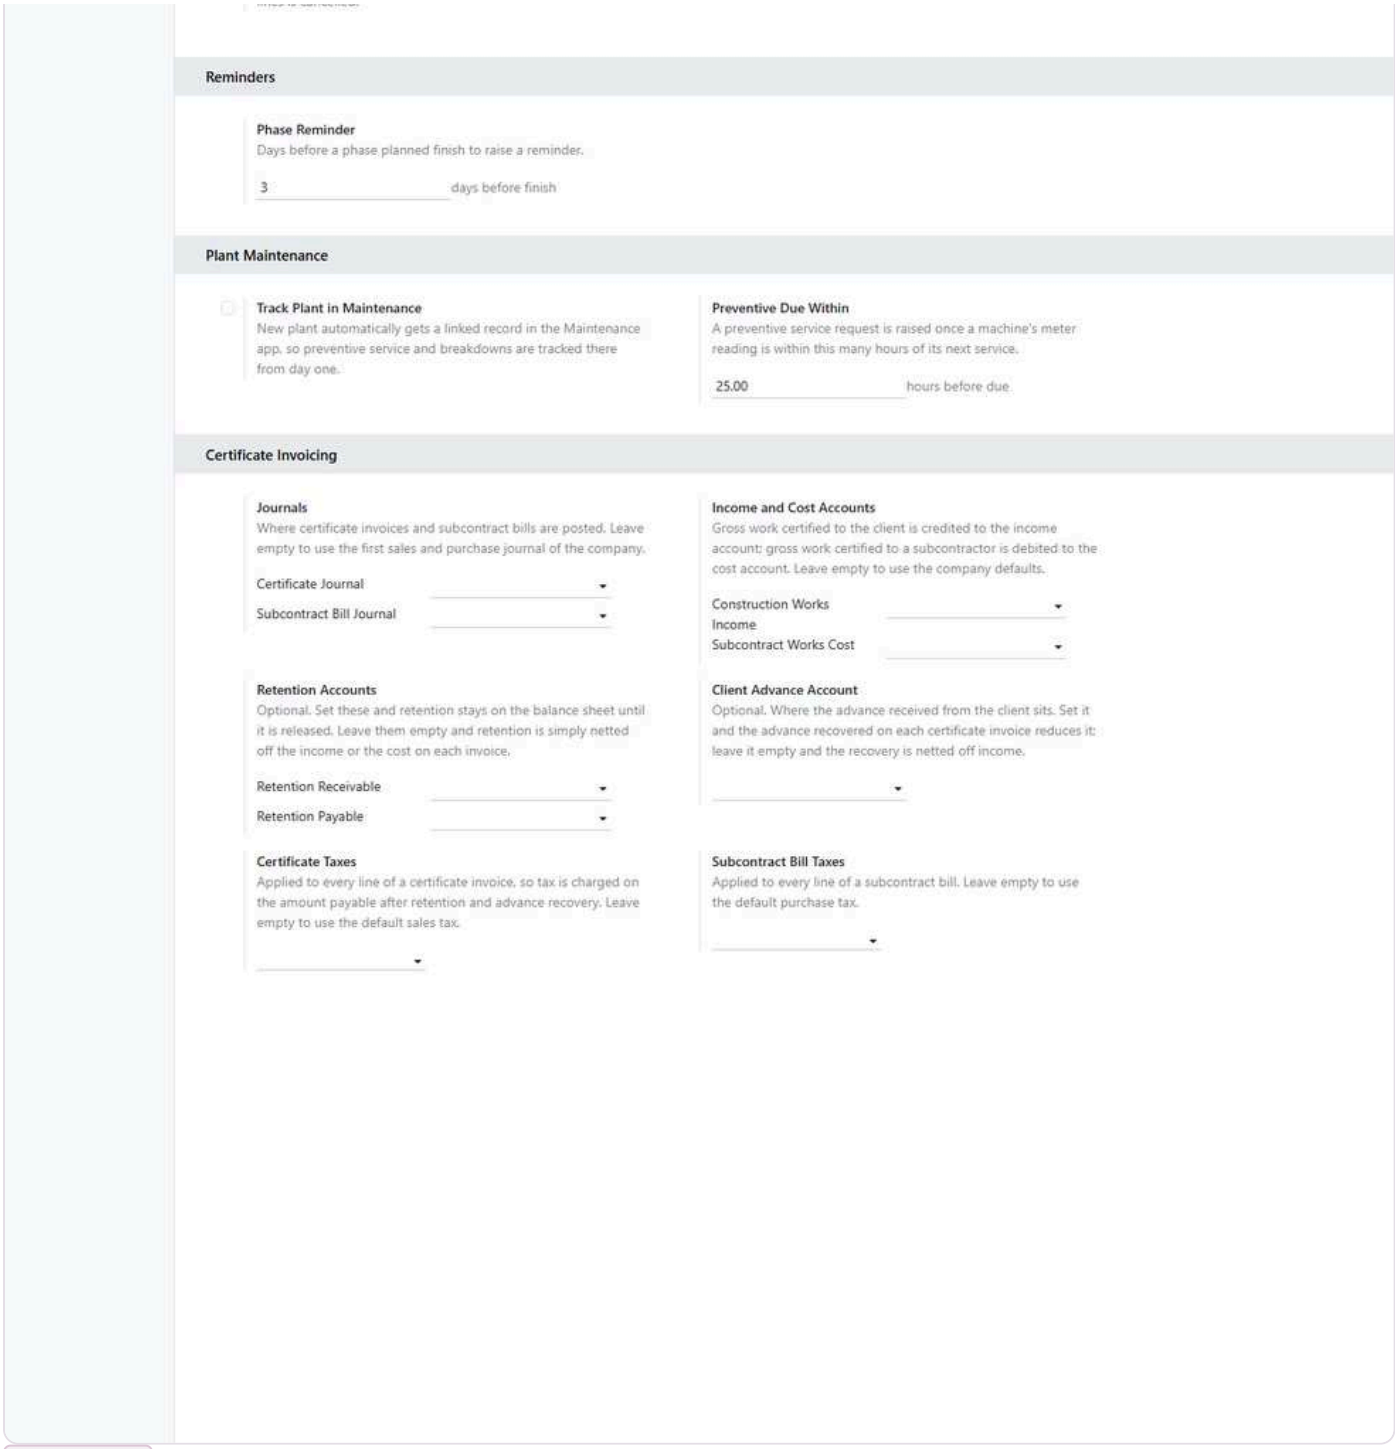

ENTERPRISE Construction settings with Enterprise installed. Each block is one rule the whole company runs on.


SETTING	WHAT IT DOES	EDITION
Default Retention	A retention percentage stored for the company, meant as the default on new subcontracts.	BASE
Phase Reminder	A number of days stored for the company, meant as the lead time before a phase finish.	BASE
Restrict to Project Team	Site, engineering, QHSE, procurement and estimating users see a project only when they manage it or are on its team.	ENTERPRISE
Budget Check	What happens when approving a requisition or confirming a subcontract would take a bill item over budget: no check, warn, block, or require approval.	ENTERPRISE

Journals	Where certificate invoices and subcontract bills are posted. Empty uses the first sales and purchase journal.	ENTERPRISE
Income and Cost Accounts	Gross work certified to the client is credited to income; gross work certified to a subcontractor is debited to cost.	ENTERPRISE
Retention Accounts	Optional. Set them and retention stays on the balance sheet until released. Empty nets retention off income or cost.	ENTERPRISE
Client Advance Account	Optional. Where the client advance sits; each certificate invoice recovers part of it.	ENTERPRISE
Certificate Taxes and Subcontract Bill Taxes	Taxes on every line of a certificate invoice or subcontract bill. Empty uses the default sales or purchase tax.	ENTERPRISE
Certificate Print Title	The heading on the payment certificate print: Interim Payment Certificate, RA Bill, Progress Claim or Payment Application.	ENTERPRISE
Track Plant in Maintenance	New plant gets a linked record in the Maintenance app from day one.	ENTERPRISE
Preventive Due Within	A preventive service request is raised once a machine is within this many running hours of its next service.	ENTERPRISE
Three-Way Match Tolerance	How far a posted vendor bill may run over the quantity ordered or received before it is flagged for review.	ENTERPRISE
Purchase Order Approval	Construction orders use the standard Purchase approval limit, and confirming one also runs the budget check.	ENTERPRISE
Material Flow	Simple: requisitions are approved and marked issued, nothing moves in Inventory. Inventory: every job has a site store and the job is charged the valued consumption.	ENTERPRISE
Central Store and Receive Orders at Site	Where requisitioned materials come from, and whether construction purchase orders are received straight into the site store.	ENTERPRISE
Commercial Lock Date and Site Lock Date	Records dated on or before these days cannot be created, changed or deleted. Usually set by Close Month (Part 24).	ENTERPRISE


> Two Base settings, Default Retention and Phase Reminder, are stored but not yet used anywhere: a new subcontract does not take the default retention, and the overdue phase reminder fires on the planned finish date itself. Set the retention on each subcontract by hand.

4.3 The libraries every job uses BASE


Configuration holds the lists that jobs pick from. Each is an editable list; add your own rows or rename the shipped ones.

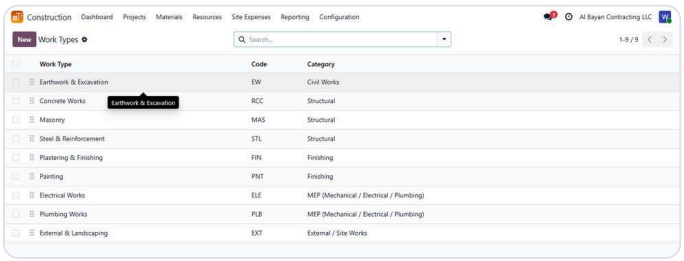

BASE **Work Types**: nine trades or packages, each with a code and a category (civil, structural, finishing, MEP, external, other).




BASE **Labour Types**: eight trades with a skill level and a default daily wage, used on every labour log.

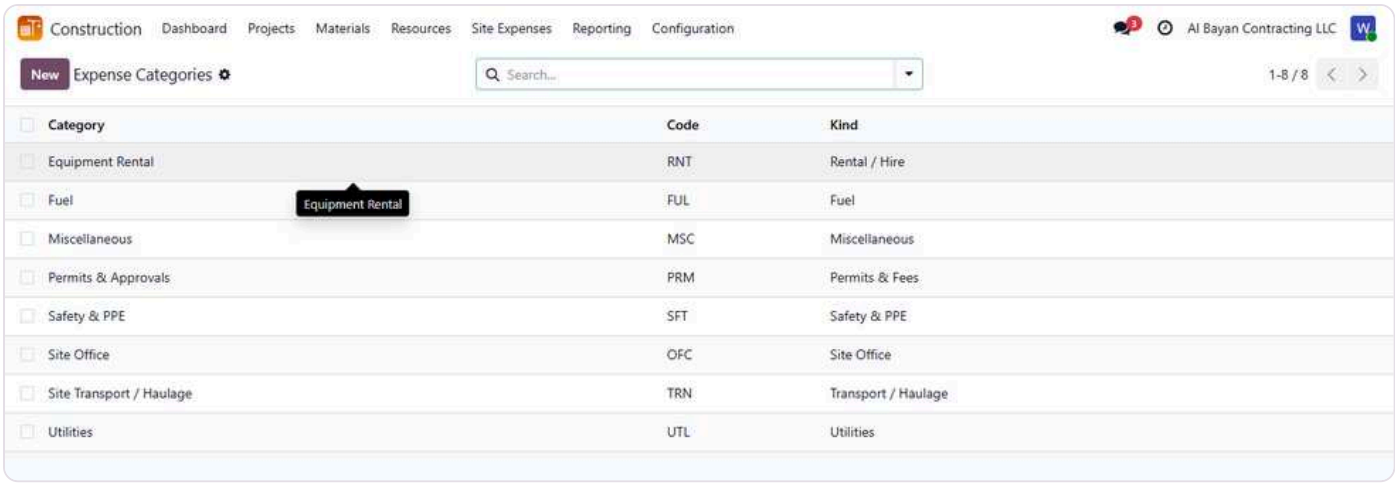


BASE **Expense Categories**: site transport, utilities, permits, safety and PPE, equipment rental, fuel, site office and miscellaneous.

4.4 Enterprise libraries ENTERPRISE

Library	Menu	What it holds
Rate Library	Construction, Configuration	Rate build-ups: labour, plant, material and subcontract components per unit, with overhead and margin (Part 6).
Bill Templates	Construction, Configuration	Standard bills with no project behind them, loaded into a new bill in one click.
Cost Codes	Construction, Configuration	A nested coding structure with a cost type per code, used by budget, CVR and petty cash.
Permit Types, Toolbox Talk Topics, Inspection and Test Plans	Construction, Configuration	The QHSE libraries (Part 22).
Access Control	Construction, Configuration	Construction Roles, the Access Matrix and Who Has Which Role (Part 25).
Forms of Contract	Commercial, Configuration	Retention, moieties, defects period, valuation day, days to certify and pay, damages rate and cap.
Valuation Methods	Commercial, Configuration	How a variation is valued: bill rates, pro rata, star rate, daywork, lump sum.
RFI Categories, Submittal Types, Review Stamps	Commercial, Configuration	Response times and review periods for the document control layer (Part 21).
Drawing Disciplines, Purposes of Issue	Commercial, Configuration	The drawing number letters and why a document was issued.
Plant Categories, Tracked Materials	Commercial, Configuration	Default hire rates and idle thresholds; materials reconciled with their allowed waste.
Delay Causes, Adverse Weather Criteria	Commercial, Configuration	Reasons a job runs late with their entitlement, and what counts as a bad weather day.
Tender Stages, Tender Loss Reasons	Commercial, Configuration	The tender pipeline columns and why bids were lost.
Project Templates, Approval Rules, Alert Rules	Commercial, Configuration	A whole job set up in one dialog, the approval chain, and the alert engine (Part 24).



ENTERPRISE **Cost Codes**: headings with sub-codes, each reporting into one cost type.



ENTERPRISE **Forms of Contract**: the terms a new contract is raised with.

4.5 A sensible order for the first week

1. Set the labour wages and the expense categories to your own (Base).
2. Give every user a construction role, and on Enterprise decide whether to restrict users to their project team.
3. On Enterprise, set the invoicing accounts and journals with your accountant before the first certificate.
4. Pick the budget check policy. Warn is a good start; Block once the budgets are trusted.
5. Load cost codes and one form of contract, then one project template for the kind of job you do most.
6. Create the first job (Part 5) and load its bill (Part 6).


PART 5 Construction projects

BASE

A construction job is an ordinary Odoo project with a construction layer on top. It keeps tasks, stages, followers and the chatter, and gains a code, a stage, a supervisor, a contract value, a site address and a cost summary that updates as costs are booked.

TRY IT YOURSELF ON THE DEMO

1. Open Construction, Projects, Projects
2. Open Marina Heights Residential Tower
3. Click Construction and read the cost summary
4. Click the Phases button at the top




1 BASE

The job board

Construction, Projects, Projects. One card per job. Only projects ticked as construction projects are listed here, so the office's other Odoo projects stay out of the way.


Switch to the list view for code, client, stage and contract value in columns.



2 BASE

Every job in a list

The list is sortable and groupable like any Odoo list. Group by construction stage to see how many jobs are planning, running, on hold, completed or handed over.

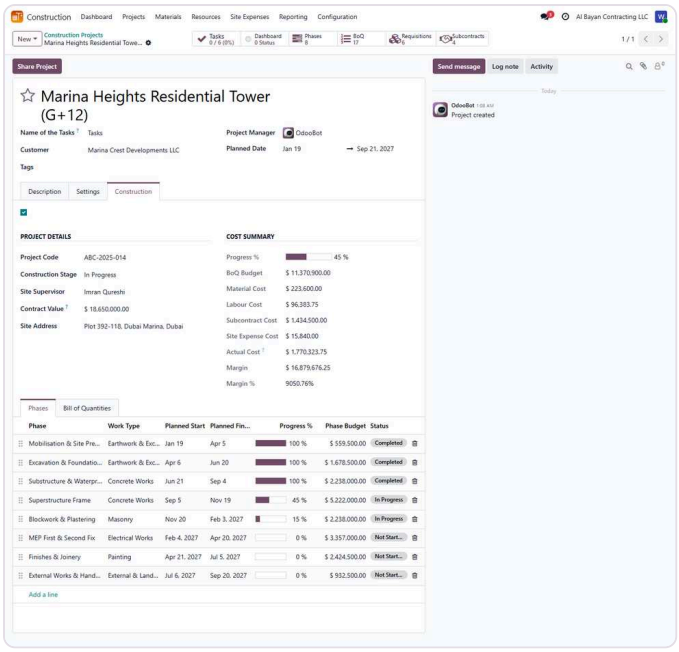


3 BASE

The Construction tab

Open a job and click **Construction**. Left: project code, construction stage, site supervisor (an employee), contract value and site address. Right: the cost summary. Under it, the job's phases and its bill of quantities as editable tabs.

The tick box at the top of the tab is **Construction Project**. It is ticked for you when the job is created from this menu; tick it on any existing Odoo project to bring it in.

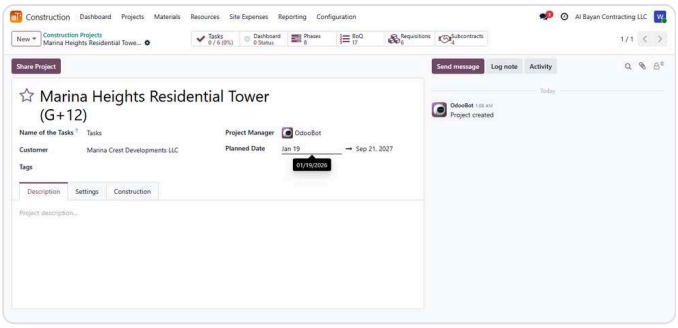

4 BASE

Smart buttons along the top


Phases, BoQ, Requisitions and Subcontracts each open the job's own records, with the count on the button. The project also has buttons for equipment, labour logs and site expenses in its action menu.

The cost summary, line by line BASE

Figure	Worked out as
Progress %	The plain average of the phases' progress.
BoQ Budget	The total of the job's bill of quantities lines.
Material Cost	Requisitions that are approved or issued, at their line subtotals.
Labour Cost	Every labour log on the job: headcount times days times daily wage.
Subcontract Cost	The billed amount of every confirmed, in progress or completed subcontract.
Site Expense Cost	Site expenses that are approved or paid.
Actual Cost	Materials, labour, subcontract billed and site expenses together.
Subcontract Committed	The full order value of every live subcontract, shown beside actual so a big order does not hide.
Committed Cost	Actual cost with the full value of let subcontracts in place of what they have billed.
Margin and Margin %	Contract value less actual cost, and that as a share of the contract value.

Margin here is contract value less cost to date, so a job that is a third built shows a very large margin. Use it to watch cost build up, not as a forecast. On the demo the Margin % field also shows the figure one hundred times too large (9050.76% for what is 90.5%), a display fault in the current release.

With Enterprise, the project form grows ENTERPRISE

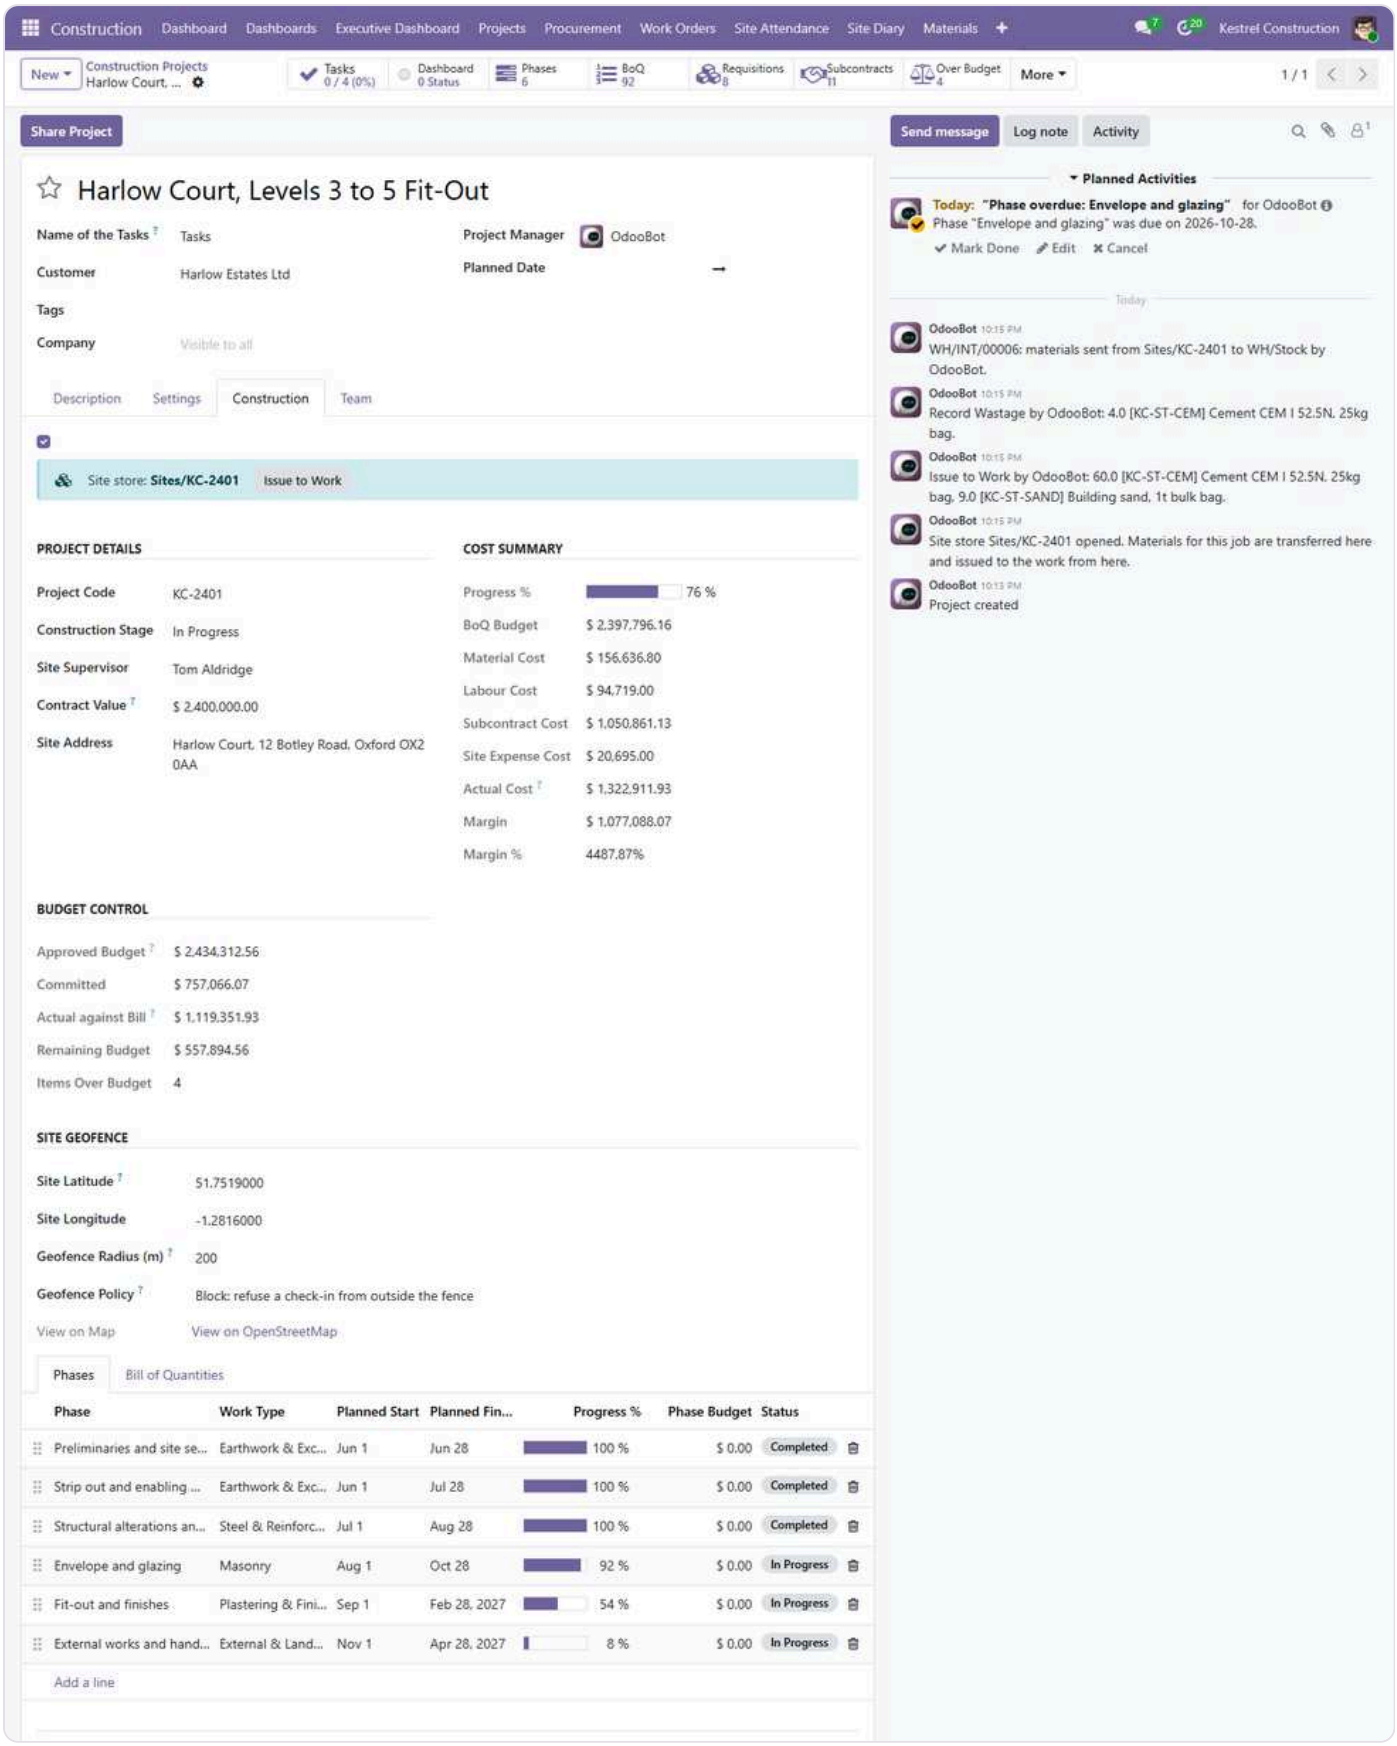

ENTERPRISE The same project with Enterprise installed: team, geofence, site store, template and the quality and safety counters join the construction fields.

Added to the project	What it is for	Part
Project Team	Who works on the job. With team restriction on, only the manager and the team see it.	25
Site latitude, longitude, radius, geofence policy	The circle the phone check-in is tested against, and whether a punch from outside is blocked or flagged.	19
Site Store	The Inventory location that holds this job's materials, created with one button.	16
Built From Template	The project template applied to it, and when.	24
Budget, committed, actual, remaining, items over budget	The bill-item budget rolled up to the job.	15
Margin at Full Commitment	Contract value less the cost the job is already signed up to.	15
Incidents, permits, toolbox talks, inspections, NCRs, snags	Counts with buttons into each register, and LTIFR and days since the last lost-time injury.	22
Plant hire cost, idle plant, plant past off-hire	The hire desk position for the job.	20

PART 6 Phases and the bill of quantities


BASE

Cost to date means nothing on its own. A job that has spent 1.7 million is fine if the work done so far was budgeted at 1.9 million, and in trouble if it was budgeted at 1.2. The bill of quantities is that budget, and phases give it a timeline.

TRY IT YOURSELF ON THE DEMO

1. Open Construction, Projects, Phases and group by project
2. Open Superstructure Frame on Marina Heights and read the planned and actual dates
3. Open Construction, Projects, Bill of Quantities and filter on one project
4. On the project, use Print, Bill of Quantities


6.1 Phases BASE

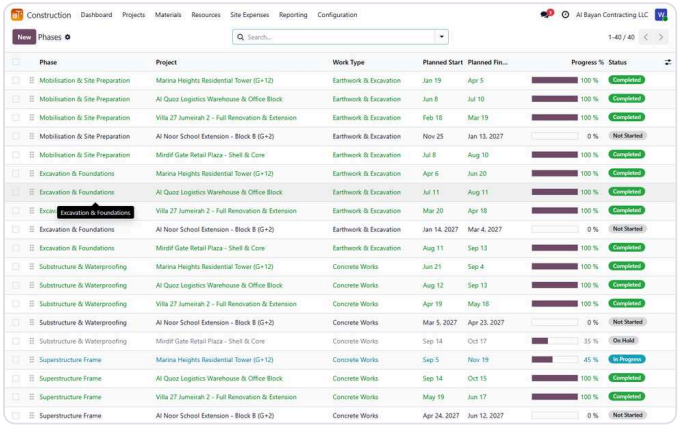

1 BASE

Phases across every job

Construction, Projects, Phases, or the Phases tab on a job. Each phase has a work type, planned start and finish, a budget, a supervisor, a progress percentage and a status. The planned finish cannot be before the planned start, and progress stays between 0 and 100.

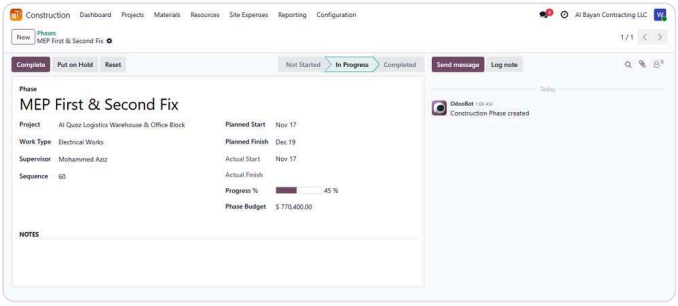

2 BASE

Move a phase through its life


Start sets it in progress and stamps the actual start the first time. **Put on Hold** parks it. **Complete** sets progress to 100 and stamps the actual finish. **Reset** takes it back to not started.

Planned and actual dates sit side by side, which is what a delay discussion a year later needs.

A daily scheduled job looks for phases past their planned finish that are not completed, and puts a "Phase overdue" to-do on the project for its manager. It does not repeat while that to-do is open. The dashboard's Overdue Phases tile counts the same phases.

> With Enterprise, a phase cannot be completed while it has open non-conformance reports; Complete is refused with the count. A phase is an area of work, and it is not finished while its defects are open.

6.2 The bill of quantities in the Base module BASE

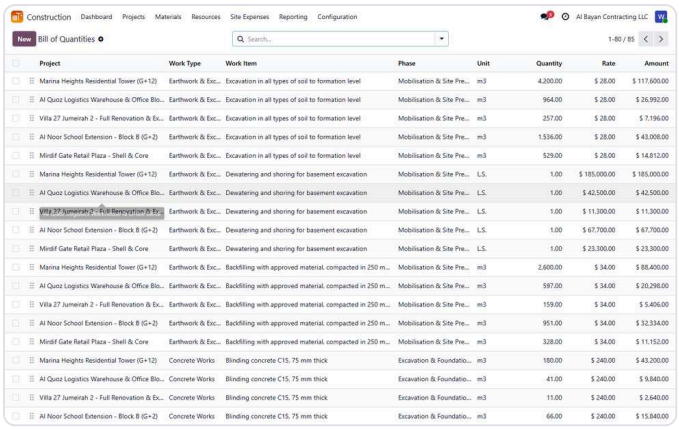


3 BASE

Every bill item in one list

Construction, Projects, Bill of Quantities: an editable list across all jobs, with a running total. Each line has a work type, the work item as it reads in the bill, a phase on the same job, a unit (m3, m2, ton, No., L.S.), quantity, rate, amount and remarks.

For a long bill, prepare it in a spreadsheet and load it with Odoo's standard import from this list.

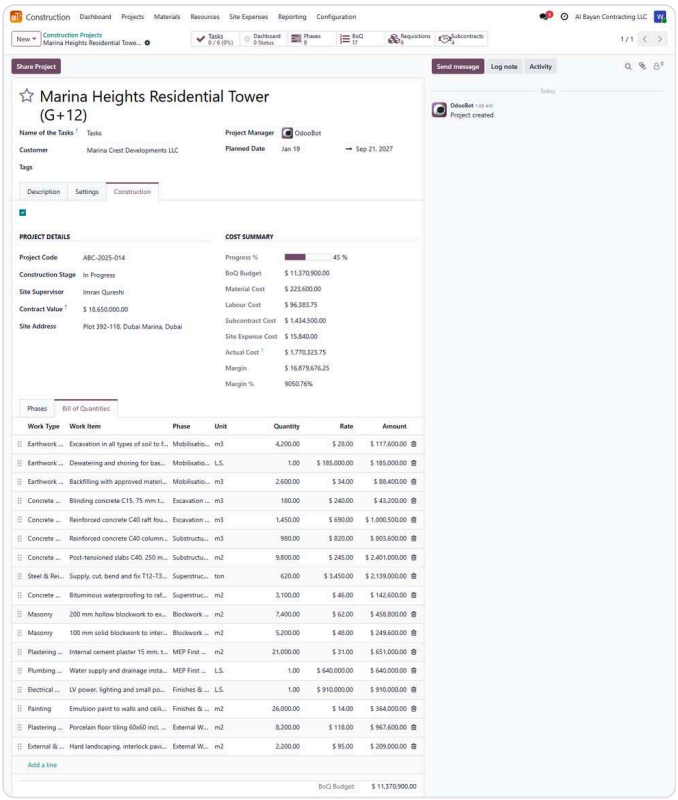


4 BASE

The bill on the job

The job's Bill of Quantities tab holds the same lines. Lines can be dragged into order, and the order is what the printout uses. The total of all lines is the job's **BoQ Budget**.

> The Base bill has one rate per line and nothing stops a quantity being changed after the job starts. Decide whether you enter cost rates or selling rates and keep to it. Enterprise separates the two, adds sections and revisions, and freezes the budget once the bill is agreed.

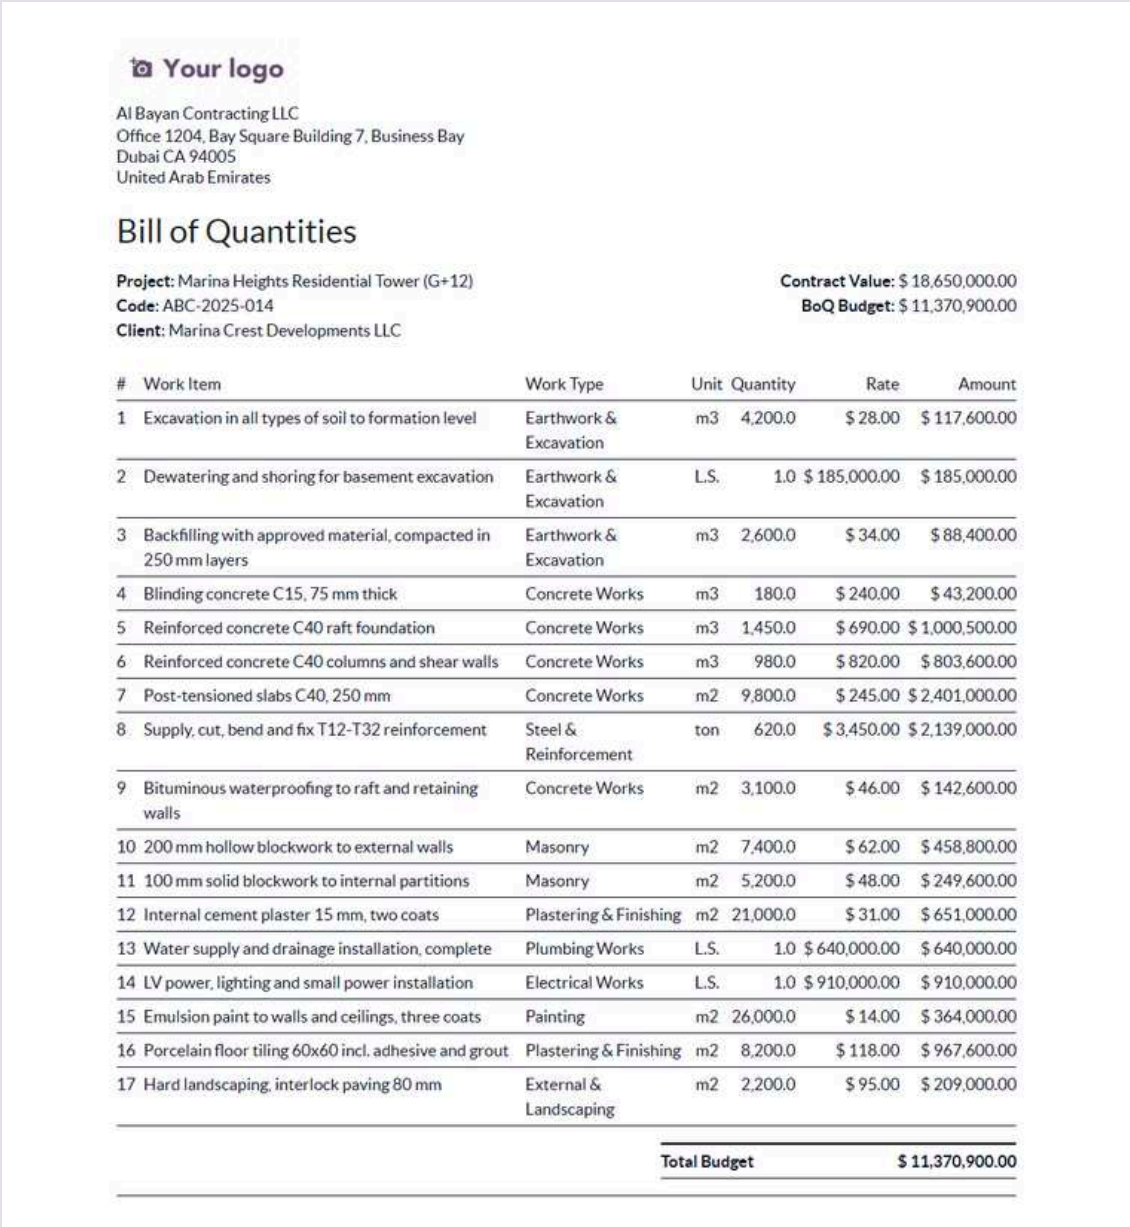

Your logo

Al Bayan Contracting LLC
Office 1204, Bay Square Building 7, Business Bay
Dubai CA 94005
United Arab Emirates

Bill of Quantities

Project: Marina Heights Residential Tower (G+12)
Code: ABC-2025-014
Client: Marina Crest Developments LLC


Contract Value: $ 18,650,000.00
BoQ Budget: $ 11,370,900.00

#	Work Item	Work Type	Unit	Quantity	Rate	Amount
1	Excavation in all types of soil to formation level	Earthwork & Excavation	m3	4,200.0	$ 28.00	$ 117,600.00
2	Dewatering and shoring for basement excavation	Earthwork & Excavation	L.S.	1.0	$ 185,000.00	$ 185,000.00
3	Backfilling with approved material, compacted in 250 mm layers	Earthwork & Excavation	m3	2,600.0	$ 34.00	$ 88,400.00
4	Blinding concrete C15, 75 mm thick	Concrete Works	m3	180.0	$ 240.00	$ 43,200.00
5	Reinforced concrete C40 raft foundation	Concrete Works	m3	1,450.0	$ 690.00	$ 1,000,500.00
6	Reinforced concrete C40 columns and shear walls	Concrete Works	m3	980.0	$ 820.00	$ 803,600.00
7	Post-tensioned slabs C40, 250 mm	Concrete Works	m2	9,800.0	$ 245.00	$ 2,401,000.00
8	Supply, cut, bend and fix T12-T32 reinforcement	Steel & Reinforcement	ton	620.0	$ 3,450.00	$ 2,139,000.00
9	Bituminous waterproofing to raft and retaining walls	Concrete Works	m2	3,100.0	$ 46.00	$ 142,600.00
10	200 mm hollow blockwork to external walls	Masonry	m2	7,400.0	$ 62.00	$ 458,800.00
11	100 mm solid blockwork to internal partitions	Masonry	m2	5,200.0	$ 48.00	$ 249,600.00
12	Internal cement plaster 15 mm, two coats	Plastering & Finishing	m2	21,000.0	$ 31.00	$ 651,000.00
13	Water supply and drainage installation, complete	Plumbing Works	L.S.	1.0	$ 640,000.00	$ 640,000.00
14	LV power, lighting and small power installation	Electrical Works	L.S.	1.0	$ 910,000.00	$ 910,000.00
15	Emulsion paint to walls and ceilings, three coats	Painting	m2	26,000.0	$ 14.00	$ 364,000.00
16	Porcelain floor tiling 60x60 incl. adhesive and grout	Plastering & Finishing	m2	8,200.0	$ 118.00	$ 967,600.00
17	Hard landscaping, interlock paving 80 mm	External & Landscaping	m2	2,200.0	$ 95.00	$ 209,000.00
				Total Budget		**$ 11,370,900.00**

BASE Print, Bill of Quantities on the project: numbered items with work type, unit, quantity, rate and amount, the project code and client at the top and the total budget at the foot.

6.3 Bills as documents ENTERPRISE


With Enterprise a bill is a document of its own (Construction, Projects, Bills of Quantities) with a name, a revision number, a date, a status and nested sections. The Base bill lines are still there; they now belong to a bill and a section.



5 ENTERPRISE

The bills register

One row per bill per revision, with the line count, bill total, cost total, margin and status. A job can have a tender bill, a contract bill and later revisions, and only the live one counts.

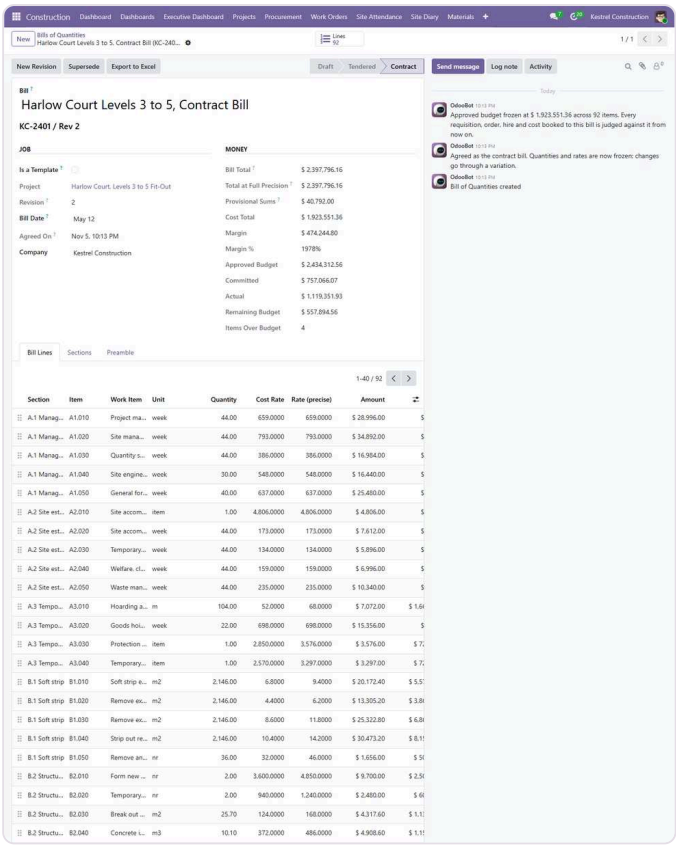


6 ENTERPRISE

A bill with its sections

Sections nest (1, 2, 2.1, 2.1.3) and each shows its own amount and the amount carried forward. The header totals the bill at the rounded print rate and at full precision, with cost, margin and the provisional sums inside it.

Renumber Sections renumbers 1, 2, 2.1 in the current order after you move things about.

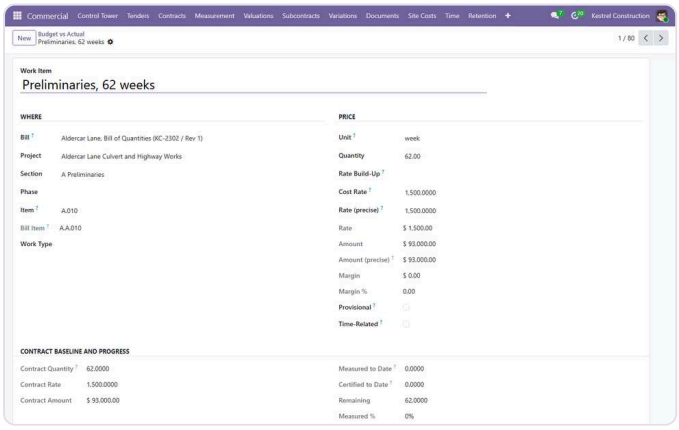

7 ENTERPRISE


A bill item in full

Each item carries an item number, a precise sell rate to four decimals, a cost rate, margin, a provisional tick, a time-related tick for preliminaries, and the contract baseline: contract quantity and rate, measured and certified to date, remaining.

The four-decimal rate matters: 2.5063 rounded to 2.51 over four thousand square metres is money lost for no reason.

Bill status and button	What happens
Draft	Yours to edit. **Load Template** pulls a standard bill in; **Import from Excel** builds it from a spreadsheet.
Issue for Tender	The bill is with the client. Still editable for clarifications.
Agree as Contract	Freezes the bill as the contract baseline: contract quantity and rate are snapshotted, and every item's budget is frozen.
New Revision	Copies the bill to the next revision and supersedes this one. Spend already booked moves across with the budget.
Supersede, Reset to Draft	Retire a bill by hand, or take a draft back.
Export to Excel	The bill with sections, items, quantities, rates and amounts as an .xlsx file.

6.4 Import a bill from Excel ENTERPRISE

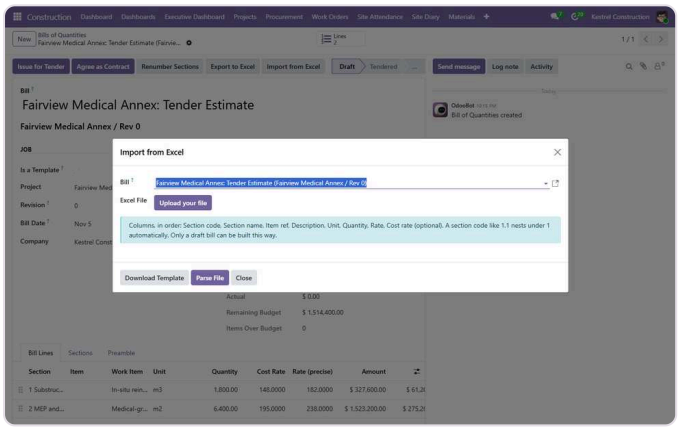

8 ENTERPRISE

The import wizard

On a draft bill, **Import from Excel**. **Download Template** gives the column layout: section code, section name, item reference, description, unit, quantity, rate and cost rate.


9 ENTERPRISE

Parse, check, confirm

Parse File reads every row into a preview with an error column, and counts rows, sections and errors. Fix the sheet and parse again until the errors are gone, then **Confirm Import**. Sections are created from the codes, lines go under them.

Only a draft bill can be built from an import, so an agreed contract bill can never be overwritten by a spreadsheet.


6.5 Bill templates and the rate library ENTERPRISE



10 ENTERPRISE

Bill templates

Construction, Configuration, Bill Templates. A standard bill with no project behind it: the preliminaries every job has, a typical fit-out, a culvert. A new bill picks it up with **Load Template**.

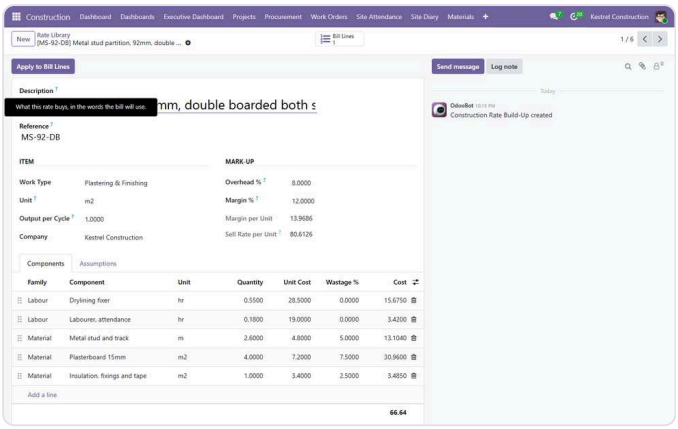

11 ENTERPRISE

A rate build-up

Construction, Configuration, Rate Library. A rate is built from components (labour by trade, plant, materials with wastage, subcontract, other) for an output per cycle. Net cost per unit, overhead and margin give the sell rate. **Apply to Bill Lines** pushes the rate onto every bill line that quotes it.

A rate with its build-up attached is a rate the estimator can defend at a tender review.

PART 7 Materials and requisitions

BASE

On most sites materials are asked for by phone and delivered without anyone signing for them. A requisition puts each request on paper, against a job and a phase, with an approval before money is committed.

TRY IT YOURSELF ON THE DEMO

1. Open Materials, Material Requisitions and filter on Submitted
2. Open MRQ/2026/00010, an approved requisition, and read the lines
3. Open MRQ/2026/00003 and compare quantity requested with quantity issued

Materials are ordinary products BASE


Tick **Construction Material** on a product (or create it from Materials, Materials, where the flag is set for you) and give it a cost price, which is offered as the unit cost when the product is picked on a requisition.

> On the live demo the Materials list is empty because the products on the requisitions were not ticked as construction materials. Requisitions still work; the flag only drives the Materials menu.

A requisition, start to finish BASE

Requisition status BASE


1. **Draft** — Engineer adds lines
2. **Submitted** — Waits for approval, chased daily
3. **Approved** — Project Manager only; now counts as cost
4. **Issued** — Quantities issued, costed

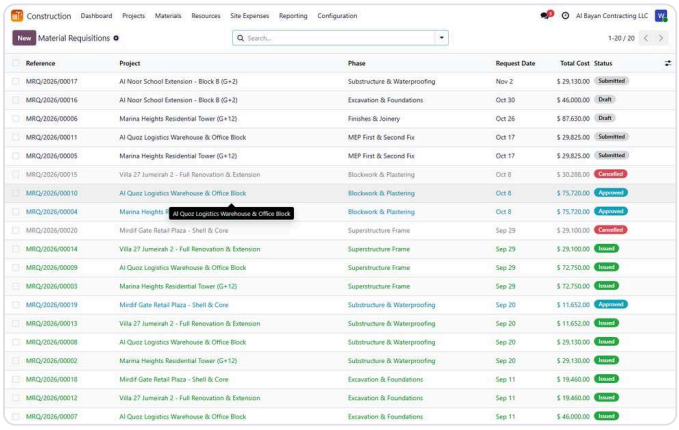

1 BASE

The requisitions list

Construction, Materials, Material Requisitions. Reference, project, phase, who asked, dates, total and status. Filter on Submitted to see what is waiting for you.

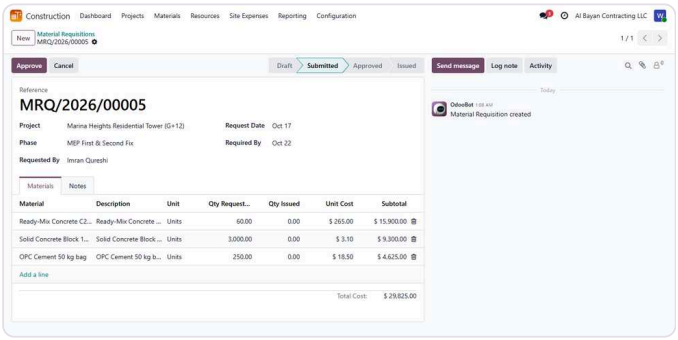


2 BASE

Submitted

The engineer picked the project, phase, who requested it and the date it is needed by, added lines (material, description, unit, quantity requested, unit cost) and pressed **Submit**. A requisition with no lines cannot be submitted.


A daily job puts a to-do on each submitted requisition until it is dealt with.

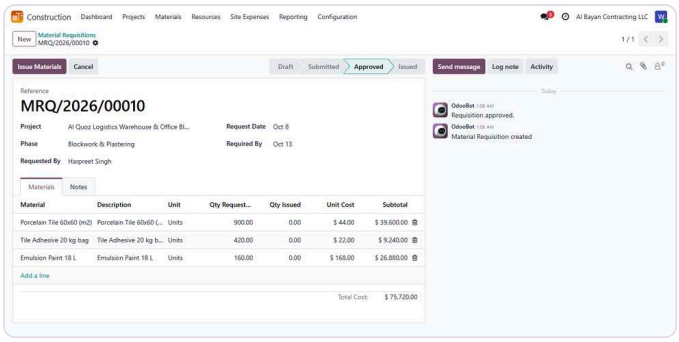

3 BASE

Approved

Only the Project Manager role sees **Approve**. From here the requisition counts as material cost on the job. A submitted or approved requisition can be cancelled, and a cancelled one reset to draft.

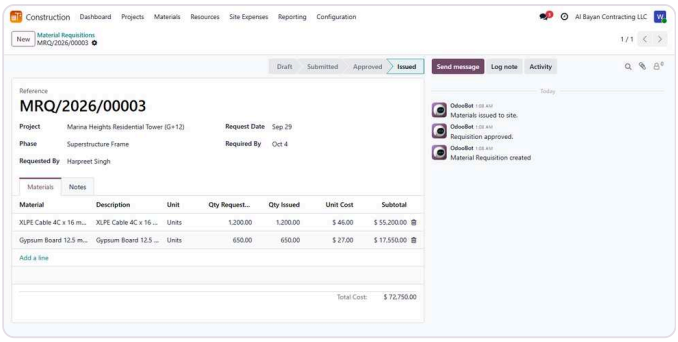

4 BASE

Issued

Issue Materials records what went to site. Lines with no quantity issued are set to the quantity requested; for a part delivery, type the issued quantity on the line first. Each line is then costed on what was issued.

Once issued it stays issued.

Your logo

Al Bayan Contracting LLC
Office 1204, Bay Square Building 7, Business Bay
Dubai CA 94005
United Arab Emirates

Material Requisition

Reference: MRQ/2026/00003
Project: Marina Heights Residential Tower (G+12)
Phase: Superstructure Frame

Date: 09/29/2026
Required By: 10/04/2026
Status: Issued

#	Material	Description	Unit	Requested	Issued	Unit Cost	Subtotal
1	XLPE Cable 4C x 16 mm2 (m)	XLPE Cable 4C x 16 mm2 (m)	Units	1,200.0	1,200.0	$ 46.00	$ 55,200.00
2	Gypsum Board 12.5 mm sheet	Gypsum Board 12.5 mm sheet	Units	650.0	650.0	$ 27.00	$ 17,550.00

Total Cost $ 72,750.00

Requested By

Approved By

BASE Print, Material Requisition: a one page request for the store or the supplier.

Issuing does not move stock in the Base module. It records quantities and cost against the job; no transfer is created. With Enterprise, switch Material Flow to Inventory and every requisition becomes a real transfer from the central store to the job's site store (Part 16).

What Enterprise adds to the requisition ENTERPRISE

Button or field	What it does	Part
Bill Item on each line	The bill item the material is for; its budget is checked when the requisition is approved.	15
Request Approval, Open the approval	When the budget policy or approval matrix needs a signature before approval.	24
Request Quotes	Sends the open lines out to vendors as a request for quotation.	16
Receive Goods	Raises a goods received note pre-filled with everything still outstanding.	16

Qty Received, Outstanding, Received %	What has been accepted on goods received notes against what was asked for.	16
Site transfers and Transfer status	In inventory mode: no transfer, waiting for stock, ready to send, on site.	16

PART 8

Labour, equipment, subcontracts and site expenses

BASE


The other four places money leaks on a site: the gang sheet, the hired machine, the subcontractor's bill and the small cash spends. Each gets a record against a job and a phase, which is what makes the cost summary and the phase comparison possible.

TRY IT YOURSELF ON THE DEMO

1. Open Resources, Labour Logs and group by labour type
2. Open Resources, Equipment and look at the Idle column
3. Open SUB/2026/00001 and compare contract value, billed and paid
4. Open Site Expenses, filter on Approved, and open one

Record	Who records it	Counts as cost when	Menu
Labour log	Site engineer	Saved (every log is a day worked)	Resources, Labour Logs
Subcontract	Project manager	Billed amount, once confirmed	Resources, Subcontracts
Site expense	Site engineer, approved by manager	Approved or paid	Site Expenses
Equipment	Project manager	Only through a site expense	Resources, Equipment

8.1 Labour logs BASE

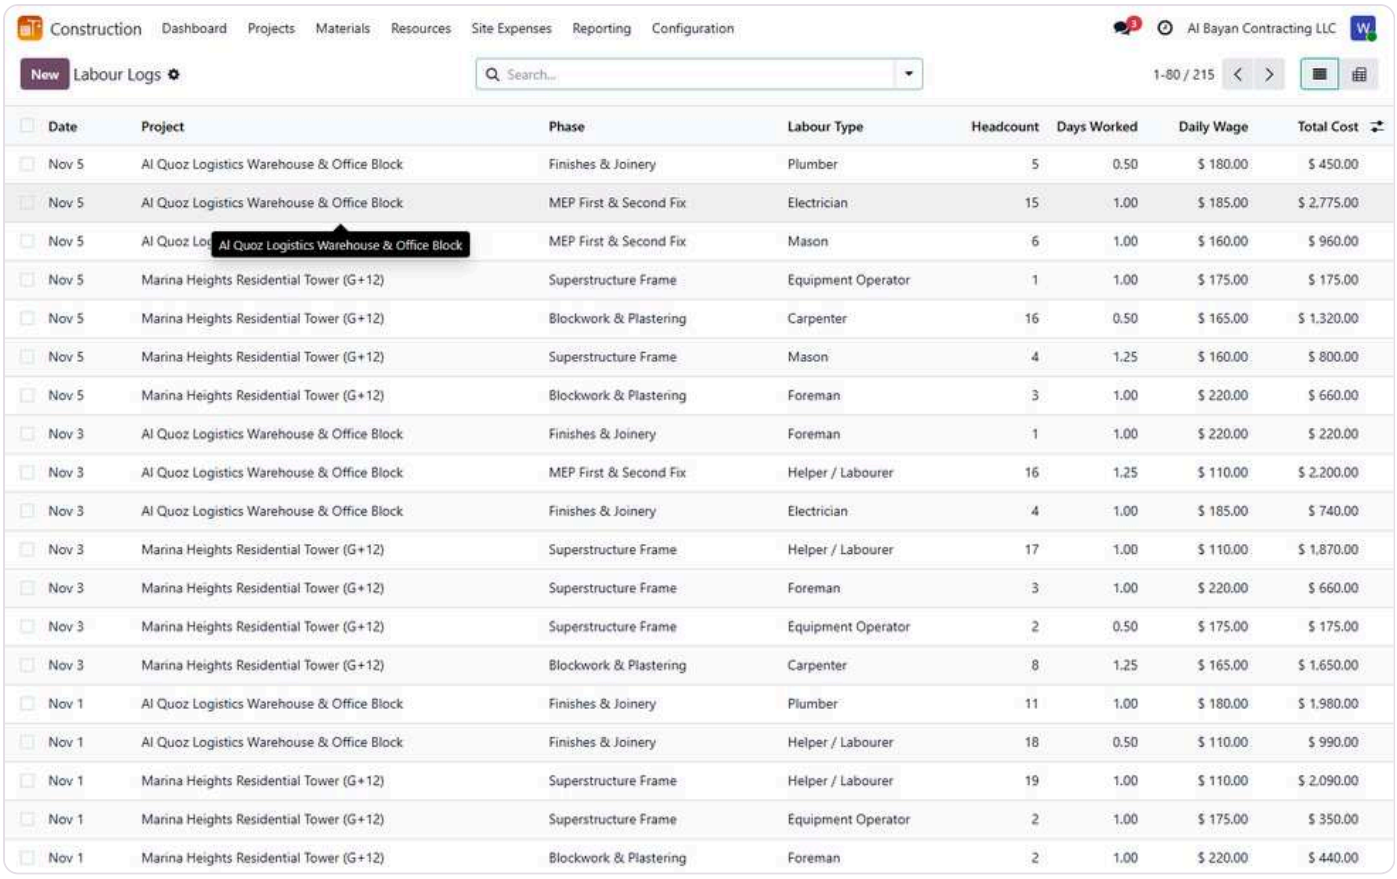


Date	Project	Phase	Labour Type	Headcount	Days Worked	Daily Wage	Total Cost
Nov 5	Al Quoz Logistics Warehouse & Office Block	Finishes & Joinery	Plumber	5	0.50	$ 180.00	$ 450.00
Nov 5	Al Quoz Logistics Warehouse & Office Block	MEP First & Second Fix	Electrician	15	1.00	$ 185.00	$ 2,775.00
Nov 5	Al Quoz Logistics Warehouse & Office Block	MEP First & Second Fix	Mason	6	1.00	$ 160.00	$ 960.00
Nov 5	Marina Heights Residential Tower (G+12)	Superstructure Frame	Equipment Operator	1	1.00	$ 175.00	$ 175.00
Nov 5	Marina Heights Residential Tower (G+12)	Blockwork & Plastering	Carpenter	16	0.50	$ 165.00	$ 1,320.00
Nov 5	Marina Heights Residential Tower (G+12)	Superstructure Frame	Mason	4	1.25	$ 160.00	$ 800.00
Nov 5	Marina Heights Residential Tower (G+12)	Blockwork & Plastering	Foreman	3	1.00	$ 220.00	$ 660.00
Nov 3	Al Quoz Logistics Warehouse & Office Block	Finishes & Joinery	Foreman	1	1.00	$ 220.00	$ 220.00
Nov 3	Al Quoz Logistics Warehouse & Office Block	MEP First & Second Fix	Helper / Labourer	16	1.25	$ 110.00	$ 2,200.00
Nov 3	Al Quoz Logistics Warehouse & Office Block	Finishes & Joinery	Electrician	4	1.00	$ 185.00	$ 740.00
Nov 3	Marina Heights Residential Tower (G+12)	Superstructure Frame	Helper / Labourer	17	1.00	$ 110.00	$ 1,870.00
Nov 3	Marina Heights Residential Tower (G+12)	Superstructure Frame	Foreman	3	1.00	$ 220.00	$ 660.00
Nov 3	Marina Heights Residential Tower (G+12)	Superstructure Frame	Equipment Operator	2	0.50	$ 175.00	$ 175.00
Nov 3	Marina Heights Residential Tower (G+12)	Blockwork & Plastering	Carpenter	8	1.25	$ 165.00	$ 1,650.00
Nov 1	Al Quoz Logistics Warehouse & Office Block	Finishes & Joinery	Plumber	11	1.00	$ 180.00	$ 1,980.00
Nov 1	Al Quoz Logistics Warehouse & Office Block	Finishes & Joinery	Helper / Labourer	18	0.50	$ 110.00	$ 990.00
Nov 1	Marina Heights Residential Tower (G+12)	Superstructure Frame	Helper / Labourer	19	1.00	$ 110.00	$ 2,090.00
Nov 1	Marina Heights Residential Tower (G+12)	Superstructure Frame	Equipment Operator	2	1.00	$ 175.00	$ 350.00
Nov 1	Marina Heights Residential Tower (G+12)	Blockwork & Plastering	Foreman	2	1.00	$ 220.00	$ 440.00

BASE Resources, Labour Logs: one line per trade per day, edited in place so a whole day's gang sheet goes in one screen.

A log carries the date, project, phase, labour type, headcount, days worked, the daily wage and a supervisor. Total cost is headcount times days times wage. Half days and overtime go in as fractions: 16 carpenters on 0.5 days, or 4 masons on 1.25. The wage fills in from the labour type when you pick the trade, and also when logs are created by an import or by another module, so no log is costed at zero by accident.

8.2 Equipment BASE

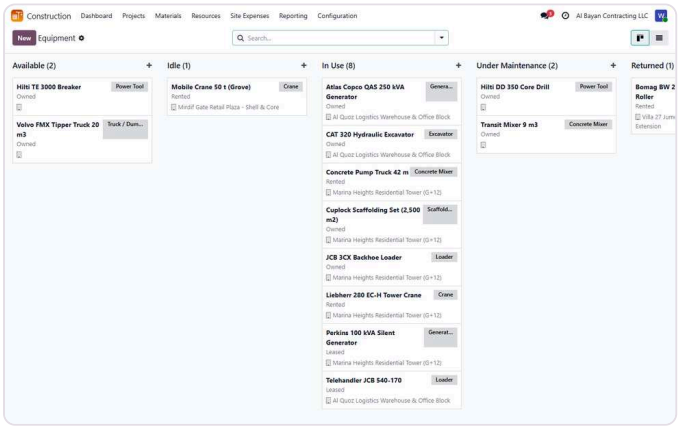


1 BASE

The equipment board

Resources, Equipment, grouped by status: available, in use, under maintenance, idle, returned. Each card shows the type, ownership and the job it is on.

Check the Idle column weekly: a hired machine standing idle is money going out for nothing.

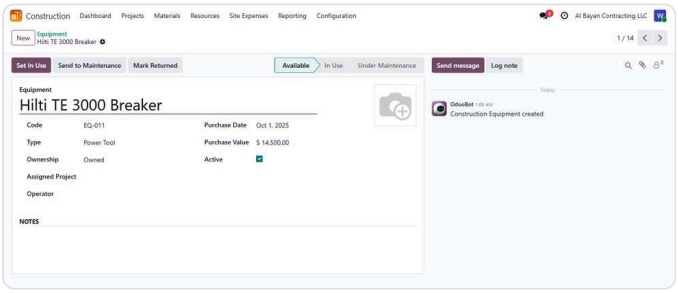


2 BASE

A machine

Name, code, type (excavator, crane, loader, mixer, roller, generator, truck, scaffolding, power tool, other), ownership (owned, rented, leased), assigned project, operator, rental supplier, daily rate, purchase date and value, photo. Buttons: **Set In Use**, **Set Available**, **Send to Maintenance**, **Mark Returned**.

In the Base module the daily rate is stored but no charge is worked out from it. Hire cost reaches the job when the hire invoice is recorded as a site expense with the machine picked. Enterprise adds plant hire with daily plant sheets that charge the job every day the machine is on site (Part 20).


8.3 Subcontracts BASE

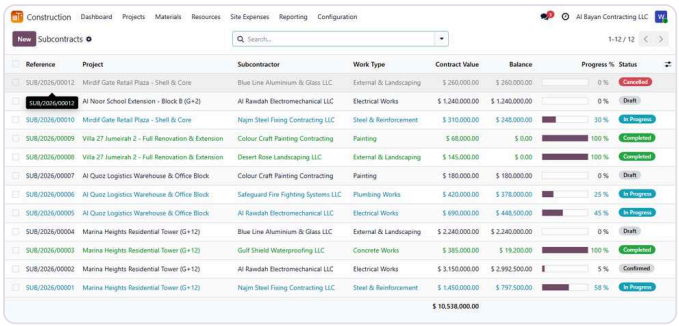

3 BASE

The subcontract register

Resources, Subcontracts. One line per order with subcontractor, work type, contract value, billed, paid, progress and status.

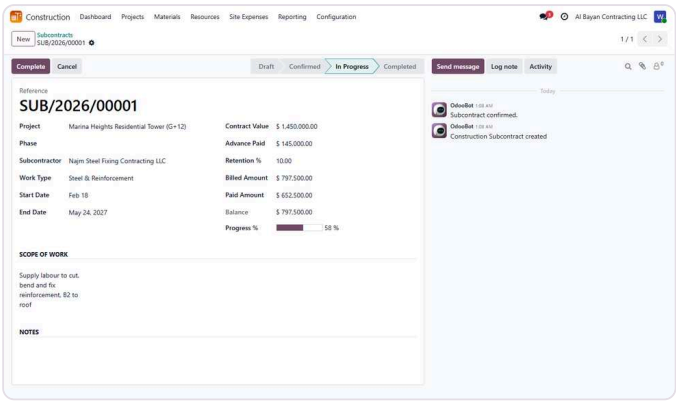

4 BASE

An order in progress


Project, phase, subcontractor, work type, scope, dates, contract value, advance paid, retention %, billed and paid amounts, balance (contract value less paid) and progress. **Confirm**, **Start Work**, **Complete** (sets progress to 100), **Cancel** and **Reset to Draft**.

For the job's cost, a live subcontract counts its **billed amount** as actual and its full contract value as **committed**, shown separately. Letting a large package does not wipe out the margin on the day it is signed, and the commitment stays in plain view. The billed and paid figures are typed on the order in the Base module; with Enterprise they come from certified subcontract valuations and paid vendor bills (Part 14).

8.4 Site expenses BASE

Site expense status BASE


1. **Draft** — Recorded with receipt ref
2. **Submitted** — For approval
3. **Approved** — Counts as cost
4. **Paid** — Payment date stamped

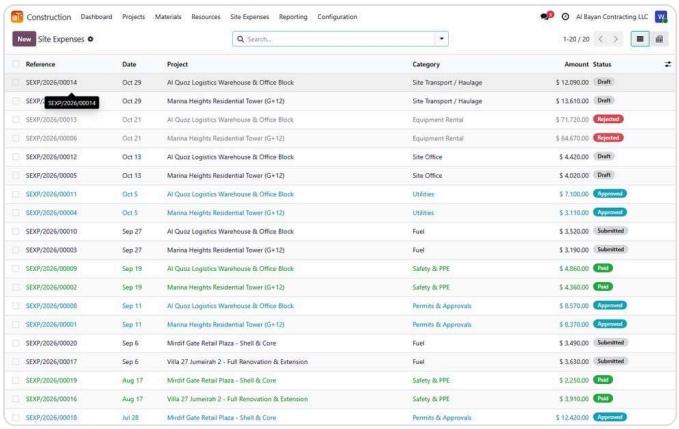

5 BASE

Everything else that costs money


Site Expenses: date, project, phase, category, the machine if it relates to one, description, amount, vendor or payee and the receipt or bill reference.

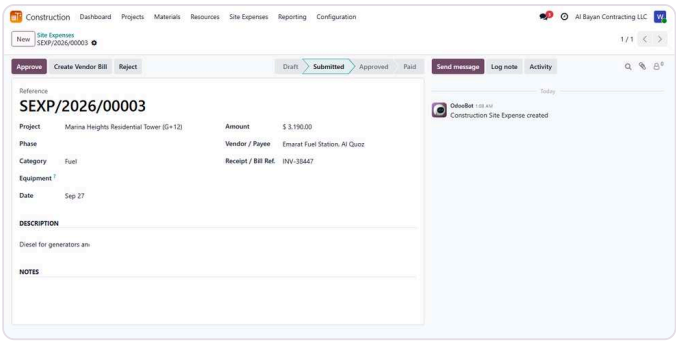

6 BASE

Submitted for approval

Approve and **Reject** are Project Manager buttons. A rejected expense can be reset to draft and corrected.

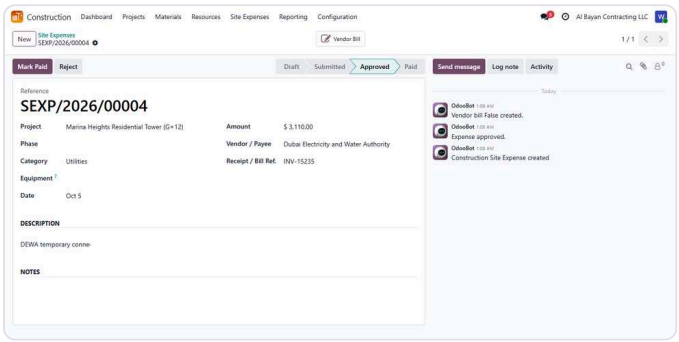


7 BASE

Approved, ready for a bill

Create Vendor Bill raises a draft vendor bill in Invoicing with the expense as one line, linked back, and a second one cannot be created. **Mark Paid** stamps the payment date.

The draft bill uses the first expense account in the chart. It is a draft so your accountant can set the right account.

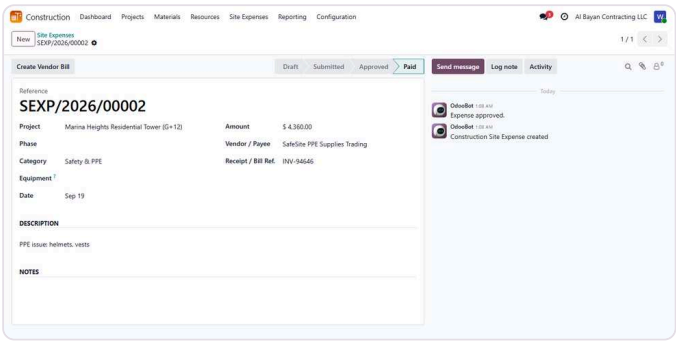

8 BASE


Paid

A paid expense keeps its link to the bill; the smart button opens it.

PART 9 The Base dashboard and reports


BASE

One screen for the whole portfolio, two analysis menus, and the project progress print for the monthly review.

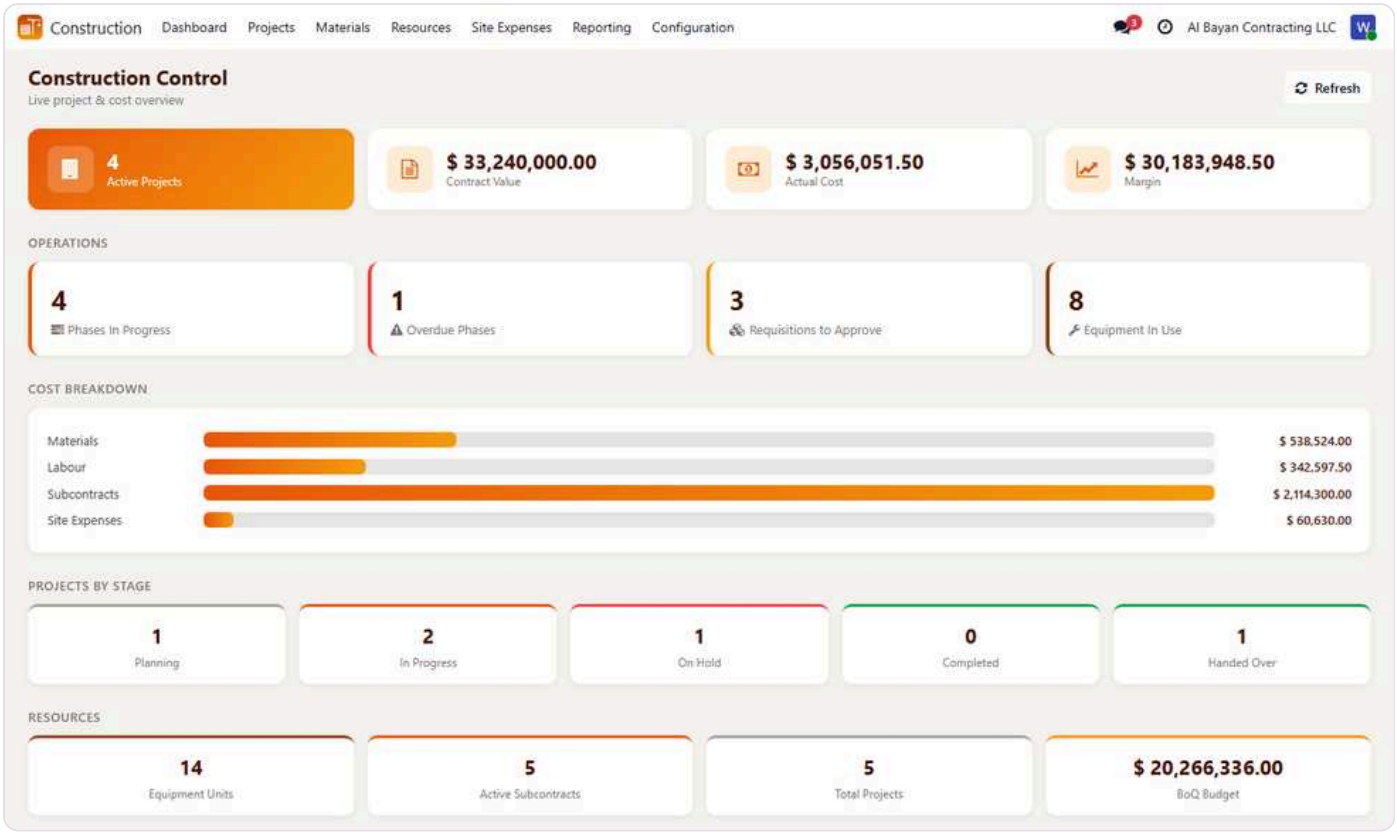

BASE Construction, Dashboard: Construction Control. Refresh reloads the figures.


Block	What it shows
Headline	Active projects, total contract value, actual cost and margin across the portfolio.
Operations	Phases in progress, overdue phases, requisitions waiting for approval, equipment in use. Each tile opens the records.
Cost Breakdown	Materials, labour, subcontracts and site expenses as bars.
Projects by Stage	Planning, in progress, on hold, completed, handed over.
Resources	Equipment units, active subcontracts, total projects and the total BoQ budget.



1 BASE

Cost Analysis

Reporting, Cost Analysis: site expenses by project against category, as a pivot, a graph and a list. It includes every expense whatever its status, so filter on approved and paid for the figure the cost summary uses.



2 BASE

Labour Analysis

Reporting, Labour Analysis: labour cost by project against trade, which is where an overrun on one trade shows first.

Your logo

Al Bayan Contracting LLC
Office 1204, Bay Square Building 7, Business Bay
Dubai CA 94005
United Arab Emirates

Project Progress Report

Project: Marina Heights Residential Tower (G+12)
Code: ABC-2025-014
Client: Marina Crest Developments LLC
Stage: In Progress

Overall Progress: 45.0%
Start: 01/19/2026
Expected Finish: 09/21/2027

Phases

Phase	Work Type	Planned Start	Planned Finish	Progress %	Status
Mobilisation & Site Preparation	Earthwork & Excavation	01/19/2026	04/05/2026	100.0	Completed
Excavation & Foundations	Earthwork & Excavation	04/06/2026	06/20/2026	100.0	Completed
Substructure & Waterproofing	Concrete Works	06/21/2026	09/04/2026	100.0	Completed
Superstructure Frame	Concrete Works	09/05/2026	11/19/2026	45.0	In Progress
Blockwork & Plastering	Masonry	11/20/2026	02/03/2027	15.0	In Progress
MEP First & Second Fix	Electrical Works	02/04/2027	04/20/2027	0.0	Not Started
Finishes & Joinery	Painting	04/21/2027	07/05/2027	0.0	Not Started
External Works & Handover	External & Landscaping	07/06/2027	09/20/2027	0.0	Not Started

Cost Summary

Contract Value	$ 18,650,000.00
BoQ Budget	$ 11,370,900.00
Material Cost	$ 223,600.00
Labour Cost	$ 96,383.75
Subcontract Cost	$ 1,434,500.00
Site Expenses	$ 15,840.00
Actual Cost	**$ 1,770,323.75**
Margin	**$ 16,879,676.25**

BASE Print, Project Progress Report on the project: every phase with dates, progress and status, then the cost summary down to margin. The director's monthly page per job.

A working week on the Base module BASE

1. Each evening the site engineer enters the day's labour logs from the gang sheet.
2. Material needs for the coming days go in as requisitions against the phase and are submitted.
3. The project manager approves requisitions and expenses from the dashboard tiles.
4. When materials arrive, the engineer records the issued quantities and issues the requisition.
5. Hire invoices, transport and small spends go in as site expenses; approved ones become draft vendor bills.

6. Once a week the project manager updates subcontract billed and paid figures and checks idle equipment.
7. At month end, print the Project Progress Report for each job and compare cost by phase with the phase budgets.

PART 10 Tenders, CRM and client quotations

ENTERPRISE


Everything from first sight of an opportunity to the award, on one record per tender: qualify it, price it, hear back. The priced estimate then becomes the job, so nothing is typed twice.

TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Tenders, Pipeline
2. Open a tender in the Estimating column and read the estimate block
3. Look at the Go / No-Go Checklist and the bid bond
4. Open Commercial, Tenders, Competitor Analysis

From opportunity to job ENTERPRISE

1. **Opportunity** — In CRM, Create Tender
2. **Qualify** — Go or no-go, bid bond
3. **Price** — Estimate bill, markup
4. **Quote** — Client quotation in Sales
5. **Award** — Project, contract and bill in one step

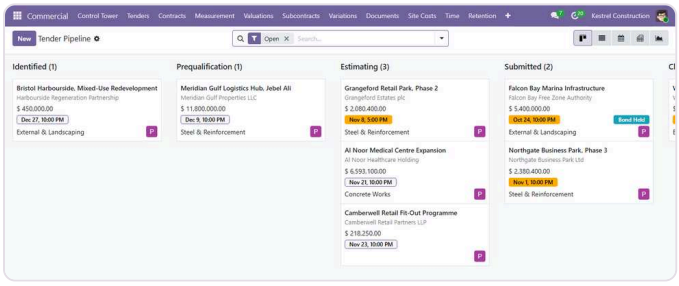


1 ENTERPRISE

The tender pipeline

Commercial, Tenders, Pipeline. A kanban by stage. Stages are rows you can add to (Commercial, Configuration, Tender Stages), each flagged as folded, bid submitted, won or lost, so a "Site Visit" stage between prequalification and estimating is a row, not a release.

The card shows the client, the deadline, the tender value and the estimator.

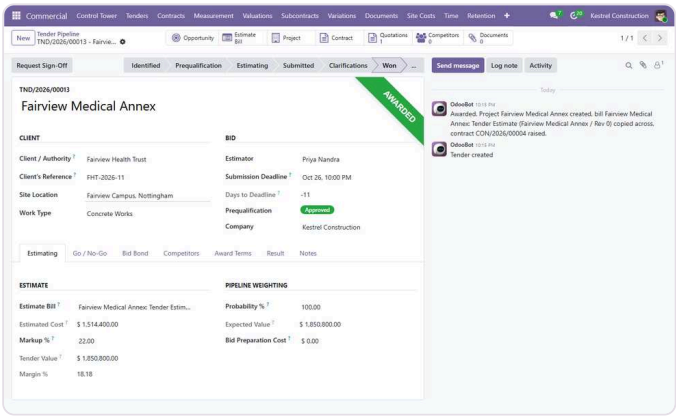


2 ENTERPRISE

A tender

Our reference, the project title, the client and their own reference, the estimator, the submission deadline with days left, site location, work type and prequalification status. Below: the estimate bill, estimated cost, **Markup %**, tender value and margin, probability and expected value, and the commercial terms: advance %, retention %, defects period, payment terms and billing basis.

Apply Markup sets every estimate line's sell rate from its cost plus the markup.

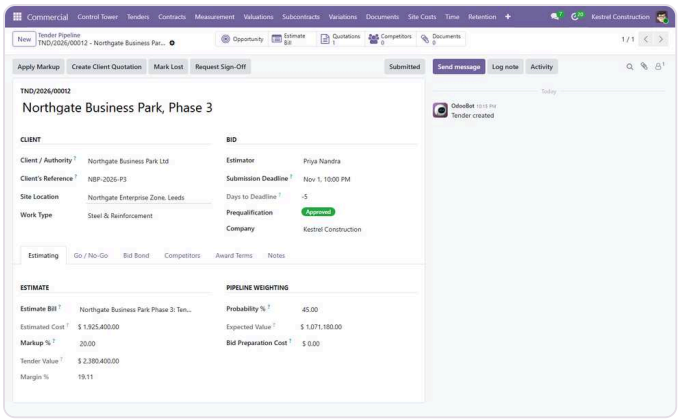


3 ENTERPRISE

Go or no-go, bid bond, competitors

The checklist is weighted yes, no or not applicable questions, and the score is the weighted share answered yes. The bid bond records the amount, percentage, bank, number, issue and expiry dates, with a warning when it is about to expire. Competitors record who else bid, their price, their rank and who won.


Request Sign-Off sends the go decision through the approval chain before the price leaves the building.

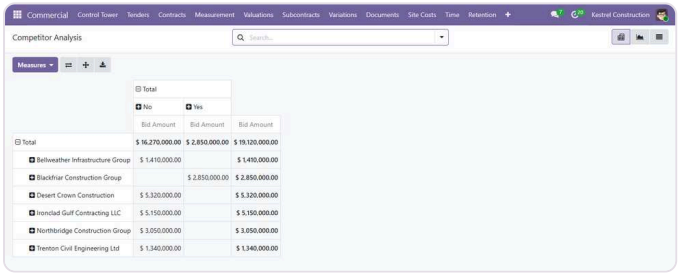

5 ENTERPRISE

Competitor analysis


A pivot of every competitor bid: how often each firm bids against you, how often it wins, and how far its prices sit from yours.



4 ENTERPRISE

Bid bonds

Tenders, Bid Bonds lists every tender whose bond is live, nearest expiry first, so a bond does not lapse while the client is still deciding.

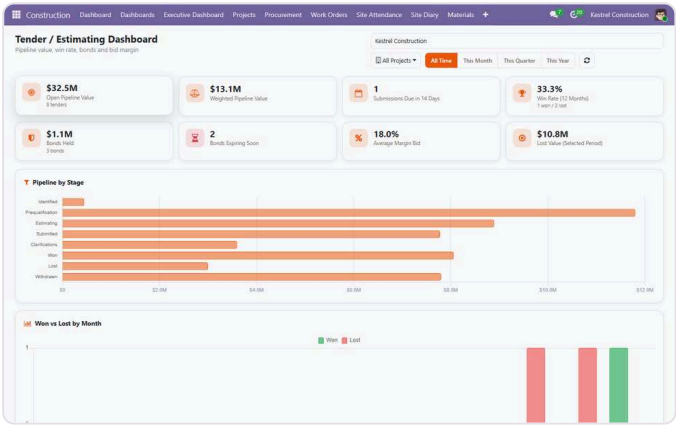


6 ENTERPRISE

The tender dashboard

Dashboards, Tender / Estimating: the pipeline by stage, value and expected value, win rate, deadlines this week and bonds expiring. Part 26 covers every dashboard.


Opportunities and quotations ENTERPRISE

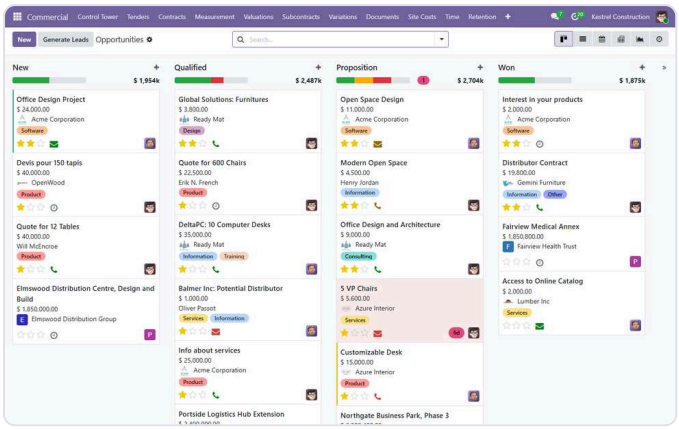

7 ENTERPRISE

Opportunities in CRM

Tenders, Opportunities opens the standard CRM pipeline. **Create Tender** on an opportunity opens one tender for it, and reopens the same tender if pressed again.

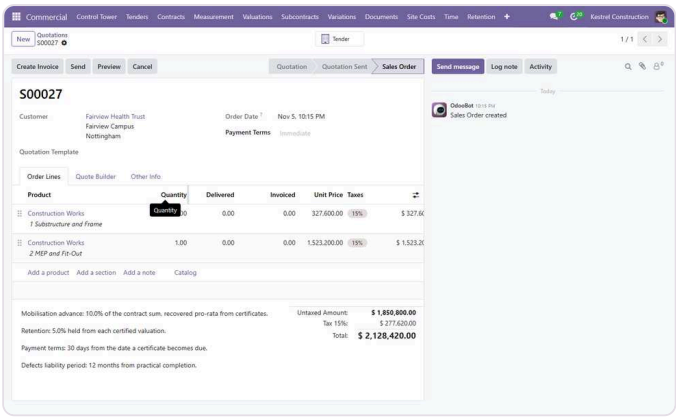

8 ENTERPRISE

The client quotation

Create Client Quotation on the tender turns the priced estimate into a normal Odoo quotation: one line per bill section or one per bill item, a validity date, and optionally the advance, retention and payment terms written into the note.

Confirming the quotation in Sales is one of two ways to award the tender; the other is the Award button.

Award or lose ENTERPRISE

Award opens a dialog with the client, project name, contract value and date of possession, and two options: apply a project template, and raise a contract (with advance %, retention %, defects period and payment terms). The estimate bill is copied to the new job as its contract bill. One click creates the project, the bill and the contract. **Mark Lost** records the outcome (lost to a competitor or withdrawn), a loss reason from the configured list, and a note.



Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Tender Submission Summary

Fairview Medical Annex

Client / Authority	Fairview Health Trust	Our Reference	TND/2026/00013
Client's Reference	FHT-2026-11	Submission Deadline	10/26/2026 10:00:00 PM
Site Location	Fairview Campus, Nottingham	Work Type	Concrete Works
Estimator	Priya Nandra	Tender Value	$ 1,850,800.00

Priced Bill Summary

Section	Amount
1 Substructure and Frame	$ 327,600.00
2 MEP and Fit-Out	$ 1,523,200.00
Tender Value	$ 1,850,800.00

Prepared By

Date

ENTERPRISE Print, Tender Submission Summary: the bid as it went out, with the estimate, markup and terms.


PART 11 Contracts, measurement and getting paid ENTERPRISE

The money chain in full: a contract that holds the terms, a measurement book against the bill, an interim valuation, the application for payment, the certificate with claimed against certified, and the invoice. Every step is a dated record with an owner.

TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Contracts, Contracts and open the Harlow Court contract
2. Open Commercial, Measurement, Measurement Book and open a certified sheet
3. Open Commercial, Valuations, Payment Certificates and compare claimed with certified
4. Open Commercial, Valuations, Raise a Valuation and read the figures, then Discard


11.1 The contract ENTERPRISE



1 ENTERPRISE

The contract register

Commercial, Contracts, Contracts. One per job, or one per section on a job let in sections. Kanban, list, calendar and pivot.

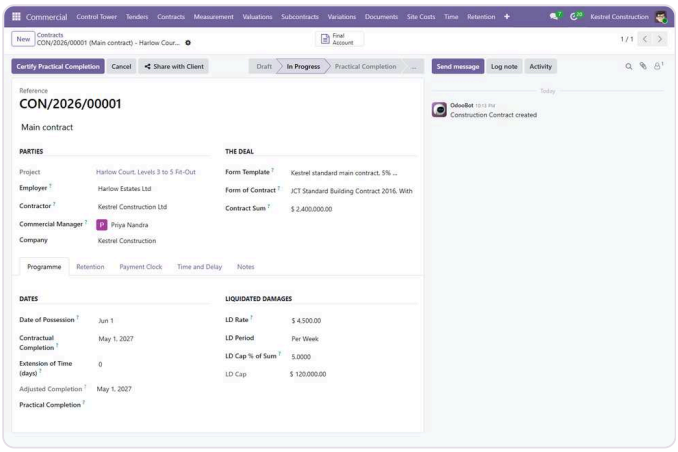

2 ENTERPRISE

A contract

Employer and contractor, the commercial manager who gets chased, the form of contract and the contract sum. Dates: possession, contractual completion, extension of time days, adjusted completion, practical completion, defects period and its end. Retention: %, limit as % of the sum, first moiety %, with both release amounts and due dates. Valuation day, days to certify, days to pay, and the next valuation, payment due and final date for payment. Liquidated damages rate, period and cap.


Pick a **Form Template** and the terms fill in from Commercial, Configuration, Forms of Contract.

Button	What it does
Start on Site	Draft to in progress. Valuations can now be raised.
Certify Practical Completion	Records the date; the first moiety of retention falls due and the defects period starts counting.
Start Defects Period	Moves the contract into defects liability.
Release First Moiety, Release Final Moiety	Write the release rows on the retention ledger with their due dates.

Close, Cancel, Reset to Draft	End of life, or a contract raised in error.
Share with Client	Opens the standard Grant Portal Access dialog for the employer, so the client can see the contract online (Part 23).
Programmes, Delay Events, EOT Claims	Smart buttons into the time layer (Part 18).

A daily job warns the commercial manager before each valuation date, using the contract's own lead time, and chases retention that has fallen due and not been released.


11.2 The measurement book ENTERPRISE

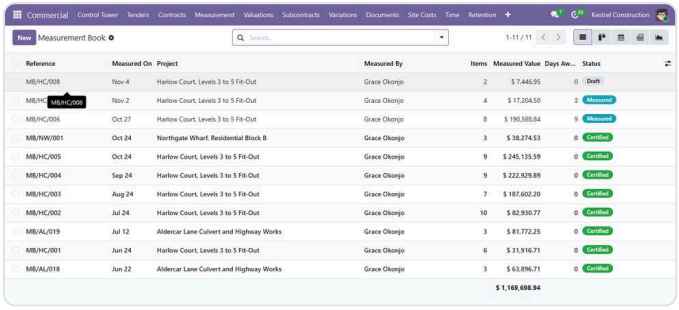

3 ENTERPRISE

Measurement sheets

Commercial, Measurement, Measurement Book. Each sheet is one visit with the tape: date, site book folio, who measured, who witnessed, items, value at bill rates, days awaiting certification and status.

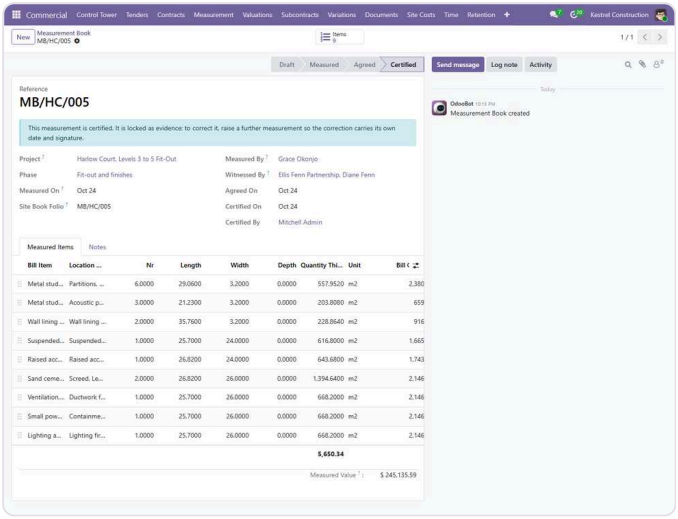

4 ENTERPRISE

A certified sheet


Each line names a bill item and the location measured, with Nr, length, width and depth; the quantity is their product with blanks ignored. Beside it: bill quantity, measured previously, measured to date and remaining in the bill.

A sheet that would take an item past its bill quantity is refused with the excess. Raise a variation instead (Part 12).

Measurement status ENTERPRISE

1. **Draft** — Being written up
2. **Measured** — Book as Measured: now a claim
3. **Agreed** — Mark Agreed: both sides signed
4. **Certified** — Certify: claimable and frozen

Commercial, Measurement, Measured Quantities lists every measured line across all sheets, for a pivot by item or by location. A daily job chases sheets that have sat measured and uncertified, because work measured and never certified is money outside the valuation.

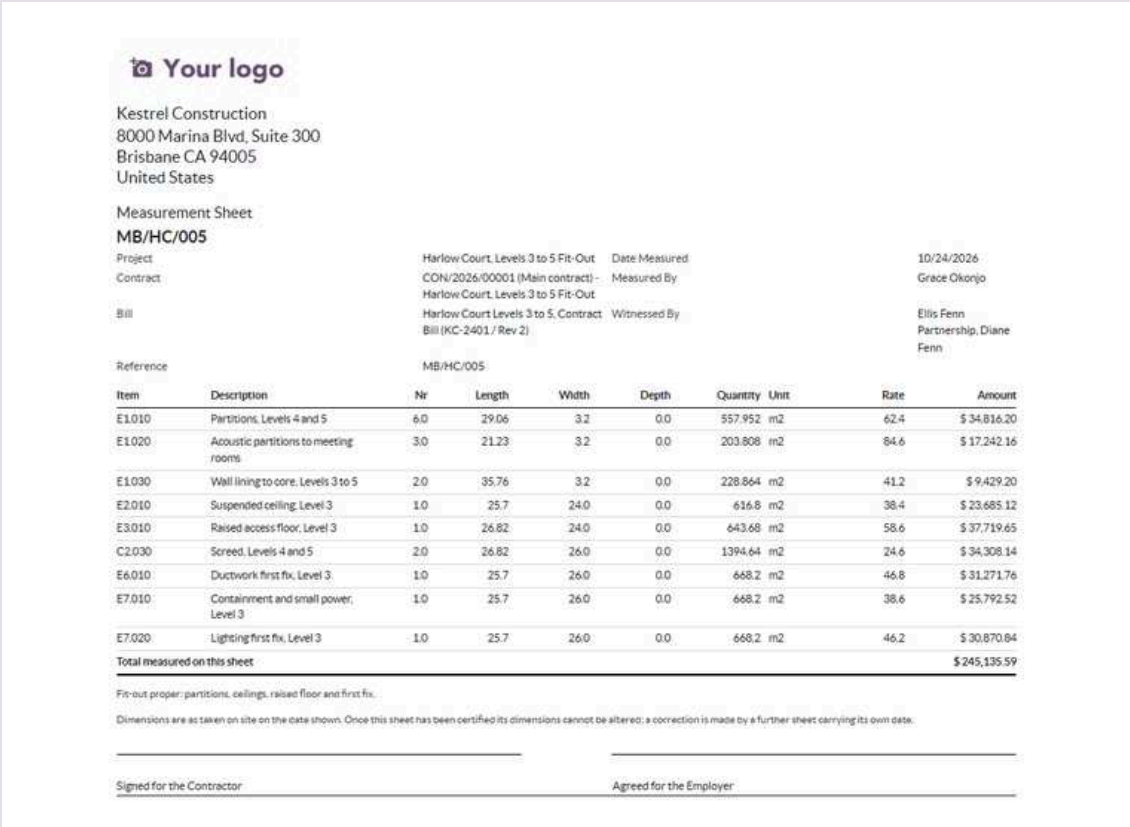

Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Measurement Sheet
MB/HC/005

Project	Harlow Court, Levels 3 to 5 Fit-Out	Date Measured	10/24/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Measured By	Grace Okonjo
Bill	Harlow Court Levels 3 to 5, Contract Bill (KC-2401 / Rev 2)	Witnessed By	Ellis Fenn Partnership, Diane Fenn
Reference	MB/HC/005		

Item	Description	Nr	Length	Width	Depth	Quantity	Unit	Rate	Amount
E1.010	Partitions, Levels 4 and 5	6.0	29.06	3.2	0.0	557.952	m2	62.4	$ 34,816.20
E1.020	Acoustic partitions to meeting rooms	3.0	21.23	3.2	0.0	203.808	m2	84.6	$ 17,242.16
E1.030	Wall lining to core, Levels 3 to 5	2.0	35.76	3.2	0.0	228.864	m2	41.2	$ 9,429.20
E2.010	Suspended ceiling, Level 3	1.0	25.7	24.0	0.0	616.8	m2	38.4	$ 23,685.12
E3.010	Raised access floor, Level 3	1.0	26.82	24.0	0.0	643.68	m2	58.6	$ 37,719.65
C2.030	Screed, Levels 4 and 5	2.0	26.82	26.0	0.0	1394.64	m2	24.6	$ 34,308.14
E6.010	Ductwork first fix, Level 3	1.0	25.7	26.0	0.0	668.2	m2	46.8	$ 31,271.76
E7.010	Containment and small power, Level 3	1.0	25.7	26.0	0.0	668.2	m2	38.6	$ 25,792.52
E7.020	Lighting first fix, Level 3	1.0	25.7	26.0	0.0	668.2	m2	46.2	$ 30,870.84
Total measured on this sheet									**$ 245,135.59**

Fit-out proper: partitions, ceilings, raised floor and first fix.


Dimensions are as taken on site on the date shown. Once this sheet has been certified its dimensions cannot be altered; a correction is made by a further sheet carrying its own date.

Signed for the Contractor

Agreed for the Employer

ENTERPRISE Print, Measurement Sheet: the dimensions as they were taken, for signature.

11.3 Raise a valuation ENTERPRISE

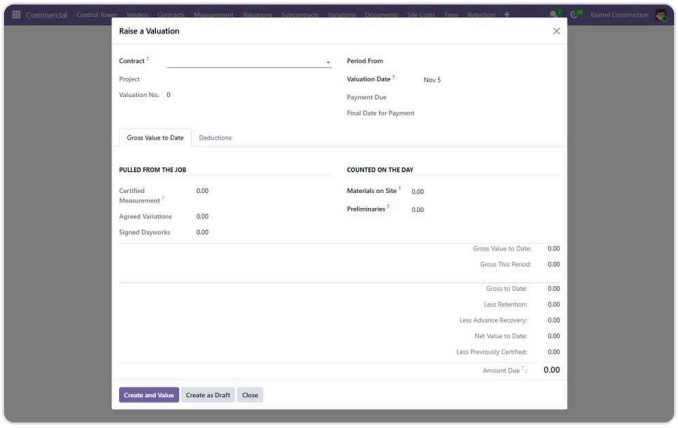


5 ENTERPRISE

The valuation wizard

Commercial, Valuations, Raise a Valuation. Pick the contract and the valuation date. It pulls certified measurement, agreed variations and signed dayworks to that date, and you key materials on site and time-related preliminaries. On the first valuation enter the advance paid and the recovery percentage; later valuations carry them forward.

The screen shows gross to date, this period, previously certified, retention, advance recovery and the amount due before anything is written.

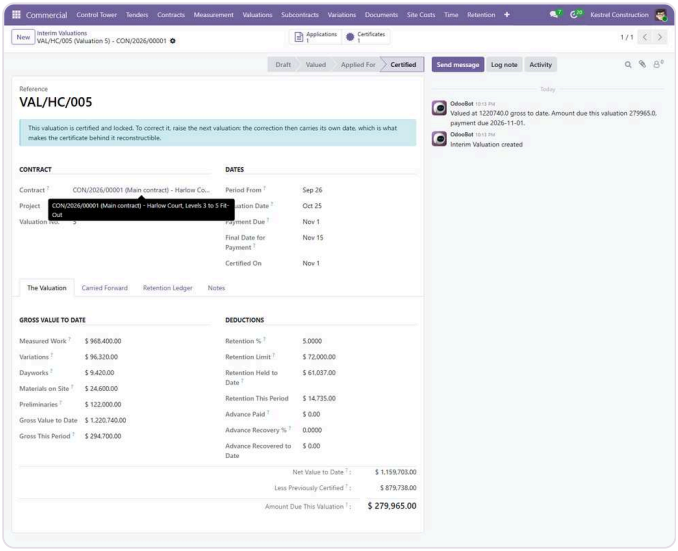


6 ENTERPRISE

An interim valuation

Create and Value writes it as valued; **Create as Draft** leaves it for review. On the form, **Pull Figures** re-reads the source documents, **Book as Valued**, **Apply for Payment** raises the application, and **Certify** holds the retention.

Valuations are numbered per contract, the way a quantity surveyor counts them.

11.4 Application and certificate ENTERPRISE

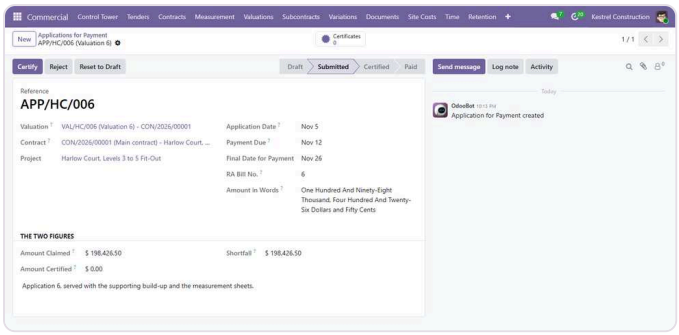


7 ENTERPRISE

Application for payment

The amount claimed is snapshotted from the valuation when the application is served. Payment due is the application date plus the days to certify; the final date for payment adds the days to pay. **Submit**, then **Certify** raises the certificate pre-filled with what was claimed.

A daily job flags an application past its due date with no certificate served: the moment to write to the client.

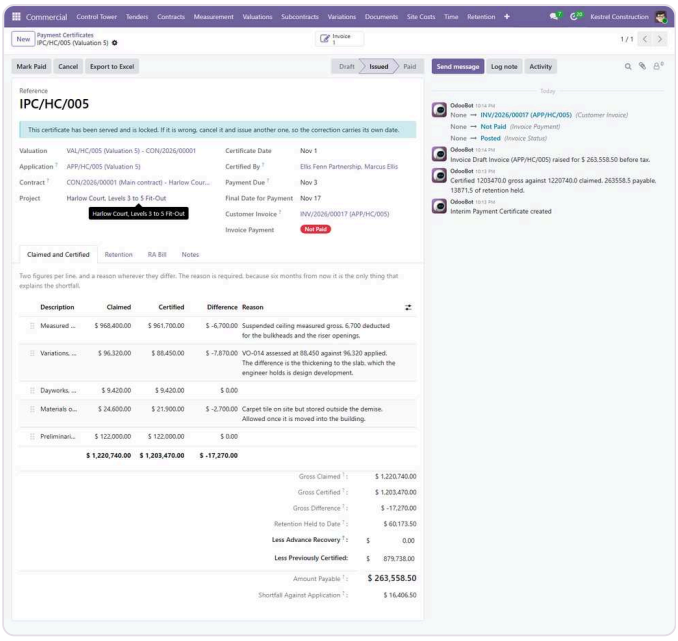


8 ENTERPRISE

The payment certificate

Claimed against certified, line by line (measured work, each variation, dayworks, materials on site, preliminaries), with the difference and a reason. A difference without a reason is refused. Below: retention %, limit, held previously, held to date and this certificate; less previously certified; less advance recovery; amount payable and the shortfall against the application.

Retention is worked on the gross certified, not the gross claimed.

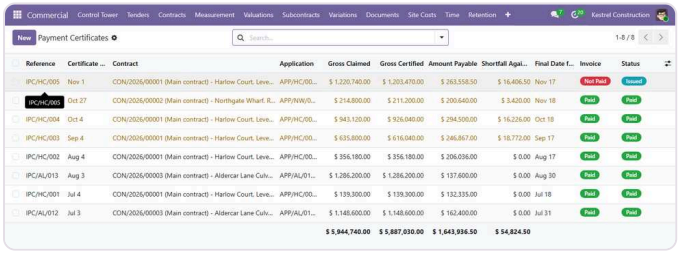


9 ENTERPRISE

Certificates in a list

Gross claimed, gross certified, amount payable, shortfall, final date for payment, invoice and status, so the gap between what you asked for and what you got is one column.

Issue Certificate serves it, writes the retention held on the ledger and stops the payment clock. **Mark Paid** records payment by hand; normally the payment comes from the invoice.

11.5 From certificate to invoice ENTERPRISE

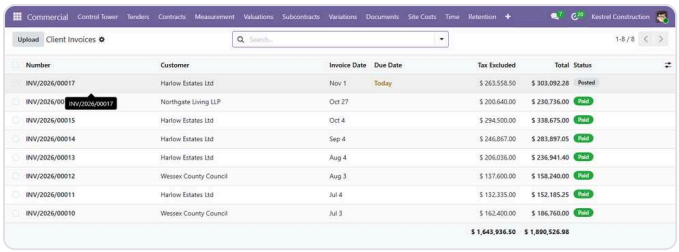

10 ENTERPRISE

Client invoices

Create Invoice on an issued certificate raises a draft customer invoice: the work certified on the income account, retention and advance recovery on their own lines, with the taxes and journal from Settings. Your accountant posts it.

Commercial, Valuations, Client Invoices lists only invoices raised from certificates.

11 ENTERPRISE

Payments flow back

When Accounting records the payment, the certificate follows to paid, and the subcontract side works the same way. A daily job catches anything still out of step.

11.6 The RA bill and the certificate prints ENTERPRISE


Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Running Account (RA) Bill No. 5
IPC/HC/005

Project	Harlow Court, Levels 3 to 5 Fit-Out	Bill Date	11/01/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Against Application	APP/HC/005
Employer	Harlow Estates Ltd		

Claimed Against Certified

Item	Claimed	Certified
Measured work to date, against the contract bill	$ 968,400.00	$ 961,700.00
Variations, agreed and assessed	$ 96,320.00	$ 88,450.00
Dayworks, signed sheets only	$ 9,420.00	$ 9,420.00
Materials on site, unfixed	$ 24,600.00	$ 21,900.00
Preliminaries, time related	$ 122,000.00	$ 122,000.00

Previous, This Bill and Cumulative

Gross value up to previous bill	$ 879,738.00
Gross value of this bill	$ 323,732.00
Cumulative gross value certified to date	**$ 1,203,470.00**

Deductions

Retention this bill	$ 13,871.50
Retention held to date (at 5.0%)	$ 60,173.50
Advance recovery to date	$ 0.00
Other deductions	$ 0.00
Less previously certified	$ 879,738.00
Net payable on this bill	**$ 263,558.50**

Amount in words: Two Hundred And Sixty-Three Thousand, Five Hundred And Fifty-Eight Dollars and Fifty Cents only.

Certified by Ellis Fenn Partnership as contract administrator.

Submitted by the Contractor — Certified by Marcus Ellis

ENTERPRISE Print, Running Account (RA) Bill from the certificate: previous, this bill and cumulative, deductions, net payable and the amount in words.


Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Interim Payment Certificate
IPC/HC/005

Project	Harlow Court, Levels 3 to 5 Fit-Out	Certificate Date	11/01/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Payment Due	11/03/2026
Against Application	APP/HC/005	Final Date for Payment	11/17/2026
Employer	Harlow Estates Ltd		

Claimed Against Certified

Item	Claimed	Certified	Difference	Reason for the Difference
Measured work to date, against the contract bill	$ 968,400.00	$ 961,700.00	$ -6,700.00	Suspended ceiling measured gross. 6,700 deducted for the bulkheads and the riser openings.
Variations, agreed and assessed	$ 96,320.00	$ 88,450.00	$ -7,870.00	VO-014 assessed at 88,450 against 96,320 applied. The difference is the thickening to the slab, which the engineer holds is design development.
Dayworks, signed sheets only	$ 9,420.00	$ 9,420.00	$ 0.00	
Materials on site, unfixed	$ 24,600.00	$ 21,900.00	$ -2,700.00	Carpet tile on site but stored outside the demise. Allowed once it is moved into the building.
Preliminaries, time related	$ 122,000.00	$ 122,000.00	$ 0.00	
Gross value certified to date	$ 1,220,740.00	$ 1,203,470.00	$ -17,270.00	

Payment

Gross value certified to date	$ 1,203,470.00
Less retention at 5.0%	$ 60,173.50
Less advance recovered	$ 0.00
Less previously certified	$ 879,738.00
Amount certified for payment	**$ 263,558.50**

This certificate is $ 10,406.50 below the sum applied for. The reason for every difference is stated against the item above.

Certified by Ellis Fenn Partnership as contract administrator.

Certified by Marcus Ellis — Date

ENTERPRISE Print, Payment Certificate: the same figures under the heading chosen in Settings.


Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Application for Payment
APP/HC/006

Project	Harlow Court, Levels 3 to 5 Fit-Out	Application Date	11/05/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Payment Due	11/12/2026
Valuation	VAL/HC/006 (Valuation 6) - CON/2026/00001	Final Date for Payment	11/26/2026
Employer	Harlow Estates Ltd		

Value of the Works

Description	Amount
Measured work to date	$ 1,110,000.00
Variations	$ 121,780.00
Dayworks	$ 12,860.00
Materials on site	$ 21,300.00
Preliminaries	$ 146,400.00
Gross value to date	**$ 1,412,340.00**
Less retention at 5.0%	$ 70,617.00
Less advance recovered	$ 0.00
Less previously certified	$ 1,143,296.50
Amount now applied for	**$ 198,426.50**

Application 6, served with the supporting build-up and the measurement sheets.

This application is made under the contract named above. Payment falls due on the date shown and the final date for payment is as stated. Any notice of intention to pay less than the sum applied for must be given in the time the contract allows.

Signed for the Contractor — Date

ENTERPRISE Print, Application for Payment.


Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Running Account (RA) Bill No. 6
APP/HC/006

Project	Harlow Court, Levels 3 to 5 Fit-Out	Bill Date	11/05/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Payment Due	11/12/2026

Amount Now Applied For

This bill	**$ 198,426.50**

Amount in words: One Hundred And Ninety-Eight Thousand, Four Hundred And Twenty-Six Dollars and Fifty Cents only.

Signed for the Contractor — Date

ENTERPRISE Print, RA Bill from the application, before it is certified.

The RA Bill number is the certificate's position among the live certificates on the contract, and **Other Deductions** on the certificate comes off the net payable on the RA Bill only. **Export to Excel** on the certificate gives the same figures as a spreadsheet.

PART 12

Variations, instructions, dayworks and provisional sums

ENTERPRISE

Change is where contractors win or lose the job. An instruction is logged with a clock on it, priced as a variation, valued from dayworks when it has to be, and only then put on the bill where it can be measured.


TRY IT YOURSELF ON THE DEMO


1. Open Commercial, Variations, Site Instructions and find a lapsed one
2. Open an agreed variation and read the priced items
3. Open Variations, Exposure as a pivot by reason
4. Open Daywork Sheets and filter on Submitted for Signature

How a change becomes money ENTERPRISE

1. **Instruction** — Verbal or written, with a confirm-by date
2. **Variation** — Priced, submitted, agreed
3. **Dayworks** — Signed sheets value it
4. **Bill items** — Create Bill Items
5. **Valuation** — Measured and certified

12.1 Site instructions ENTERPRISE

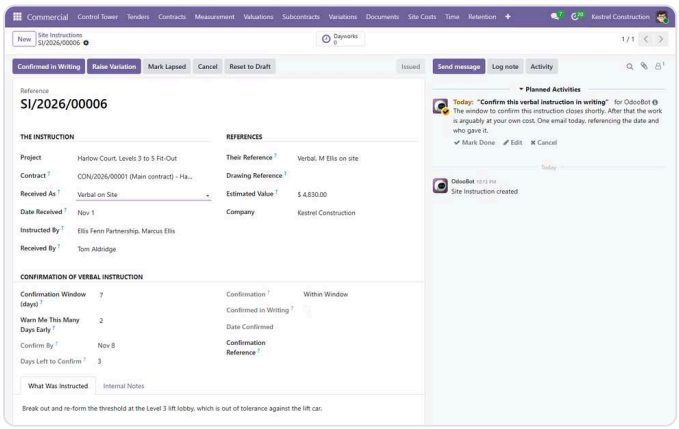

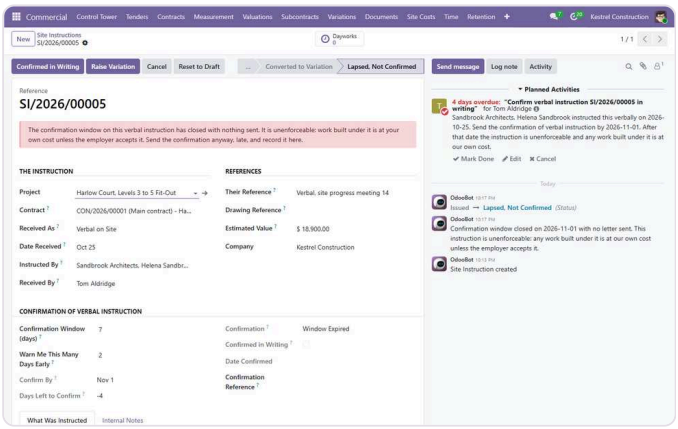

1 ENTERPRISE

An instruction

Commercial, Variations, Site Instructions. How it was received (verbal, written, drawing), the date, their reference, the drawing, who instructed and who received it, the words used, and a rough value. A verbal instruction has a confirmation window in days and a warning lead time; **Confirm By** is worked out from them.


Issue makes it live. **Confirmed in Writing** records the letter. **Raise Variation** creates one variation from it.

2 ENTERPRISE

Lapsed, not confirmed

If the window shuts with nothing sent, the daily job records it as lapsed. **Mark Lapsed** does the same by hand. Reporting, Unconfirmed Verbal Instructions lists every verbal instruction still at risk.


12.2 Variations ENTERPRISE

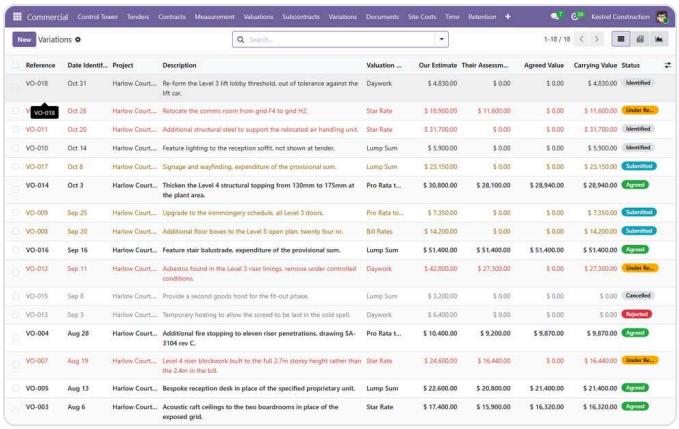

3 ENTERPRISE

The variation register

Commercial, Variations, Variations. Reference, project, reason (client change, design development, site condition, statutory, error in the documents, other), valuation method, our estimate, their assessment, agreed value and status.

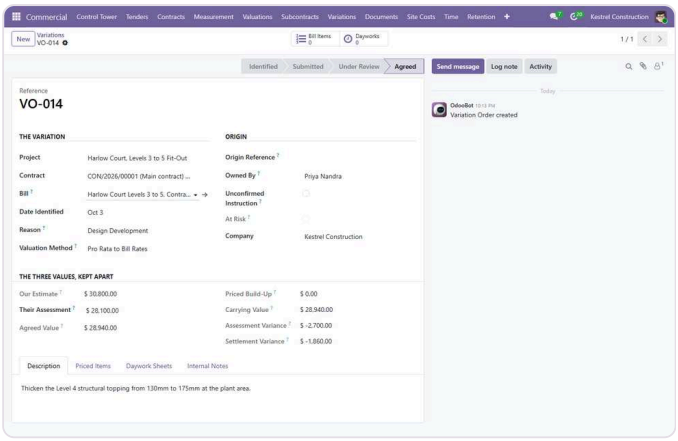


4 ENTERPRISE

An agreed variation

Priced items (item number, description, unit, quantity, precise rate, cost rate, margin) sit inside the variation, not on the bill, until it is agreed. **Submit to Client**, **Under Review**, **Agreed** (the agreed value is written here and nowhere else), **Rejected**, **Withdraw**.

Create Bill Items turns the priced items into bill items the book can measure.



5 ENTERPRISE

Exposure

Variations, Exposure: every variation not yet settled, at its carrying value, by reason and by job. The money still in argument.



Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Variation Order
VO-014

Project	Harlow Court, Levels 3 to 5 Fit-Out	Date	10/03/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Status	Agreed
Instruction	None	Valuation Method	Pro Rata to Bill Rates

The Work

Thicken the Level 4 structural topping from 130mm to 175mm at the plant area.

Value


Submitted by the Contractor	$ 30,800.00
Assessed by the Employer	$ 28,100.00
Agreed value	$ 28,940.00

Signed for the Contractor

Agreed for the Employer

ENTERPRISE Print, Variation Order: the instruction, the priced items and the values.

12.3 Daywork sheets ENTERPRISE

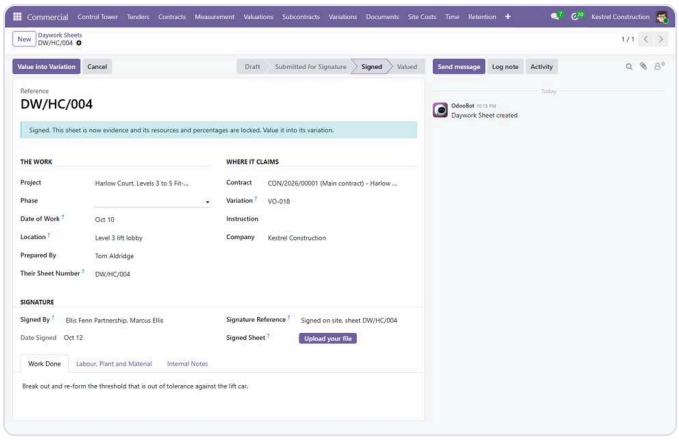


6 ENTERPRISE

A signed daywork sheet

Date, location, work done, their sheet number, and resources: labour by trade, plant and materials, each with hours or quantity and the contract daywork rate. Labour, plant and material additions for overheads are percentages on the sheet.

A sheet dated a fortnight after the work is a sheet the client refuses. Date it the day it happened.




7 ENTERPRISE

Unsigned sheets

Reporting, Unsigned Daywork Sheets, with the days each has waited. A daily job chases them as they age.

Daywork button	What it does
Submit for Signature	Out to the client's representative today.
Record Signature	Who signed, when, the reference, and a scan of the signed sheet. Now it is money.
Signature Refused	Record why on the day, while somebody remembers.
Value into Variation	Take the signed sheet into its variation, and push the total onto the variation estimate.

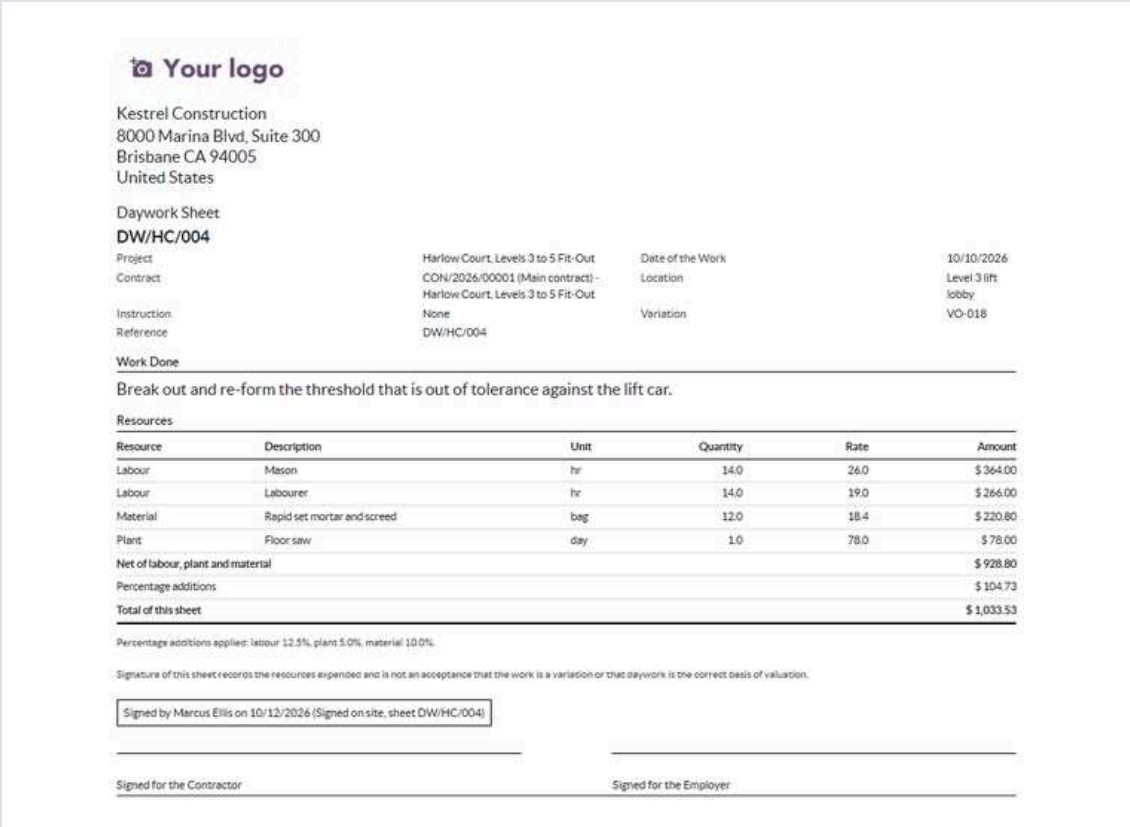

Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Daywork Sheet
DW/HC/004

Project	Harlow Court, Levels 3 to 5 Fit-Out	Date of the Work	10/10/2026
Contract	CON/2026/00001 (Main contract) - Harlow Court, Levels 3 to 5 Fit-Out	Location	Level 3 lift lobby
Instruction	None	Variation	VO-018
Reference	DW/HC/004		

Work Done

Break out and re-form the threshold that is out of tolerance against the lift car.

Resources

Resource	Description	Unit	Quantity	Rate	Amount
Labour	Mason	hr	14.0	26.0	$ 364.00
Labour	Labourer	hr	14.0	19.0	$ 266.00
Material	Rapid set mortar and screed	bag	12.0	18.4	$ 220.80
Plant	Floor saw	day	1.0	78.0	$ 78.00
Net of labour, plant and material					$ 928.80
Percentage additions					$ 104.73
Total of this sheet					$ 1,033.53

Percentage additions applied: labour 12.5%, plant 5.0%, material 10.0%.

Signature of this sheet records the resources expended and is not an acceptance that the work is a variation or that daywork is the correct basis of valuation.


Signed by Marcus Ellis on 10/12/2026 (Signed on site, sheet DW/HC/004)

Signed for the Contractor

Signed for the Employer

ENTERPRISE Print, Daywork Sheet, ready for the client's signature.

12.4 Provisional sums ENTERPRISE

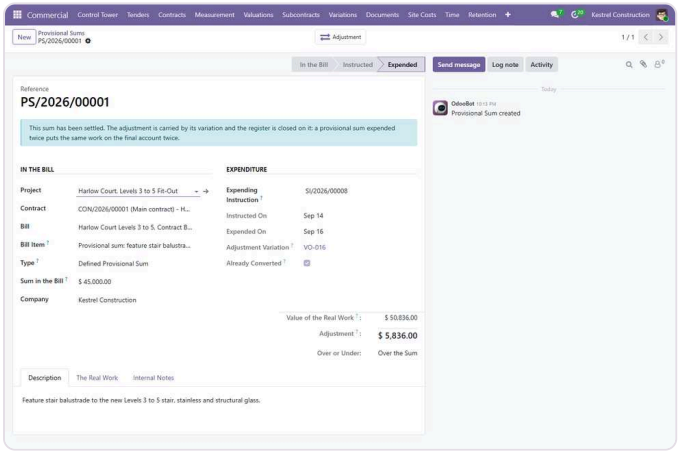

8 ENTERPRISE

A provisional sum, expended

A sum in the bill for work not yet defined: defined, undefined or prime cost. **Record Instruction** when the architect says what it is for; price the real work on its lines; **Expend the Sum** converts it in one step, raising the adjustment variation for the difference. **Omit in Full** takes the whole sum off.

12.5 Valuation methods ENTERPRISE

Commercial, Configuration, Valuation Methods: bill rates, pro rata, star rate, daywork, lump sum, and any you add. A method flagged "valued from daywork sheets" expects signed dayworks; one flagged "needs a new rate" expects a star rate to be agreed.

PART 13 Retention and the final account


ENTERPRISE


Retention is a ledger, not a percentage field, and the final account is a statement built from the registers rather than a spreadsheet assembled at the end. Both exist so money held back is money collected.

TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Retention, Retention Ledger and group by contract
2. Open Nobody Chased This
3. Open Final Account, Everything Holding a Job Open

13.1 The retention ledger ENTERPRISE

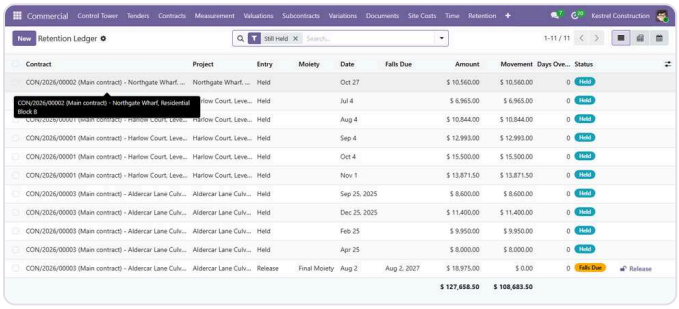



1 ENTERPRISE

Every movement of retention


Commercial, Retention, Retention Ledger. Each issued certificate writes a dated "held" row, capped at the contract limit. Practical completion and the end of the defects period write the two release rows with their due dates and their share of what was actually held. Kanban, list, pivot and calendar.

A release cannot exist without a due date.

2 ENTERPRISE

Nobody Chased This

Releases that fell due and have not been paid, with days overdue and the number of times chased. A daily job raises each moiety as it falls due and then chases it.



3 ENTERPRISE


Snags Holding Retention

A snag can be ticked **Holds Retention**. While it is open, retention on that contract cannot be released, and this list shows exactly which defects stand between you and the money.

Ledger button	What it does
Confirm	A draft row becomes held.
Release	The money came back: records it and tells the contract.
Cancel	Row raised in error.

13.2 The final account ENTERPRISE


Commercial, Final Account, Final Accounts. One statement per contract, drawn at a date. The project's Final Account button opens it, raising one on the spot if there is none yet.

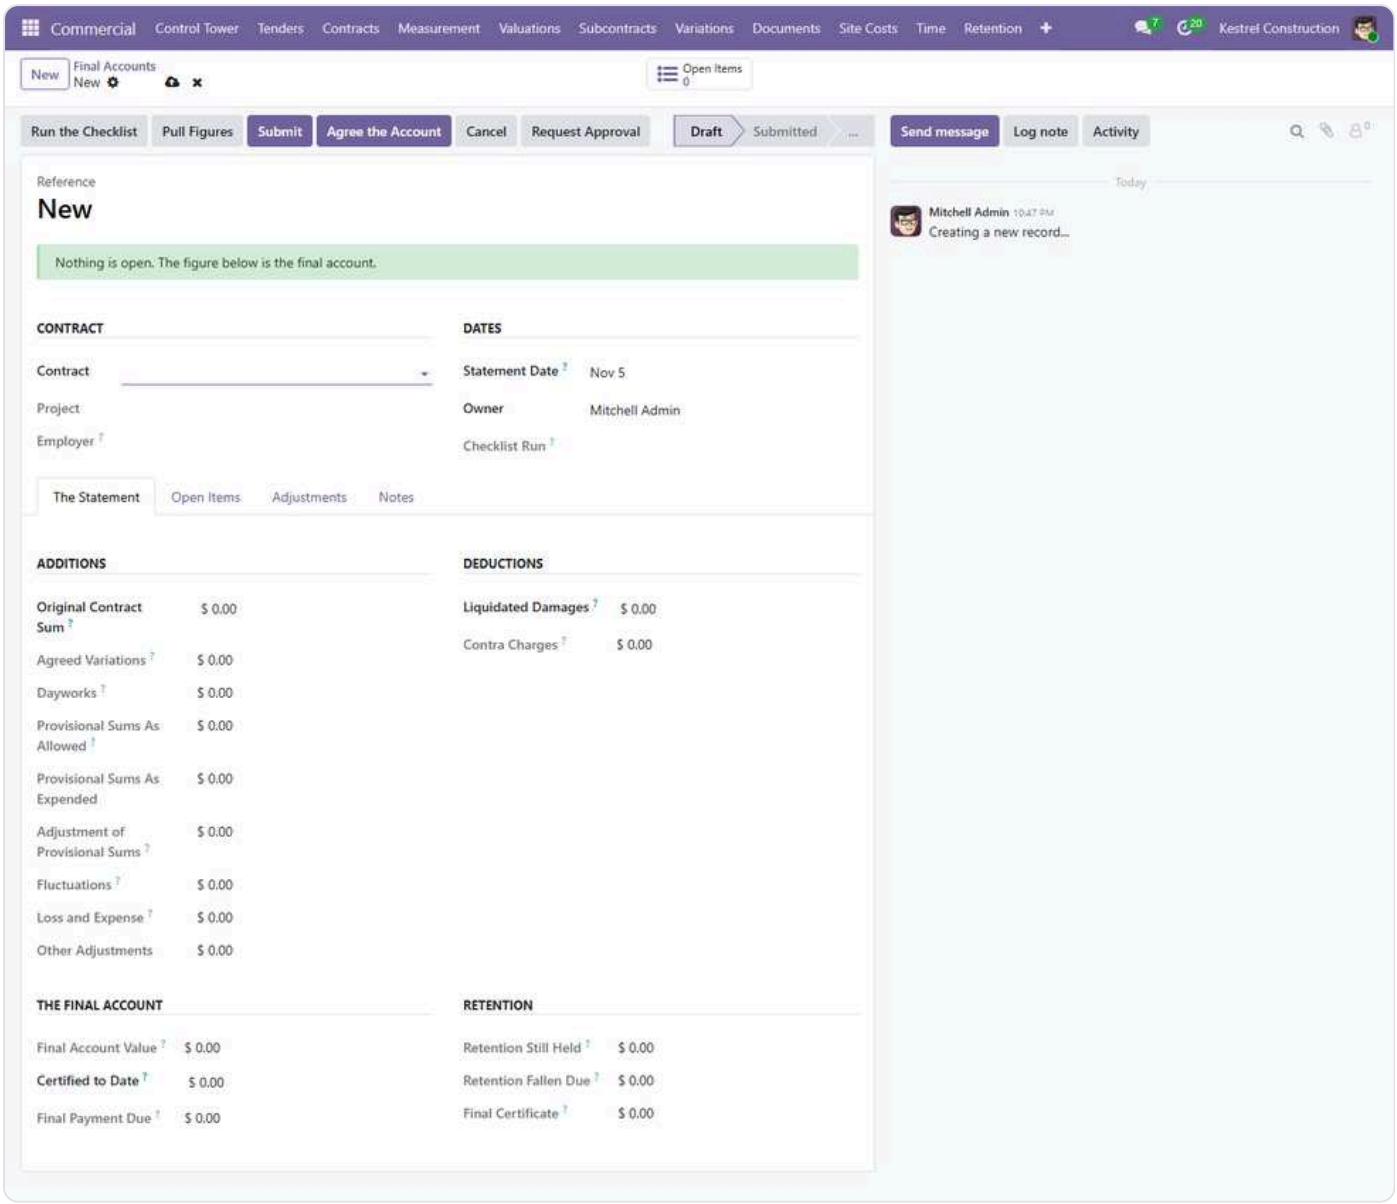

ENTERPRISE A final account form. The figures fill in from the registers once a contract is picked.

Line on the statement	Comes from
Original Contract Sum	The contract.
Agreed Variations	Agreed variations only, never ones still in argument.
Dayworks	Signed daywork sheets not already inside a variation.
Provisional Sums as allowed, as expended, adjustment	The provisional sum register.
Fluctuations, Contra Charges, Other Adjustments	Adjustment lines on the account, each with a reference.
Loss and Expense	Agreed claims only.

Liquidated Damages	Computed at the contract rate from the overrun against the adjusted completion date, up to the cap.
Final Account Value	All of the above.



4 ENTERPRISE

Everything Holding a Job Open

Run the Checklist rebuilds a list of open items from the records as they stand: unagreed variations, unsigned dayworks, unexpended provisional sums, open claims, unissued certificates, unreleased retention, open snags. Each has a value at risk and opens the record.


5 ENTERPRISE


Submit, agree, final certificate

Pull Figures re-reads the figures a surveyor may overwrite. **Submit**, **Agree the Account** (through the approval chain when one applies) and **Issue Final Certificate**, which also releases the retention it frees.

Overwriting a pulled figure needs a reason, so the account can be defended line by line.

13.3 Loss and expense ENTERPRISE

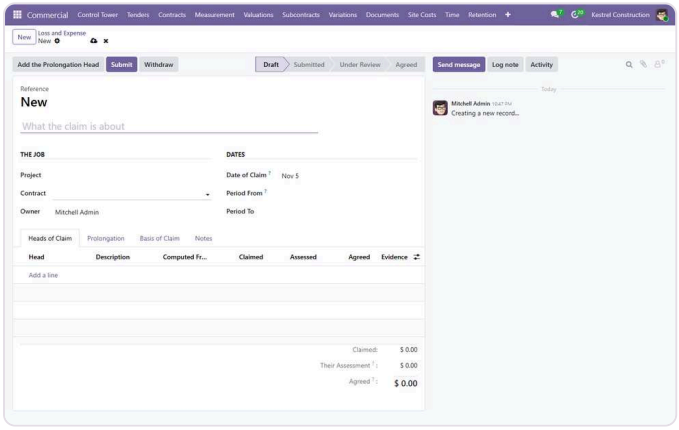



6 ENTERPRISE

A loss and expense claim

Commercial, Final Account, Loss and Expense. Subject, period, the extension of time claim it runs alongside, days claimed and awarded, and the basis. Heads of claim (prolongation, disruption, finance charges and others) each carry claimed, assessed and agreed amounts with their own evidence.

Add the Prolongation Head prices prolongation from the bill items ticked as time-related preliminaries, over the weeks awarded, claimed or stated.

7 ENTERPRISE

Claimed against agreed

Reporting, Claimed Against Agreed: a pivot by head, because claims are settled head by head ("we pay the prolongation and none of the disruption").

PART 14 Subcontract management


ENTERPRISE

A package is let against an allowance in the bill, valued monthly at the subcontractor's own rates, certified with retention and contra charges, and billed. The Base subcontract stays the order; Enterprise wraps the commercial process round it.

TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Subcontracts, Packages and sort by buying gain
2. Open a package and compare quoted with levelled
3. Open a certified subcontract valuation and read net payable


14.1 Packages and levelled quotes ENTERPRISE

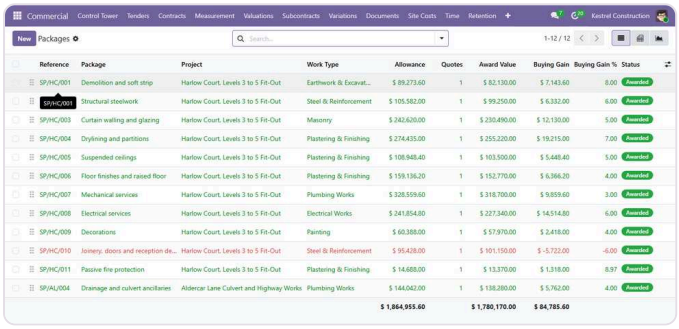

1 ENTERPRISE

Packages

Commercial, Subcontracts, Packages. Scope (and what is excluded), the bill items it covers, the allowance from the bill or typed by hand, enquiry and return dates, the date needed on site, quotes received, lowest levelled quote, award value and the **buying gain**: allowance less award.

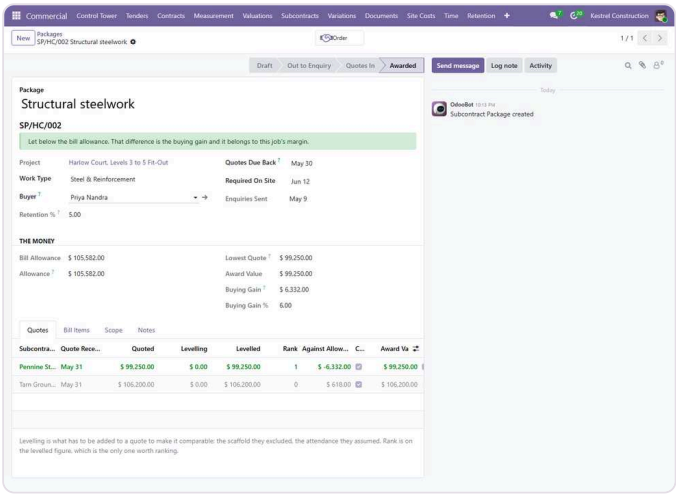

2 ENTERPRISE

Quotes, levelled


Each firm's quote keeps the figure on their letter untouched, plus a **levelling** adjustment for what they excluded and others included. Rank, variance against allowance and against lowest, programme weeks, compliance and the qualifications in their words. Tick the recommended one and **Award**: the subcontract order is created from it.

Comparing unlevelled quotes is how a package goes to the firm with the best exclusions rather than the best price.

14.2 The order, extended ENTERPRISE

The Base subcontract gains the package it came from, the order value at award, confirmed variations and the revised order value, retention limit %, retention held, released and outstanding, certified gross and net, what is left to certify, an over-certified warning, contra charges deducted and pending, and the insurance expiry date and reference. A shipped alert rule chases insurance thirty days before it lapses. Confirming an order runs the budget check and, above a size, the approval chain.


14.3 Subcontract valuations ENTERPRISE

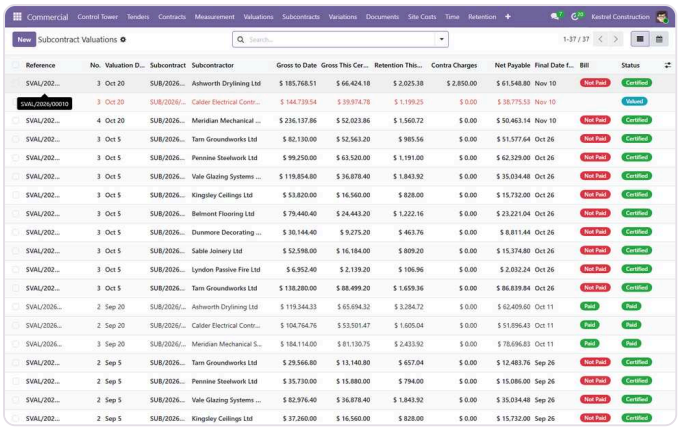

3 ENTERPRISE

Valuations and certificates

Commercial, Subcontracts, Subcontract Valuations. Their application reference and amount, the period, gross to date, previously certified, this certificate, retention, contra charges and net payable.

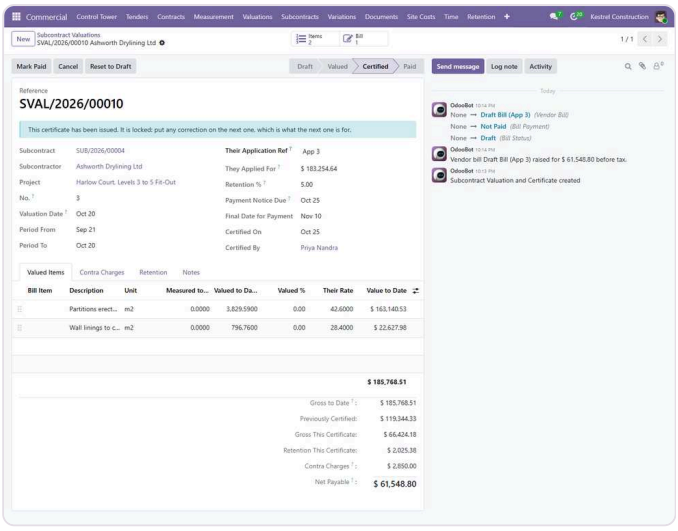


4 ENTERPRISE

A certified valuation

Items are priced at **their rate**, not the bill rate; the gap is your margin on the package. **Value from Measurement** pulls your own measured quantities onto the lines. An item cannot be valued beyond what the book says was built.

Mark Valued, **Certify** (through approval when one applies), **Create Bill**, **Mark Paid**.

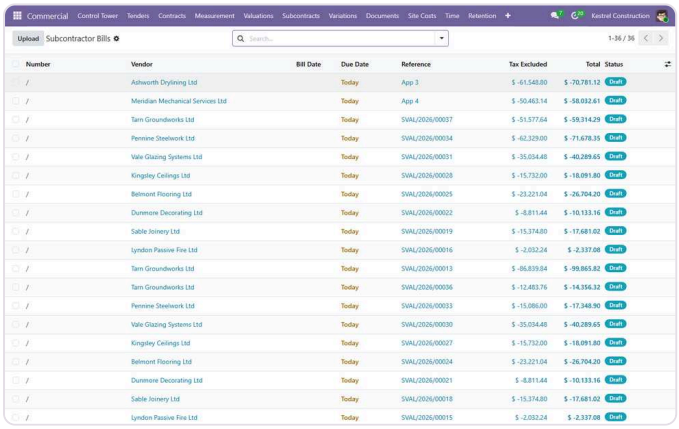


5 ENTERPRISE


Subcontractor bills

Create Bill on a certified valuation raises a draft vendor bill on the subcontract cost account, with retention and each contra charge deducted on their own lines. When the bill is paid, the valuation follows. The order's billed amount (its actual cost) is kept in step by every certified valuation.

14.4 Order variations and contra charges ENTERPRISE

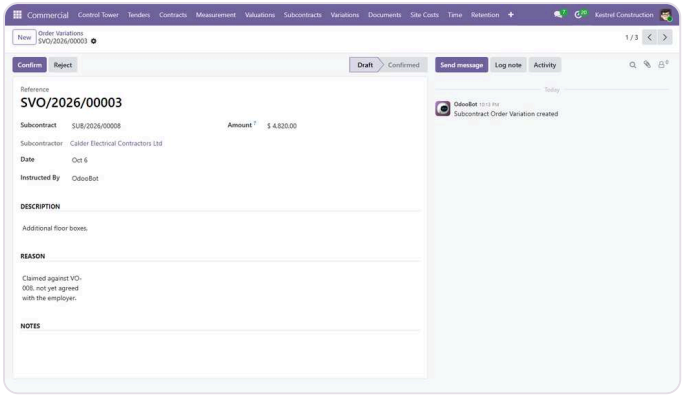

ENTERPRISE **Order Variations**: a change to the order with its reason; an omission is a negative amount. Only a confirmed one moves the revised order value.

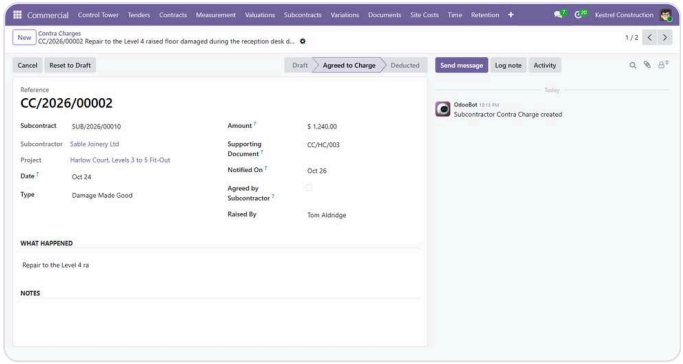

ENTERPRISE **Contra Charges**: attendance, plant, materials supplied, work done by others, damage, cleaning, welfare. Notified date, agreed or not, supporting document; once agreed, the next certificate deducts it.

PART 15 Budget control, CVR and cash flow

ENTERPRISE

Three answers a commercial manager needs every month: is any item going over budget, what is the true margin today, and when does the job run short of cash.


TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Reporting, Lines Over Budget
2. Open the signed CVR on Harlow Court and read the margin
3. Open Commercial, Reporting, Job Cost Sheet, pick a job, and Print PDF

15.1 Budget, committed, actual and remaining

ENTERPRISE


Every bill item carries an **approved budget** (from its cost, or typed by hand), **committed** (approved requisitions not yet issued, open subcontract value, plant hire expected, confirmed purchase orders not yet billed), **actual** (materials issued, labour logged, subcontract certified, plant charged, approved site expenses, posted supplier bills) and **remaining**. Each is also split by resource: materials, labour, subcontract, plant, site expenses.



1 ENTERPRISE

Budget vs Actual

Commercial, Reporting, Budget vs Actual: a pivot of every live bill item, by job and section.



2 ENTERPRISE

Lines Over Budget

Only the items where committed plus actual already exceed the approved budget.

Budget Check setting	When a requisition is approved or a subcontract confirmed over budget
No Check	Nothing happens.
Warn	A warning on the record; it goes through.
Block	Refused, with the item and the overrun.
Require Approval	An approval is raised for a budget overrun sign-off; the document waits until it is signed.


> Once the bill is agreed as the contract, budgets are frozen. **Follow the Estimate Again** on an item lets its budget track the cost again, but only on a bill that is not yet agreed.

15.2 Cost codes

ENTERPRISE

Construction, Configuration, Cost Codes. Codes nest: Substructure, then Piling under it. A heading carries no money; it totals its children. Each code reports into one cost type. Bill items, packages, plant hire, accruals and petty cash all take a cost code, which is how the CVR reports cost by code.


15.3 The cost value reconciliation ENTERPRISE



3 ENTERPRISE

Reconciliations

Commercial, Cost Value Reconciliation, Reconciliations. One per contract per period, drawn at the period end.

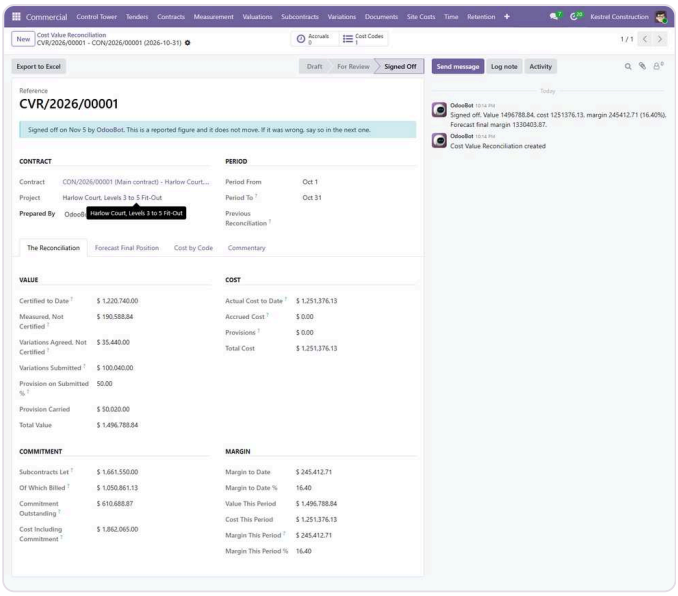


4 ENTERPRISE

A signed CVR

Value: certified to date, measured not certified, variations agreed not certified, variations submitted with a provision %. **Cost**: actual to date, accrued, provisions with what they are for. **Commitment**: subcontracts let. Then margin and margin %, and lines by cost code with budget, actual, accrued, total and variance.


Pull Figures snapshots every source; **Raise Accruals** drafts an accrual for everything delivered or done and not billed; **Sign Off** locks it.



5 ENTERPRISE

Cost by code


Every CVR line in one pivot, so the code that is four percent light stands out.



6 ENTERPRISE

Jobs Losing Money

Reporting, Jobs Losing Money: the reconciliations with a negative margin.

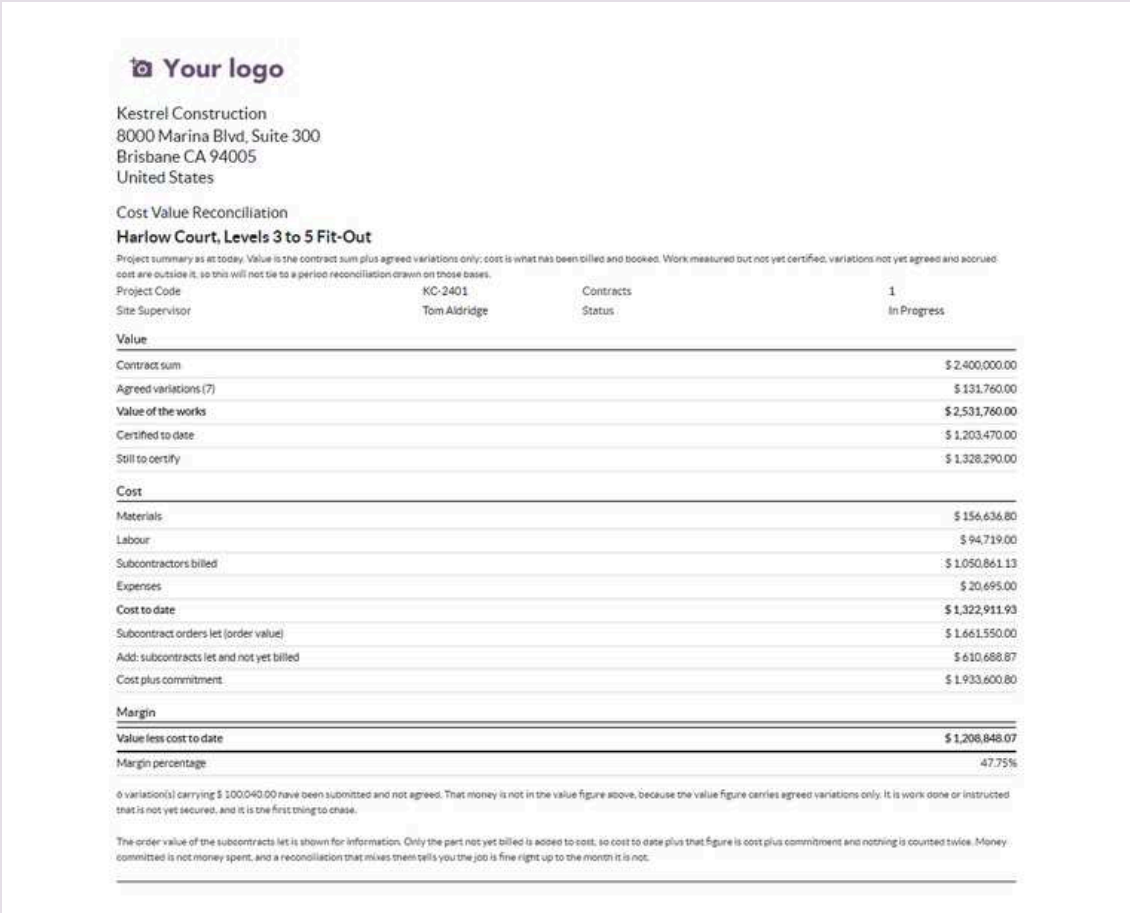

Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Cost Value Reconciliation

Harlow Court, Levels 3 to 5 Fit-Out

Project summary as at today. Value is the contract sum plus agreed variations only; cost is what has been billed and booked. Work measured but not yet certified, variations not yet agreed and accrued cost are outside it, so this will not tie to a period reconciliation drawn on those bases.

Project Code	KC-2401	Contracts	1
Site Supervisor	Tom Aldridge	Status	In Progress

Value	
Contract sum	$ 2,400,000.00
Agreed variations (7)	$ 131,760.00
Value of the works	**$ 2,531,760.00**
Certified to date	$ 1,203,470.00
Still to certify	$ 1,328,290.00

Cost	
Materials	$ 156,636.80
Labour	$ 94,719.00
Subcontractors billed	$ 1,050,861.13
Expenses	$ 20,695.00
Cost to date	**$ 1,322,911.93**
Subcontract orders let (order value)	$ 1,661,550.00
Add: subcontracts let and not yet billed	$ 610,688.87
Cost plus commitment	$ 1,933,600.80


Margin	
Value less cost to date	**$ 1,208,848.07**
Margin percentage	47.75%


6 variation(s) carrying $ 100,040.00 have been submitted and not agreed. That money is not in the value figure above, because the value figure carries agreed variations only. It is work done or instructed that is not yet secured, and it is the first thing to chase.

The order value of the subcontracts let is shown for information. Only the part not yet billed is added to cost, so cost to date plus that figure is cost plus commitment and nothing is counted twice. Money committed is not money spent, and a reconciliation that mixes them tells you the job is fine right up to the month it is not.

ENTERPRISE Print, Cost Value Reconciliation. Export to Excel gives the same.

15.4 Accruals ENTERPRISE





7 ENTERPRISE

Accruals


Cost incurred and not yet invoiced, on one of three bases: goods received not invoiced, work measured not invoiced, or a manual estimate, which needs a reason. Each has an accrued-at date and reverses on the first day of the next period. **Post**, **Reverse Now**, **Cancel**.

8 ENTERPRISE

Accruals to Reverse

Accruals whose source document has since been invoiced, so the real cost is in the ledger. A daily job reverses what has fallen due and chases what has been overtaken.

15.5 Cash flow forecast ENTERPRISE

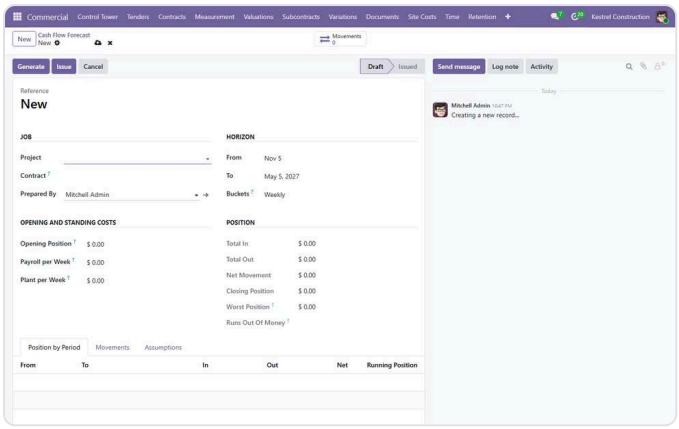


9 ENTERPRISE

A forecast

Commercial, Cost Value Reconciliation, Cash Flow Forecast. Pick the job, the dates, weekly or monthly buckets, the opening position, payroll per week and plant per week. **Generate** builds dated movements in and out (certificates by their final date for payment, retention releases, subcontract payments, payroll, plant) and the running position per period.

The forecast shows the closing position, the worst position and the date the job runs out of money if it does.




10 ENTERPRISE

Cash Movements

Every movement of every forecast in a pivot. Movements typed by hand survive a regenerate.

15.6 The Job Cost Sheet ENTERPRISE



11 ENTERPRISE

Print the Job Cost Sheet

Commercial, Reporting, Job Cost Sheet. Pick one or several jobs and an as-at date. **Print PDF** gives one sheet per job in one file; **Export to Excel** gives the same as a spreadsheet.

Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Job Cost Sheet

Harlow Court, Levels 3 to 5 Fit-Out

Figures as at 2026-11-05. Budget, committed and actual are today's live position: nothing in the budget layer carries a date to draw them at a past one. Certified to date and the adjusted sum are drawn as at the date above.

Job	Harlow Court, Levels 3 to 5 Fit-Out	Client	Harlow Estates Ltd
Contract Sum	$ 2,400,000.00	Adjusted Sum (with agreed variations)	$ 2,531,760.00
Certified to Date	$ 1,220,740.00	Progress	48.2%

A.1 Management and staff

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Preliminaries	$ 122,792.00	$ 0.00	$ 6,390.00	$ 116,402.00	$ 122,792.00	$ 0.00	5.2%
Section total	$ 122,792.00	$ 0.00	$ 6,390.00	$ 116,402.00	$ 122,792.00	$ 0.00	

A.2 Site establishment

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Preliminaries	$ 35,650.00	$ 0.00	$ 10,660.00	$ 24,990.00	$ 35,650.00	$ 0.00	29.9%
Section total	$ 35,650.00	$ 0.00	$ 10,660.00	$ 24,990.00	$ 35,650.00	$ 0.00	

A.3 Temporary works and access

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Plant	$ 34,328.00	$ 0.00	$ 21,898.00	$ 12,430.00	$ 34,328.00	$ 0.00	63.8%
Section total	$ 34,328.00	$ 0.00	$ 21,898.00	$ 12,430.00	$ 34,328.00	$ 0.00	

B.1 Soft strip

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 86,572.00	$ 0.00	$ 82,406.00	$ 4,166.00	$ 86,572.00	$ 0.00	95.2%
Section total	$ 86,572.00	$ 0.00	$ 82,406.00	$ 4,166.00	$ 86,572.00	$ 0.00	

B.2 Structural alterations

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Material	$ 16,487.20	$ 0.00	$ 3,318.00	$ 13,169.20	$ 16,487.20	$ 0.00	20.1%
Section total	$ 16,487.20	$ 0.00	$ 3,318.00	$ 13,169.20	$ 16,487.20	$ 0.00	

C.1 Structural steelwork

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 105,210.00	$ 0.00	$ 99,250.00	$ 5,960.00	$ 105,210.00	$ 0.00	94.3%
Section total	$ 105,210.00	$ 0.00	$ 99,250.00	$ 5,960.00	$ 105,210.00	$ 0.00	

C.2 Floor build-up

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Material	$ 65,200.80	$ 243.20	$ 1,120.80	$ 63,836.80	$ 65,200.80	$ 0.00	2.1%
Section total	$ 65,200.80	$ 243.20	$ 1,120.80	$ 63,836.80	$ 65,200.80	$ 0.00	

D.1 Curtain walling and glazing

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 280,786.00	$ 110,635.20	$ 119,854.80	$ 50,296.00	$ 280,786.00	$ 0.00	82.1%
Section total	$ 280,786.00	$ 110,635.20	$ 119,854.80	$ 50,296.00	$ 280,786.00	$ 0.00	

D.2 Roof and plant screen

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 43,141.20	$ 0.00	$ 0.00	$ 43,141.20	$ 43,141.20	$ 0.00	0.0%
Section total	$ 43,141.20	$ 0.00	$ 0.00	$ 43,141.20	$ 43,141.20	$ 0.00	

E.1 Partitions and linings

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 361,780.00	$ 195,501.09	$ 202,070.91	$ 0.00	$ 397,572.00	$ -35,792.00	109.9%
Section total	$ 361,780.00	$ 195,501.09	$ 202,070.91	$ 0.00	$ 397,572.00	$ -35,792.00	

E.2 Suspended ceilings

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 142,600.00	$ 83,040.00	$ 60,974.00	$ 0.00	$ 144,014.00	$ -1,414.00	101.0%
Section total	$ 142,600.00	$ 83,040.00	$ 60,974.00	$ 0.00	$ 144,014.00	$ -1,414.00	

E.3 Floor finishes

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 186,087.20	$ 73,329.60	$ 79,440.40	$ 33,317.20	$ 186,087.20	$ 0.00	82.1%
Section total	$ 186,087.20	$ 73,329.60	$ 79,440.40	$ 33,317.20	$ 186,087.20	$ 0.00	

E.4 Joinery and doors

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Material	$ 141,861.20	$ 48,552.00	$ 52,598.00	$ 40,711.20	$ 141,861.20	$ 0.00	71.3%
Section total	$ 141,861.20	$ 48,552.00	$ 52,598.00	$ 40,711.20	$ 141,861.20	$ 0.00	

E.5 Decorations

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Labour	$ 78,256.00	$ 27,825.60	$ 30,144.40	$ 20,286.00	$ 78,256.00	$ 0.00	74.1%
Section total	$ 78,256.00	$ 27,825.60	$ 30,144.40	$ 20,286.00	$ 78,256.00	$ 0.00	


E.6 Mechanical services

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 368,443.00	$ 93,752.14	$ 236,137.86	$ 38,553.00	$ 368,443.00	$ 0.00	89.5%
Section total	$ 368,443.00	$ 93,752.14	$ 236,137.86	$ 38,553.00	$ 368,443.00	$ 0.00	

E.7 Electrical services

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 267,067.60	$ 122,575.24	$ 104,764.76	$ 39,727.60	$ 267,067.60	$ 0.00	85.1%
Section total	$ 267,067.60	$ 122,575.24	$ 104,764.76	$ 39,727.60	$ 267,067.60	$ 0.00	

E.8 Sanitaryware and above ground drainage

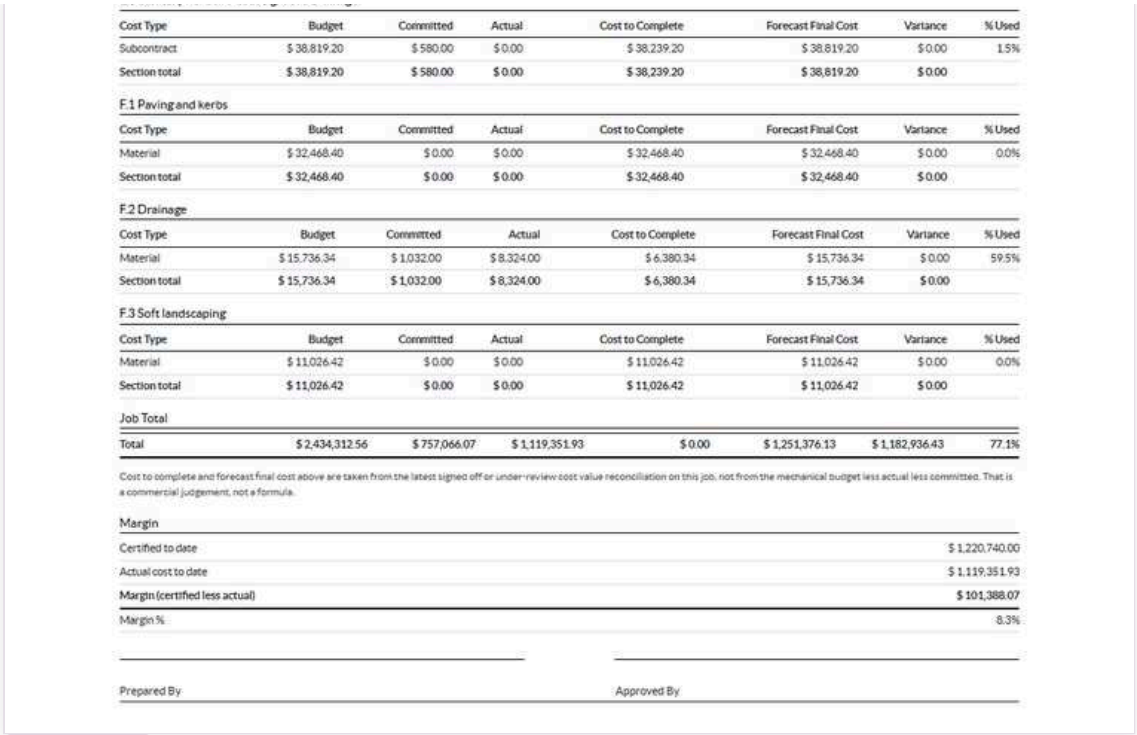

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Subcontract	$ 38,819.20	$ 580.00	$ 0.00	$ 38,239.20	$ 38,819.20	$ 0.00	1.5%
Section total	$ 38,819.20	$ 580.00	$ 0.00	$ 38,239.20	$ 38,819.20	$ 0.00	

F.1 Paving and kerbs

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Material	$ 32,468.40	$ 0.00	$ 0.00	$ 32,468.40	$ 32,468.40	$ 0.00	0.0%
Section total	$ 32,468.40	$ 0.00	$ 0.00	$ 32,468.40	$ 32,468.40	$ 0.00	

F.2 Drainage

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Material	$ 15,736.34	$ 1,032.00	$ 8,324.00	$ 6,380.34	$ 15,736.34	$ 0.00	59.5%
Section total	$ 15,736.34	$ 1,032.00	$ 8,324.00	$ 6,380.34	$ 15,736.34	$ 0.00	

F.3 Soft landscaping

Cost Type	Budget	Committed	Actual	Cost to Complete	Forecast Final Cost	Variance	% Used
Material	$ 11,026.42	$ 0.00	$ 0.00	$ 11,026.42	$ 11,026.42	$ 0.00	0.0%
Section total	$ 11,026.42	$ 0.00	$ 0.00	$ 11,026.42	$ 11,026.42	$ 0.00	

Job Total

Total	$ 2,434,312.56	$ 757,066.07	$ 1,119,351.93	$ 0.00	$ 1,251,376.13	$ 1,182,936.43	77.1%

Cost to complete and forecast final cost above are taken from the latest signed off or under-review cost value reconciliation on this job, not from the mechanical budget less actual less committed. That is a commercial judgement, not a formula.

Margin

Certified to date	$ 1,220,740.00
Actual cost to date	$ 1,119,351.93
Margin (certified less actual)	$ 101,388.07
Margin %	8.3%

Prepared By

Approved By

ENTERPRISE The Job Cost Sheet: by section and cost type, budget against committed and actual, with the contract position on top.

PART 16 Procurement and site stores

ENTERPRISE

An approved requisition goes out for prices, the quotes are compared side by side, the award raises the purchase order in Odoo Purchase, delivery is checked on a goods received note, and the supplier's bill is matched against both. With the inventory flow on, every job has a store of its own.


TRY IT YOURSELF ON THE DEMO

1. Open Construction, Procurement, Requests for Quotation and open one in Quotes In
2. Read the comparison grid and the lowest price per line
3. Open Procurement, Bills to Review

From requisition to paid bill ENTERPRISE

1. **Requisition** — Approved on site
2. **RFQ** — Several vendors asked
3. **Compare** — Lowest compliant per line
4. **Order** — Purchase order raised
5. **Receive** — GRN, accepted and rejected
6. **Match** — Bill against order and GRN


16.1 Requests for quotation ENTERPRISE

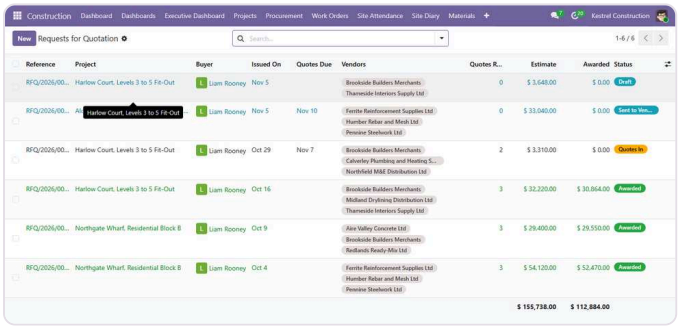

1 ENTERPRISE

Requests for quotation

Construction, Procurement, Requests for Quotation. Pick approved requisitions on one project and **Request Quotes**: one request with their open lines, the vendors to ask, a quotes-due date, and a quote opened for each vendor if you send it now.

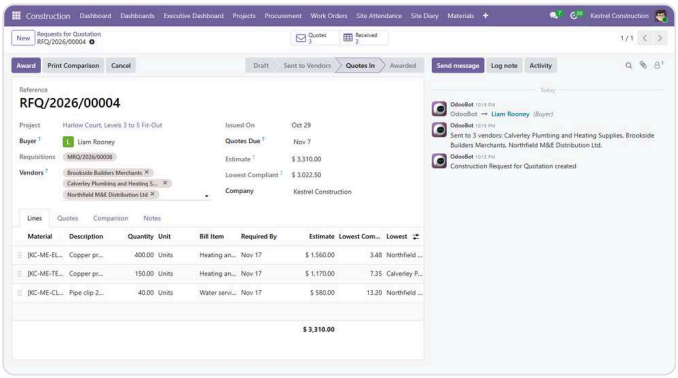


2 ENTERPRISE

A request with its quotes

Lines down the side, vendors across the top, the lowest compliant price per line marked. Each quote records the vendor's reference, received date, validity, payment terms, technical compliance and lead time per line. **Send to Vendors**, **Quotes In**, then **Award**.

A vendor that did not price a line leaves it at zero; it is not counted as cheapest.

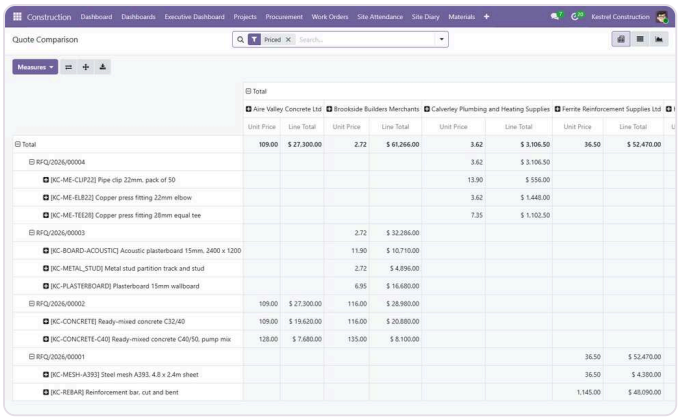

3 ENTERPRISE

Quote comparison

Procurement, Quote Comparison: every quoted price in a pivot, line against vendor.

The award dialog offers the whole request to one vendor (only a compliant quote that priced every line qualifies) or a split by line. If the award does not go to the cheapest compliant price, a justification is required. **Award and Raise Orders** creates one purchase order per vendor, each line linked to its requisition line and bill item.

Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Quote Comparison
RFQ/2026/00004


Project	Harlow Court, Levels 3 to 5 Fit-Out	Buyer	Liam Rooney
Issued	10/29/2026	Quotes Due	11/07/2026
Estimate	$ 3,310.00	Lowest Compliant	$ 3,022.50

Unit price, then line total and lead time. The lowest compliant price on each line is shaded; a non-compliant offer is struck through; the awarded price is boxed.

Item	Qty	Northfield M&E Distribution Ltd	Calverley Plumbing and Heating Supplies	Brookside Builders Merchants awaiting
[KC-ME-ELB22] Copper press fitting 22mm elbow E.6.E6.030 Heating and chilled water pipework	400.00 Units	**$ 3.48** **$ 1,392.00, 8 days**	$ 3.62 $ 1,448.00, 3 days	-
[KC-ME-TEE28] Copper press fitting 28mm equal tee E.6.E6.030 Heating and chilled water pipework	150.00 Units	$ 7.60 $ 1,140.00, 8 days	**$ 7.35** **$ 1,102.50, 3 days**	-
[KC-ME-CLIP22] Pipe clip 22mm, pack of 50 E.8.E8.040 Water services and boosted cold supply	40.00 Units	**$ 13.20** **$ 528.00, 8 days**	$ 13.90 $ 556.00, 3 days	-
Total		$ 3,060.00	$ 3,106.50	-
Lines quoted		3 / 3	3 / 3	-
Longest lead time		8 days	3 days	-
Valid until		2026-12-01	2026-12-01	-
Payment terms		30 Days	30 Days	-
Technically compliant		Yes	Yes	Yes

ENTERPRISE Print, Quote Comparison: the table a buyer signs before placing the order.


16.2 Purchase orders, goods received and the three-way match ENTERPRISE



4 ENTERPRISE

Construction purchase orders

Procurement, Purchase Orders: standard Odoo purchase orders that carry a construction project and, per line, a bill item. Confirming one runs the budget check against its bill items and uses the standard Purchase approval limit. Confirmed value not yet billed is committed cost on the item.

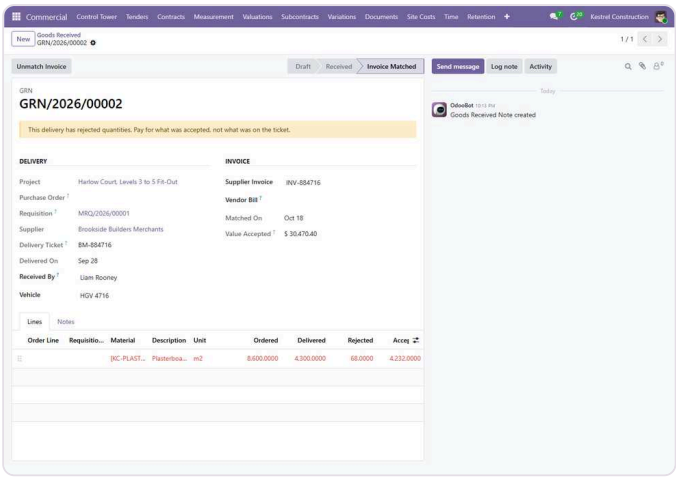

5 ENTERPRISE

A goods received note

Requisition or order, supplier, delivery ticket, date, who received it, vehicle. Each line: ordered, delivered, rejected with a reason, accepted, over or short, unit cost and the batch or mill certificate number. **Confirm Receipt**, then **Match Invoice** once the supplier's bill is in.

Receive Goods on a requisition or order raises a GRN with everything still to come.




6 ENTERPRISE

Bills to Review

A posted vendor bill for a construction order is checked line by line against what was ordered and what was received. Each line is matched, over billed or not received, and the bill takes the worst. Bills outside the tolerance in Settings land here until someone presses **Mark Match Reviewed**.

16.3 Site stores and the inventory flow ENTERPRISE


With Settings, Material Flow set to **Inventory**, each job gets a site store (**Create Site Store** on the project). An approved requisition becomes a transfer from the central store; issuing it sends the transfer. Purchase orders can be received straight to site. Material is charged to the job when it is issued to the work, at its stock value, rather than when the requisition is approved.



7 ENTERPRISE

Site Stores


What is on each site: quantity, reserved, free to issue, and its value at today's cost.



8 ENTERPRISE

Site Transfers


The Inventory transfers into and out of the site stores, each tied to its project and requisition.

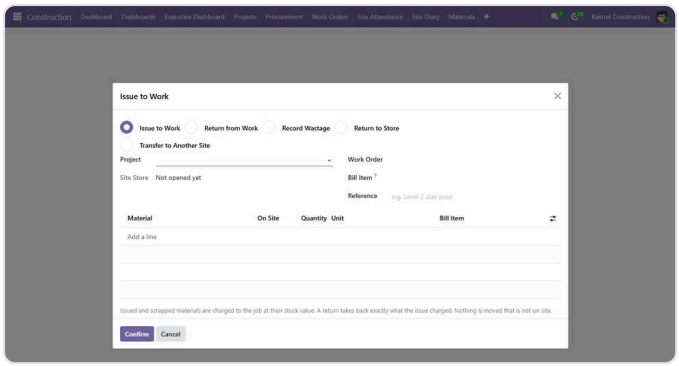

9 ENTERPRISE

Issue to Work

One dialog for five movements: issue to work, return from work, record wastage (with a reason), return to store, transfer to another site. Lines show what is free to issue on site. A bill item and a work order can be set for every line at once.




10 ENTERPRISE

Consumption Analysis

Every issue, return and scrap, with the cost to the job, by project, bill item, work order or material.

16.4 Material reconciliation ENTERPRISE

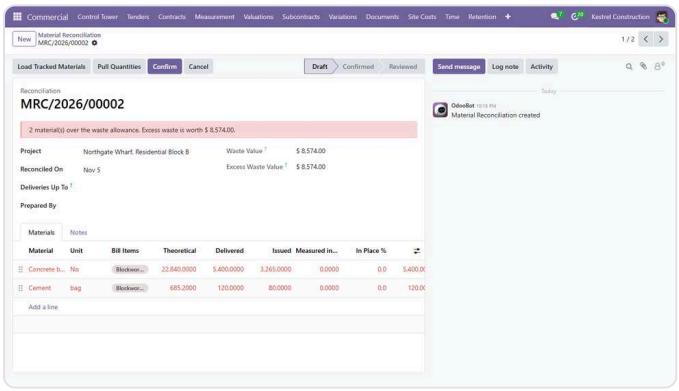


11 ENTERPRISE

Delivered against built

Commercial, Site Costs, Material Reconciliation. For each tracked material: theoretical (bill quantity times usage factor), delivered, issued, measured in place, still in store, waste and waste %, against the allowed waste. Lines over the allowance are flagged and the excess waste is priced. **Load Tracked Materials**, **Pull Quantities**, **Confirm**, **Mark Reviewed**.


Tracked materials and their allowed waste are set in Commercial, Configuration, Tracked Materials.



12 ENTERPRISE

Waste by Material

Every reconciliation line in one pivot.

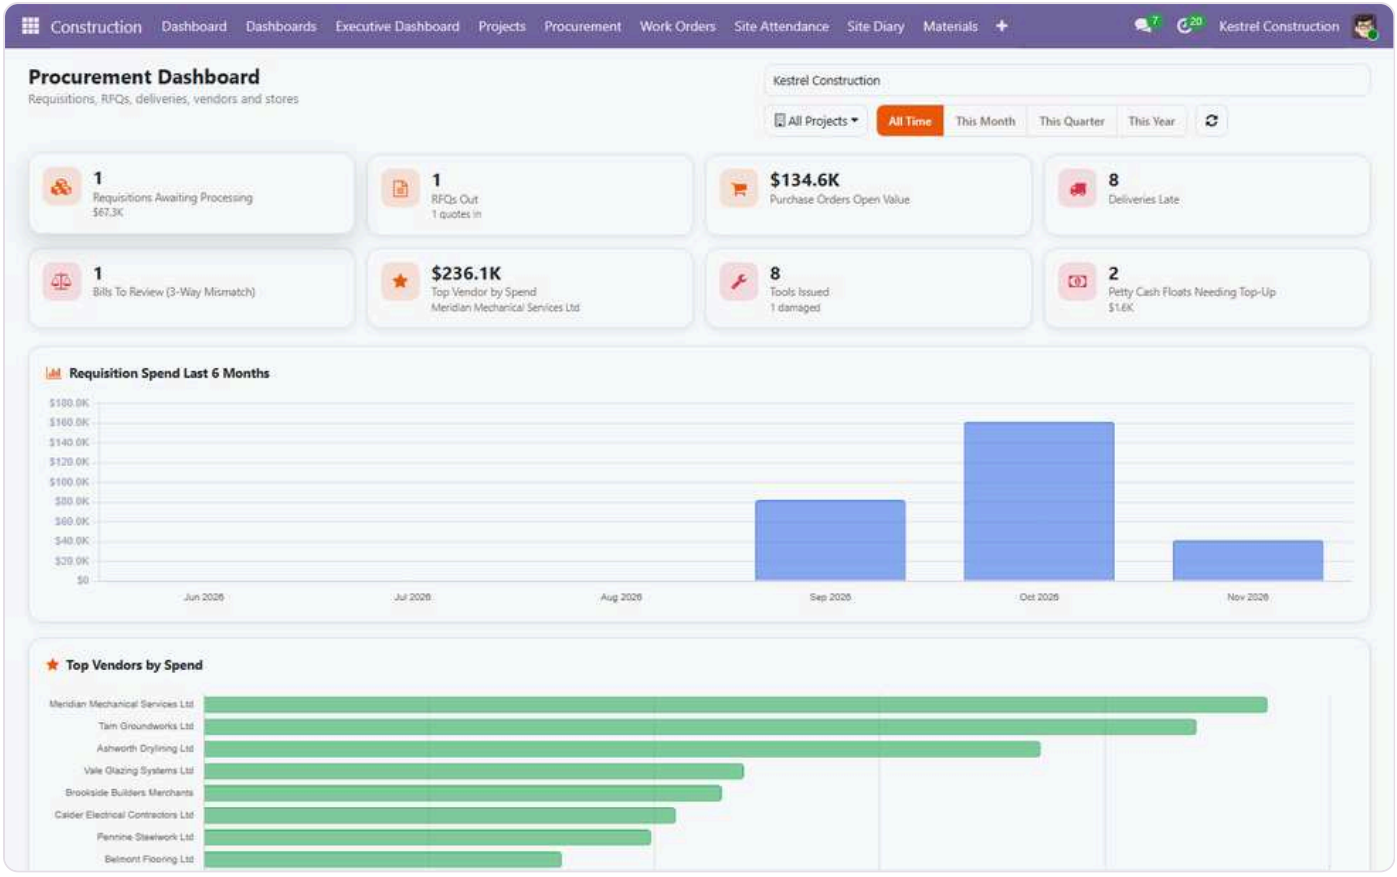

ENTERPRISE Dashboards, Procurement: requisitions waiting, quotes due, orders to receive, bills to review and site stock value.

PART 17 Work orders, job sheets, gangs and manpower


ENTERPRISE

The bill says what to build; a work order hands part of it to a gang or a subcontractor, job sheets report the daily progress, and gangs make labour cost land on the item it built.

TRY IT YOURSELF ON THE DEMO

1. Open Work Orders, Work Orders and open one in progress
2. Open its Job Sheets button
3. Open Commercial, Site Costs, Gangs and look at productivity %


17.1 Work orders ENTERPRISE

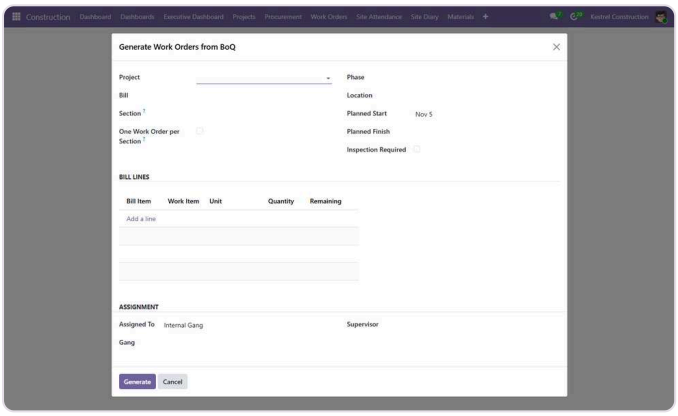

1 ENTERPRISE

Generate work orders from the bill


Work Orders, Generate Work Orders from BoQ. Pick the job and bill, then a section (all its lines come in) or single lines. One work order per section, or one for all. Set phase, location, internal gang or subcontractor, supervisor, dates and whether an inspection is required.



2 ENTERPRISE

The work order board

Work Orders, Work Orders: kanban, list, calendar, pivot. Planned and done quantity and progress %. Work Orders, Delayed Work Orders lists those past their planned finish and not done.

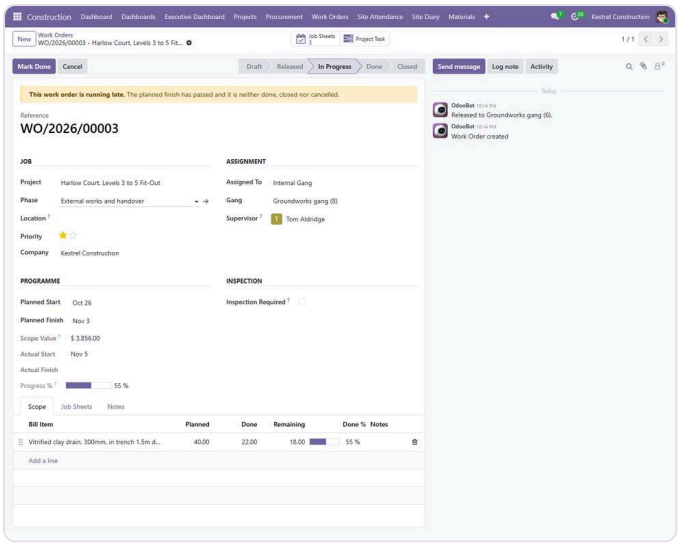

3 ENTERPRISE

A work order

Scope lines name bill items with the planned quantity; done quantity comes only from approved job sheets. **Release** hands it to the gang or subcontractor and creates a project task; **Start**; **Mark Done** raises the inspection when one is wanted; **Close** only once every claimed quantity is measured.

A work order above a size goes through the approval chain before it can be released.



Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Work Order
WO/2026/00003

Project	Harlow Court, Levels 3 to 5 Fit-Out	Location	
Assigned To	Groundworks gang (8)	Supervisor	Tom Aldridge
Planned Start	10/26/2026	Planned Finish	11/03/2026

Scope of Work

Bill Item	Planned Qty	Done Qty	Unit
F.2.F2.010 Vitrified clay drain, 300mm, in trench 1.5m deep	40.0000	22.0000	m

Notes: Running behind the wet week; chase daily.


Issued by, on behalf of the company

Received by (foreman / subcontractor)

This job card records the scope and dates handed over. It is not a certificate of quantity; the measurement book is.

ENTERPRISE Print, Work Order Job Card for the gang.

17.2 Job sheets ENTERPRISE

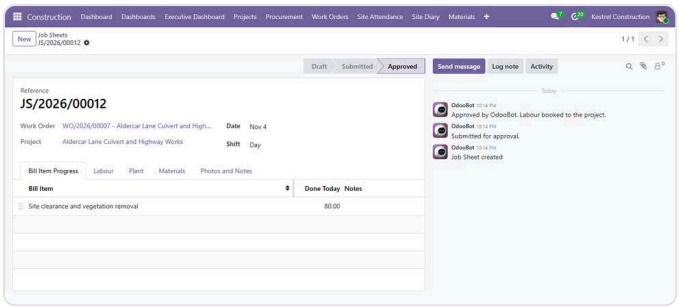


4 ENTERPRISE

A day on a work order

Date and shift (day or night), then four tabs: bill item progress (quantity done today on the work order's items only), labour by trade with headcount and hours, plant with hours, materials used. Photos attach as evidence.

Submit, then **Approve**: the labour is booked as allocations and labour logs, the done quantity moves, and the sheet locks.

17.3 Manpower requests ENTERPRISE

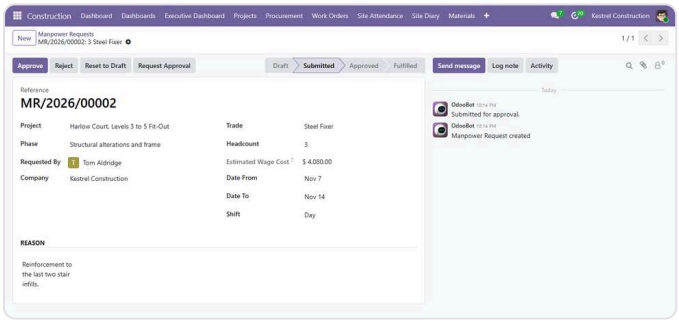


5 ENTERPRISE

Ask the office for people

Project, phase, trade, headcount, from and to dates, shift and the reason. The estimated wage cost is headcount times days times the trade's rate. **Submit**, **Approve** or **Reject** with a reason, then **Mark Fulfilled** with the gang that answered it.

17.4 Gangs and labour allocation ENTERPRISE

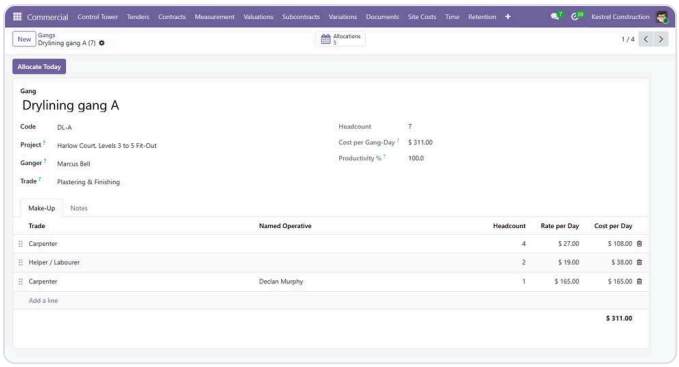


6 ENTERPRISE

A gang

Commercial, Site Costs, Gangs. Ganger, trade, project (or none for a gang that moves), and the make-up: trade, headcount or a named operative, rate per day. Cost per gang-day and productivity % across confirmed allocations.


Allocate Today drafts one allocation per gang for today on its last bill item.



8 ENTERPRISE

Gangs Below Norm

Allocations under the norm. A daily job raises one activity per gang running below norm over the last week.

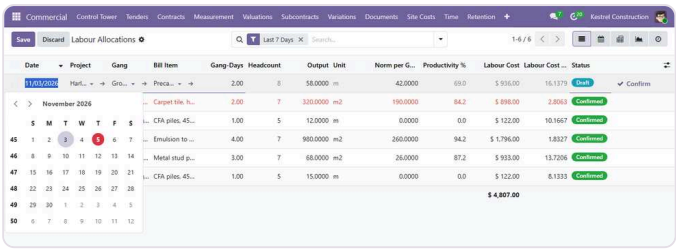

7 ENTERPRISE

An allocation

Gang, bill item, date, gang-days (1.0 is the whole gang for a day), output in the bill unit and the norm per gang-day from the item. Productivity %, below norm, and labour cost per unit built. **Confirm** writes the base labour logs once; **Copy to Tomorrow** drafts the same gang on the same item.

PART 18


Programme, schedule, delays and extension of time

ENTERPRISE

A delay claim is won or lost on what was written down at the time. The programme gives the critical path; delay events carry the notice clock; the extension of time claim gathers the evidence in one click.

TRY IT YOURSELF ON THE DEMO


1. Open Commercial, Time, Programmes and open the baseline
2. Open Commercial, Time, Schedule (Gantt)
3. Open Commercial, Time, Extension of Time Claims and open the awarded one

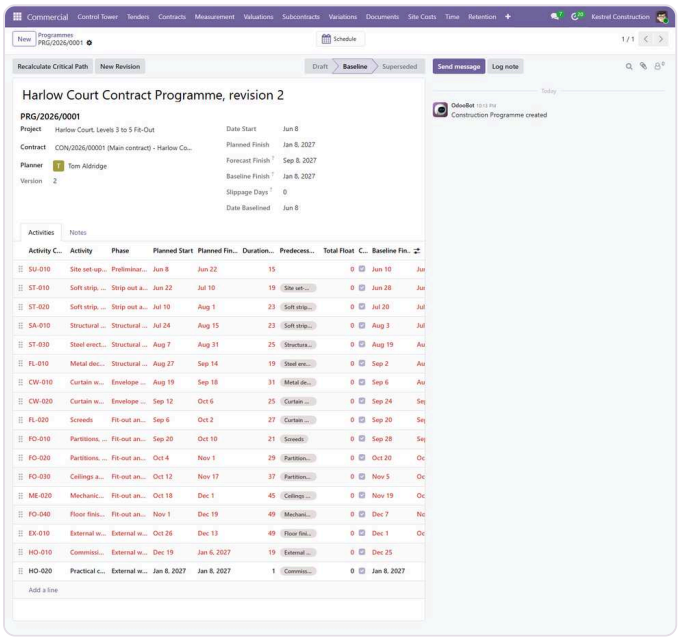

1 ENTERPRISE

A programme


Commercial, Time, Programmes. Activities with codes, phase, planned dates, predecessors and lag. **Recalculate Critical Path** works out early and late dates, float and the critical activities. **Freeze as Baseline** keeps the dates; **New Revision** carries the baseline so slippage shows against it.

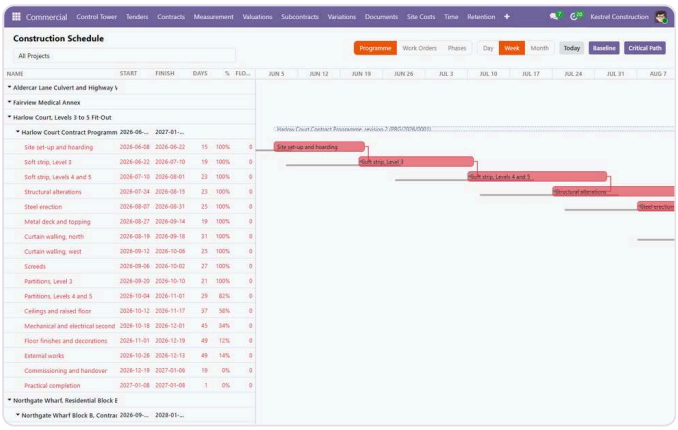

2 ENTERPRISE

The schedule (Gantt)

Commercial, Time, Schedule, or Work Orders, Schedule. Programme activities, work orders and phases on one chart, with dependencies, the critical path, the baseline bars, and drag to reschedule.




3 ENTERPRISE

Delay events

Site Diary, Delays and Stoppages, or Commercial, Time, Delay Events. Cause (from the library, with its entitlement and whose risk it is), what happened, dates, calendar and working days, activities affected and whether one is critical, and the notice due date.

A daily job chases the notice before the deadline, never after. Reporting, Delay Notices Due lists them.

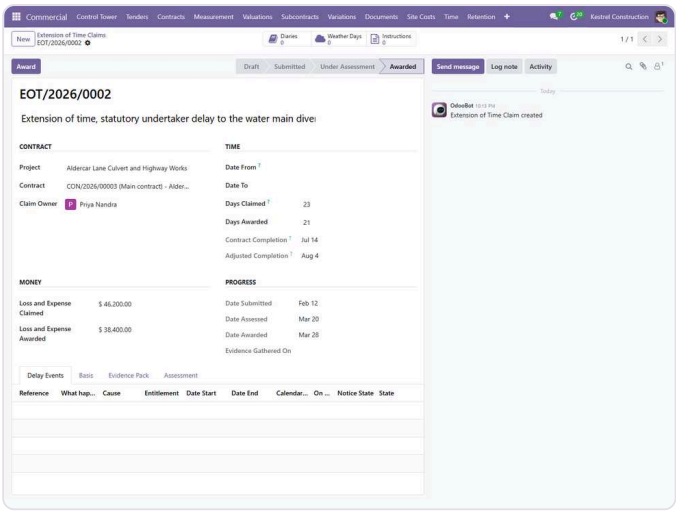

4 ENTERPRISE

An extension of time claim

Assemble EOT Claim on selected delay events opens one claim. **Gather Evidence Pack** pulls every site diary, weather record and instruction inside the claim window. **Submit**, **Under Assessment**, then **Award**: awarded days move the contract's adjusted completion date, and with it the liquidated damages.

Library	Where	Used for
Delay Causes	Commercial, Configuration	Each cause with its usual entitlement (time, time and money, none), whose risk it is and the default notice period.
Adverse Weather Criteria	Commercial, Configuration	Rain, wind, frost and heat thresholds that make a day exceptionally adverse. A contract can have its own.

PART 19 Site diary, weather and attendance

ENTERPRISE

The diary is the site's daily record, signed off by the person who was there. Attendance comes from a phone page tested against the site's geofence, or a supervisor's roll call for crews without phones.

TRY IT YOURSELF ON THE DEMO

1. Open Site Diary, Site Diaries and open a posted day
2. Read the manpower and plant tabs
3. Open Site Attendance, Exceptions


19.1 The site diary ENTERPRISE



1 ENTERPRISE

Site diaries

Site Diary, Site Diaries. One per site per day. Site Diary, Today opens today's diary on your default site, creating it if there is none. **Copy Yesterday** prefills from the last diary on the site.

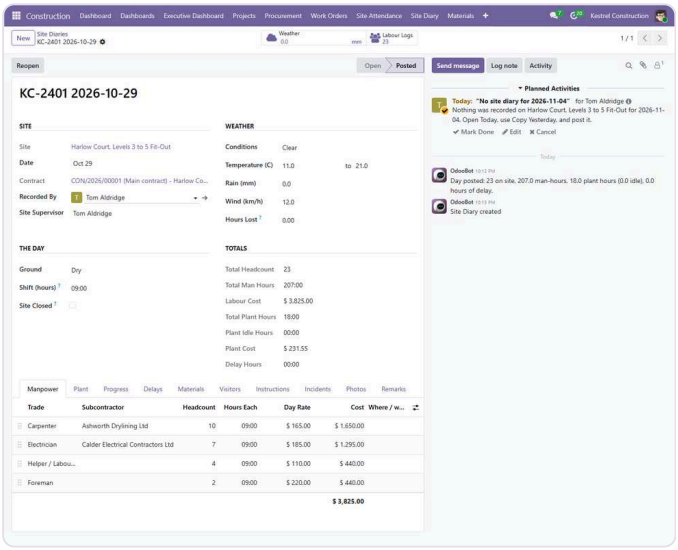


2 ENTERPRISE

A posted diary


Weather, ground conditions, shift length, and tabs for manpower (own and subcontract, by trade), plant (worked and idle hours with a reason), progress against programme activities, delays and stoppages, materials received, visitors (inducted or not), instructions received and incidents. Totals: headcount, man-hours, labour cost, plant hours and idle hours.

Post Day locks it and writes the labour logs and linked delay events. **Reopen** is commercial only, and logged.

An instruction noted in the diary can be raised as a formal site instruction with a confirmation clock from its line. A daily job chases yesterday's diary if it is still open or was never started. Site Diary, Manpower Histogram and Plant Utilisation chart the diary lines.

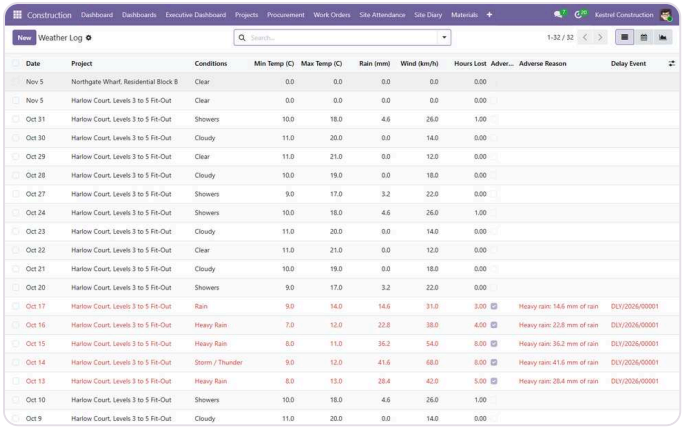


ENTERPRISE **Weather Log**: temperature, rain, wind, hours lost, and whether the day breaches the adverse weather criteria.

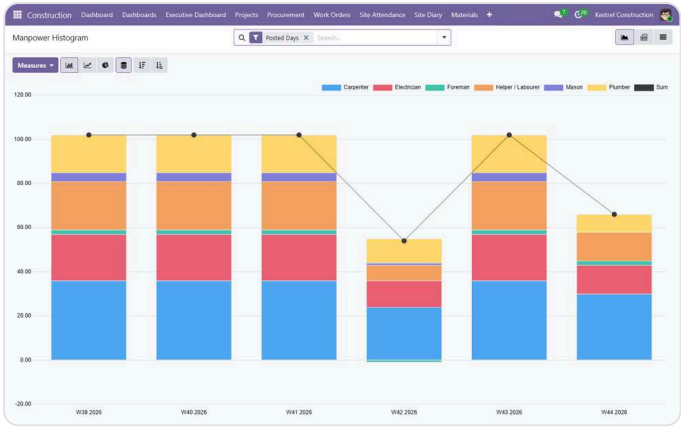

ENTERPRISE **Manpower Histogram**: people on site per day by trade.

19.2 Geofenced check-in from a phone ENTERPRISE

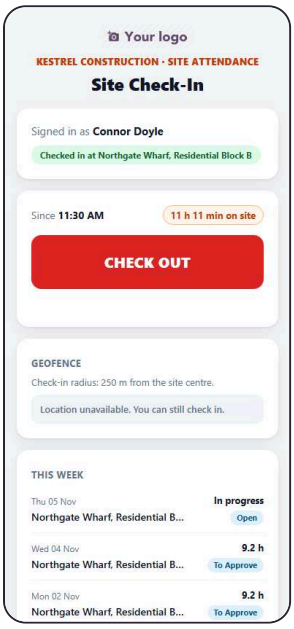

3 ENTERPRISE

My Site Check-In

Site Attendance, My Site Check-In opens **/construction/checkin** in the phone's browser: who is signed in, the site they are checked in at, since when and for how long, one big Check In or Check Out button, the geofence radius, and the week's shifts with their status. The phone's location is sent and the server decides whether it is inside the circle set on the project (site latitude, longitude, radius).

A project set to Block refuses a punch from outside the fence and tells the worker why; Flag records it for review.


4 ENTERPRISE

What the server records

Check-in and check-out times and positions, the reported accuracy, the distance from the site centre, inside or outside the fence, worked and overtime hours (beyond the company's standard day), and an exception flag: outside geofence, low GPS accuracy, no check-out or manual entry.

An hourly job flags shifts open far too long as having no check-out.


19.3 Roll call and approval ENTERPRISE

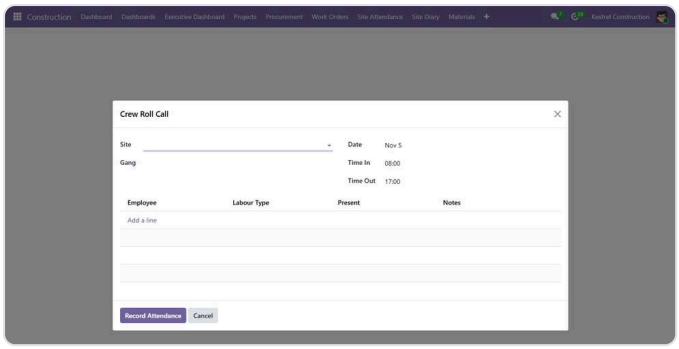

5 ENTERPRISE

Crew roll call


Site Attendance, Crew Roll Call. A supervisor picks the site, gang, date and times and ticks who is present. **Record Attendance** writes one attendance per person.



7 ENTERPRISE

Exceptions

Only the flagged records. Attendance by Site is the pivot and graph by site and day.

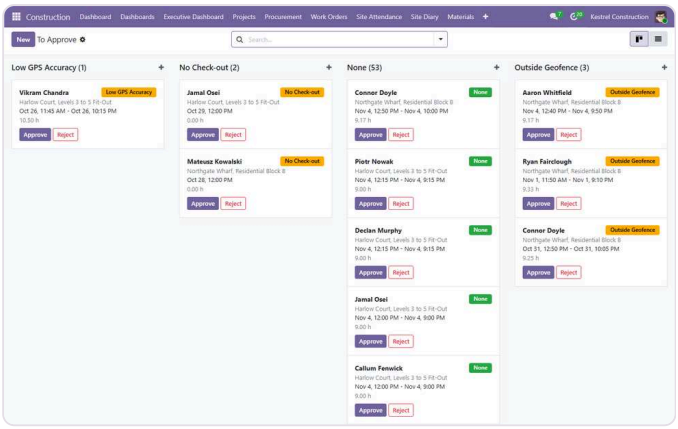

6 ENTERPRISE

To approve

Site Attendance, To Approve. **Approve** writes a labour log for the job at the worker's labour type rate; **Reject**; **Send Back to Approval** undoes a rejection made in error.

PART 20 Plant, tools, maintenance and petty cash


ENTERPRISE

Hired plant charges the job every day it stands on site, so it is tracked daily. Small tools move between people inside an afternoon, so custody is signed for. Site cash has a ceiling and a receipt rule.

TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Site Costs, Plant Hire
2. Open Resources, Custody Register and group by holder
3. Open Petty Cash, Floats and open a site float


20.1 Plant hire ENTERPRISE



1 ENTERPRISE

Hires

Commercial, Site Costs, Plant Hire. Machine, category (default rates and idle threshold), hire company, operator, rate basis (daily, weekly, monthly), minimum hire, delivery and collection charges, on hire, planned and actual off hire, hire contract and off-hire numbers, days on hire and chargeable days. **Put On Hire**, **Off Hire**, **Today's Sheet**.

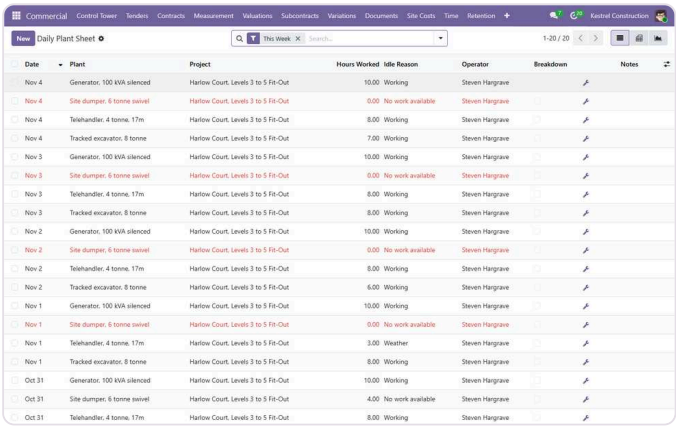


2 ENTERPRISE

The daily plant sheet

One line per machine per day: hours worked, idle reason, operator, fuel, breakdown. **Report Breakdown** raises a maintenance request.

A daily job warns before the planned off-hire date and flags machines idle past their category threshold.




3 ENTERPRISE

Idle and Overdue Plant

Reporting, Idle and Overdue Plant: hires standing idle or past their planned off-hire date.


20.2 Plant maintenance ENTERPRISE



4 ENTERPRISE

Maintenance requests


Resources, Plant Maintenance, Maintenance Requests: the Odoo Maintenance app, with the job, operator, downtime start and end, downtime hours, parts and labour cost. The repair cost is posted to the job as one site expense.

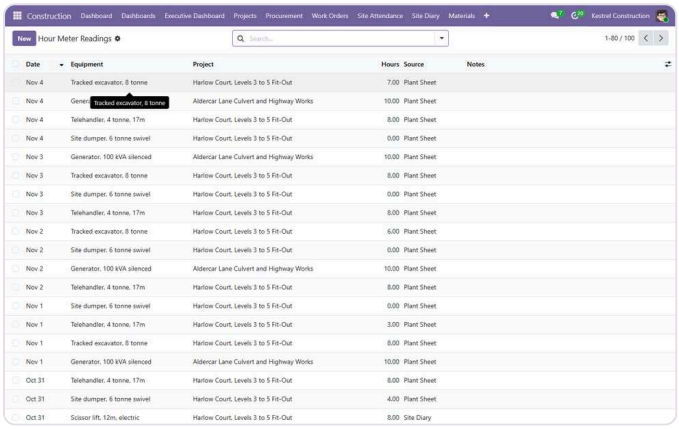

6 ENTERPRISE

Hour meter readings

Running hours from plant sheets and diary plant lines, kept in step automatically. A daily job raises a preventive service request once a machine is within the hours set in Settings. Due for Service and Downtime Analysis list and chart them.




5 ENTERPRISE

Fleet availability

Every machine with its meter reading, hours to next service, open requests, downtime and maintenance cost. **Link to Maintenance** creates the Maintenance equipment record.


20.3 Small tools and custody ENTERPRISE

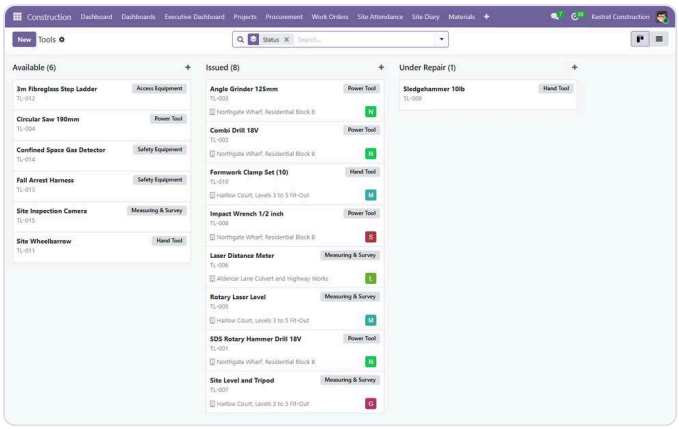

7 ENTERPRISE

The tools register


Resources, Tools. Serial or asset number, category, photo, replacement value, status (available, issued, under repair, lost, retired), current holder and project. **Mark Lost**, **Retire**, **Return to Store**.

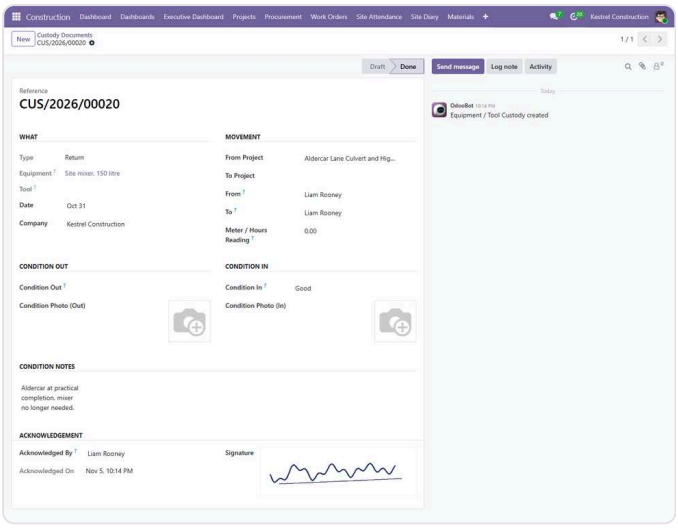

8 ENTERPRISE

A custody note


A handover, return or transfer for one tool or one machine: from and to project and person, condition out and in, meter reading, photos, who acknowledged it, when, and a signature. **Complete** moves the holder.



9 ENTERPRISE


The custody register

Who holds what right now, tools and plant in one list, to group by project or by person.

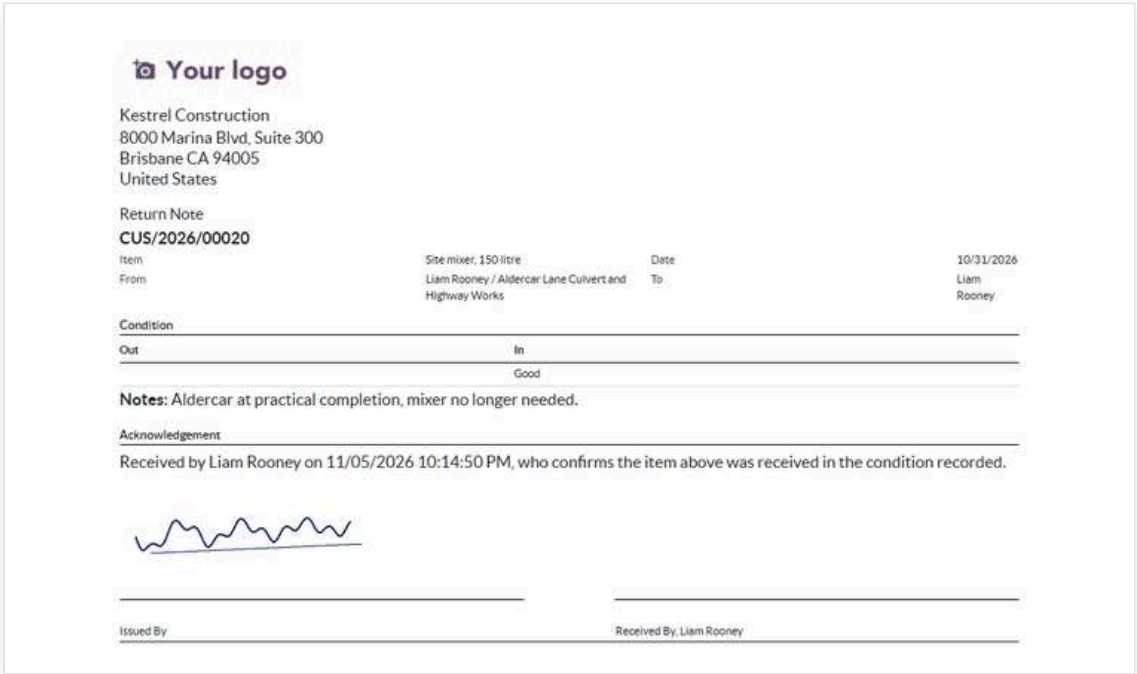

ENTERPRISE Print, Custody Note for signature.


20.4 Petty cash ENTERPRISE

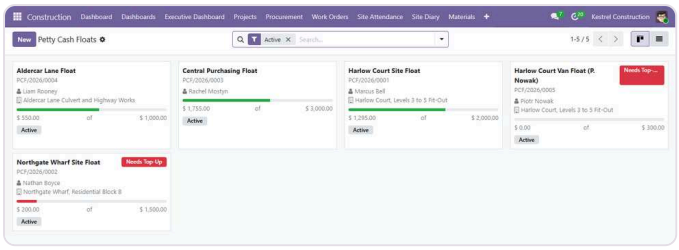

10 ENTERPRISE

Floats

Petty Cash, Floats. A float is held by one person: a site float carries a project; a purchase agent's float has none and each expense names its project. Ceiling, per-transaction limit, receipt required above, replenish below %, allowed categories.

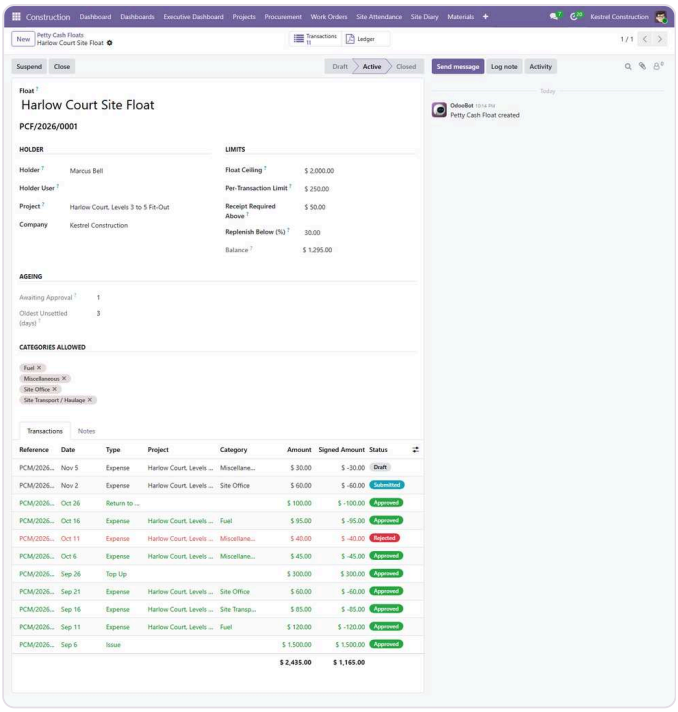


11 ENTERPRISE

A float and its statement

Balance, balance against the ceiling, needs top-up, awaiting approval and oldest unsettled days. Transactions: issue, top up, expense, return to office, recovery or adjustment. **Activate**, **Replenish** (raises the top-up back to the ceiling), **Suspend**, **Close**.


An approved and posted expense becomes a site expense on the job, with its cost code.



12 ENTERPRISE

To approve

Expense claims waiting. **Approve** needs the Finance or Commercial role; **Post** writes the site expense. Floats Needing Top-Up lists those below their threshold.

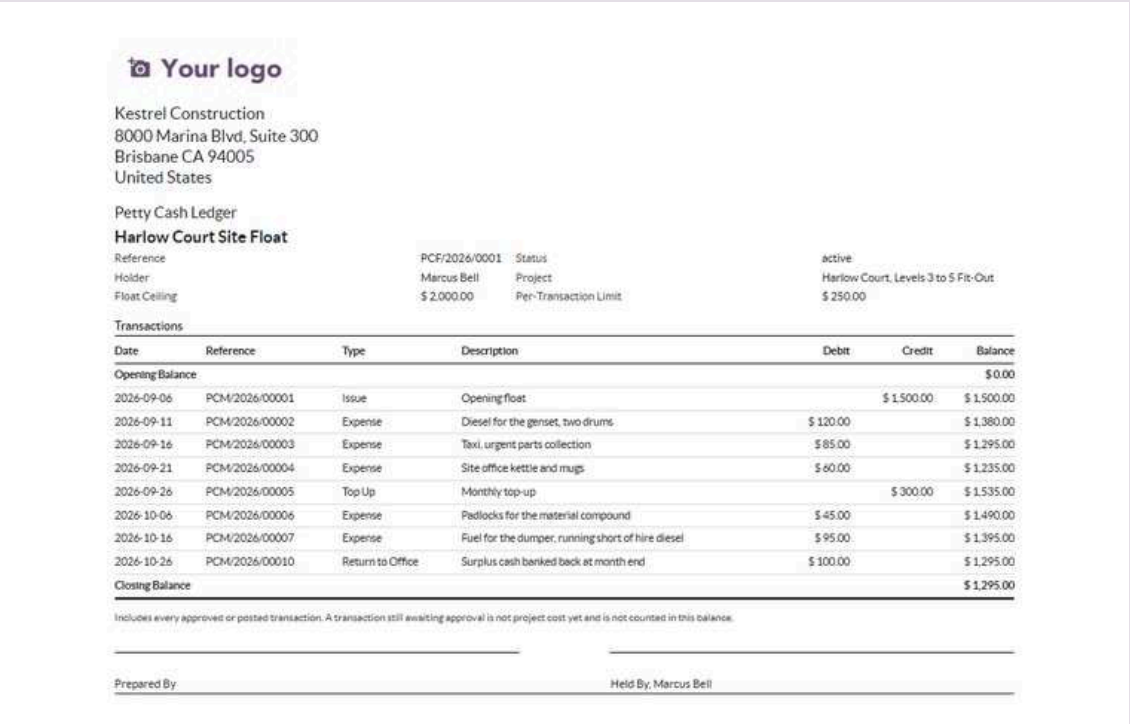

Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Petty Cash Ledger

Harlow Court Site Float

Reference	PCF/2026/0001	Status	active
Holder	Marcus Bell	Project	Harlow Court, Levels 3 to 5 Fit-Out
Float Ceiling	$ 2,000.00	Per-Transaction Limit	$ 250.00

Transactions

Date	Reference	Type	Description	Debit	Credit	Balance
Opening Balance						$ 0.00
2026-09-06	PCM/2026/00001	Issue	Opening float		$ 1,500.00	$ 1,500.00
2026-09-11	PCM/2026/00002	Expense	Diesel for the genset, two drums	$ 120.00		$ 1,380.00
2026-09-16	PCM/2026/00003	Expense	Taxi, urgent parts collection	$ 85.00		$ 1,295.00
2026-09-21	PCM/2026/00004	Expense	Site office kettle and mugs	$ 60.00		$ 1,235.00
2026-09-26	PCM/2026/00005	Top Up	Monthly top-up		$ 300.00	$ 1,535.00
2026-10-06	PCM/2026/00006	Expense	Padlocks for the material compound	$ 45.00		$ 1,490.00
2026-10-16	PCM/2026/00007	Expense	Fuel for the dumper, running short of hire diesel	$ 95.00		$ 1,395.00
2026-10-26	PCM/2026/00010	Return to Office	Surplus cash banked back at month end	$ 100.00		$ 1,295.00
Closing Balance						$ 1,295.00

Includes every approved or posted transaction. A transaction still awaiting approval is not project cost yet and is not counted in this balance.

Prepared By

Held By, Marcus Bell

ENTERPRISE Print, Petty Cash Ledger for the float.

PART 21


Documents: RFIs, submittals, drawings and transmittals

ENTERPRISE

An RFI is evidence of when a question was asked, a submittal of when approval was sought, a transmittal of who had which revision. Each carries a clock and a chaser.

TRY IT YOURSELF ON THE DEMO

1. Open Commercial, Documents, Requests for Information
2. Open RFIs Holding Up Work
3. Open the Drawing Register and a drawing with several revisions

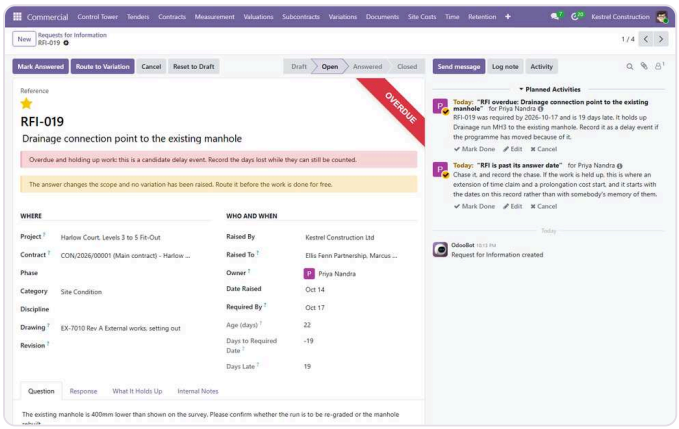


1 ENTERPRISE

A request for information

Commercial, Documents, Requests for Information. Subject, category (which sets the required-by date), drawing and revision, priority, raised to, the question and the response, age, days late, holds up work. **Raise**, **Mark Answered**, **Close**, **Reopen**, **Route to Variation** when the answer costs money.

Outstanding Information and RFIs Holding Up Work list the ones that matter today.

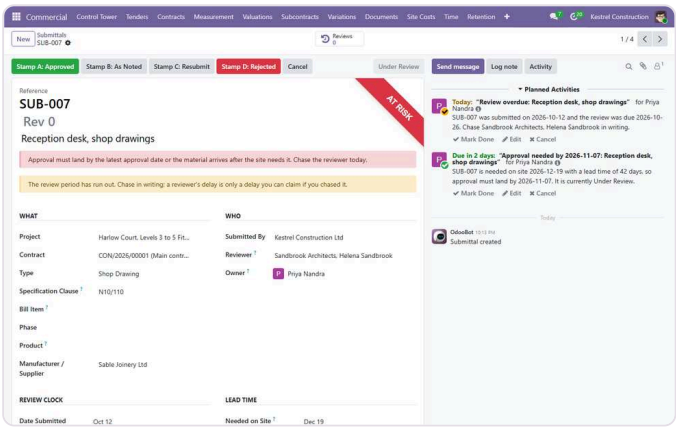


2 ENTERPRISE

A submittal

Type, specification clause, bill item, product, supplier, reviewer, revision. Review due is submitted date plus the type's review period; latest approval is needed-on-site less the lead time. Stamps: **A Approved**, **B As Noted**, **C Resubmit**, **D Rejected**; every stamp is kept in the review history.


Approvals at Risk lists submittals whose latest approval date is close or past.



3 ENTERPRISE

The drawing register

Number, title, discipline, type, originator, scale, sheet size, current revision and status (not issued, preliminary, for construction, withdrawn). **New Revision** opens the next one; **Issue on a Transmittal** sends the selected drawings.

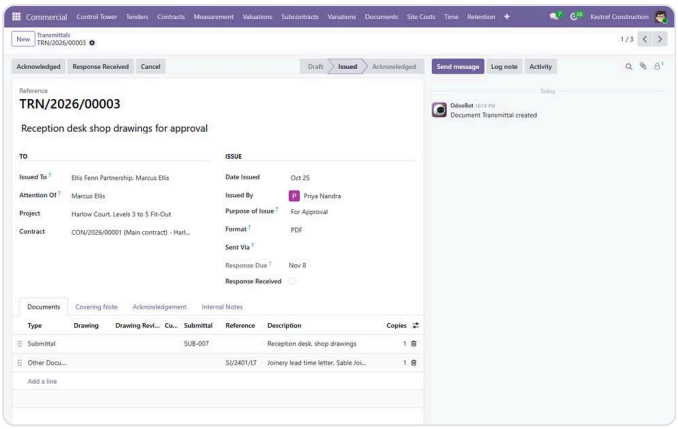

4 ENTERPRISE

A transmittal

Issued to, attention of, purpose of issue, format, method, covering note, and the documents with revision and copies. **Swap to Current Revisions** replaces any superseded revision on a draft. **Issue**, **Acknowledged**, **Response Received**.

Who Had What lists every document ever sent, to whom and at which revision.

Daily jobs chase RFIs before and after their required date, submittal reviews past due and approvals at risk, and transmittal responses before they are due. The libraries (RFI categories, submittal types, review stamps, disciplines and purposes of issue) are in Commercial, Configuration.

PART 22


QHSE: permits, toolbox talks, incidents, inspections, NCRs and snags

ENTERPRISE

Quality, health, safety and environment on one menu, each record tied to a project, a phase and a location, and each with its own chaser.

TRY IT YOURSELF ON THE DEMO

1. Open QHSE, Permits to Work and a live permit
2. Open QHSE, Hold Points Awaiting Release
3. Open QHSE, Snags and filter on Holds Retention

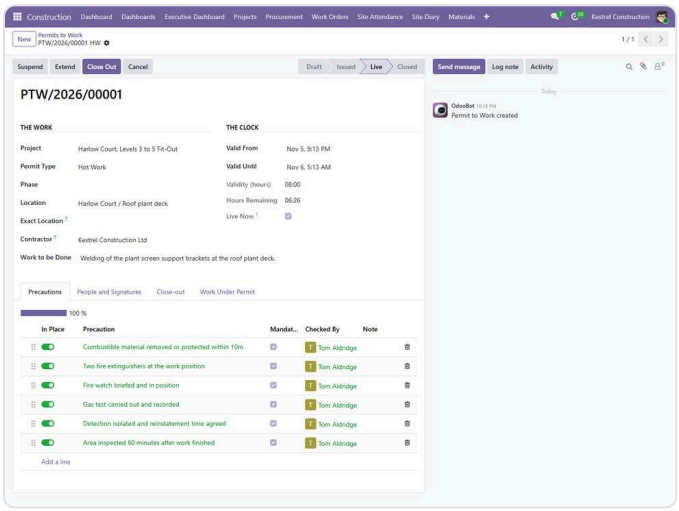


1 ENTERPRISE

A permit to work

QHSE, Permits to Work. Type (hot work, confined space, height, excavation, electrical isolation, lifting), exact location, work, contractor, permit holder, valid from and until, precautions checklist, gas test, isolation certificate, fire watch, both signatures. **Issue** needs every mandatory precaution ticked; **Accept (Holder)**, **Suspend**, **Resume**, **Extend** within the type's ceiling, **Close Out**, **Renew for Today**.

A 15 minute job expires permits as their clock runs out. Permit Board shows them on a calendar.

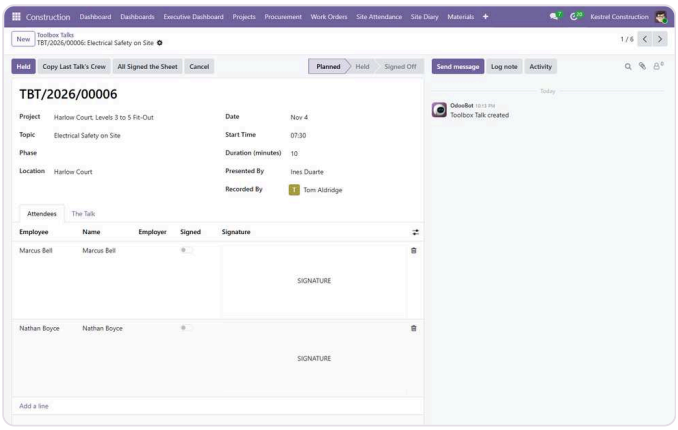


2 ENTERPRISE

A toolbox talk

Topic (key points and check questions copied from the library), date, presenter, site-specific points, attendees with signatures. **Copy Last Talk's Crew**, **All Signed the Sheet**, **Next Talk, Same Crew**.

A live job that has heard no talk in a week gets a to-do.

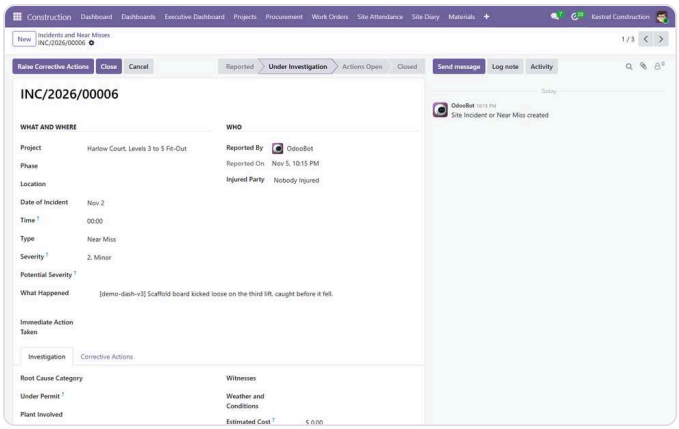


3 ENTERPRISE

An incident or near miss

Type, actual and potential severity, injured party, lost time days, and whether it is reportable to the authority (worked out from type and severity, with the report due date). Investigation, root cause, corrective actions with owners and due dates.

A daily job raises the statutory report before its deadline and chases the actions.

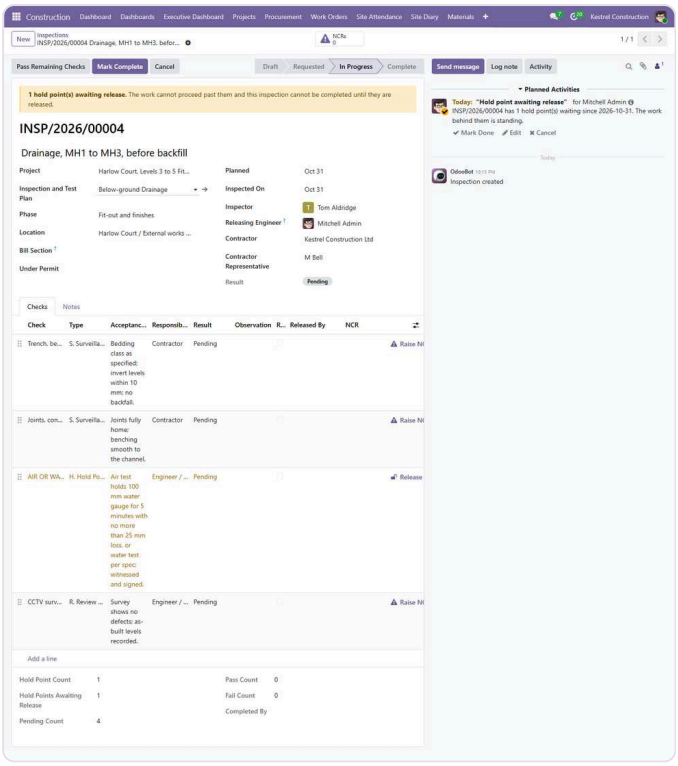


4 ENTERPRISE

An inspection with hold points

From an inspection and test plan: checks with acceptance criteria, type and responsible party. Each check passes, fails or is not applicable; a hold point needs a named release. **Request Engineer**, **Pass Remaining Checks** (never hold points), **Raise NCR** from a failed check, **Mark Complete**.


Hold Points Awaiting Release lists the work that cannot proceed.

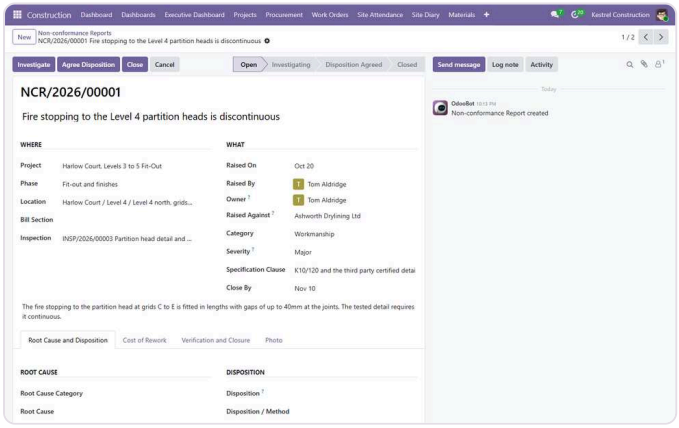

5 ENTERPRISE

A non-conformance report


Category, severity, raised against (a subcontractor), specification clause, close-by date, root cause, disposition (rework, repair, accept as is with a concession, reject and replace), cost of rework and whether it is recoverable. **Raise Re-inspection** proves the rework.

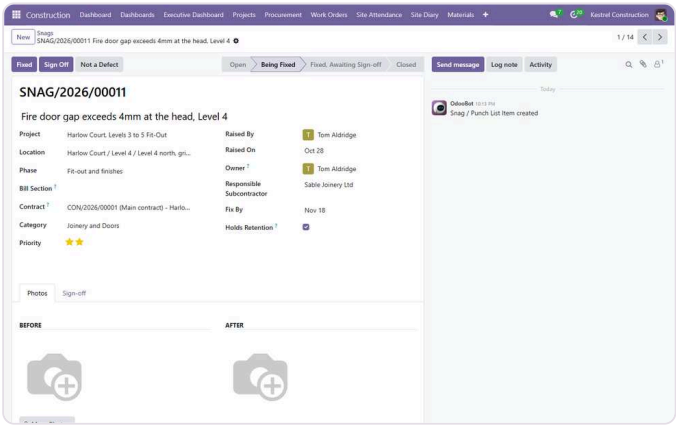

6 ENTERPRISE

A snag


Location, category, priority (normal, high, stops handover), photos before and after, owner, responsible subcontractor, fix by, holds retention. **Being Fixed**, **Fixed**, **Sign Off** by somebody other than the raiser, **Not a Defect**.

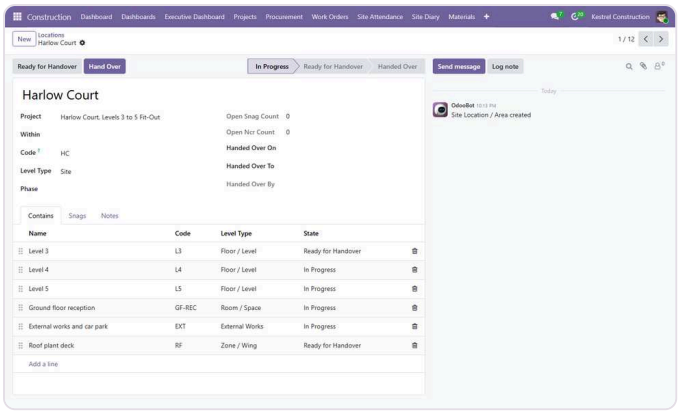

7 ENTERPRISE

Locations and handover

QHSE, Locations: site, block, floor, zone, room. **Ready for Handover** and **Hand Over**, refused while anything open sits in the area or below it.

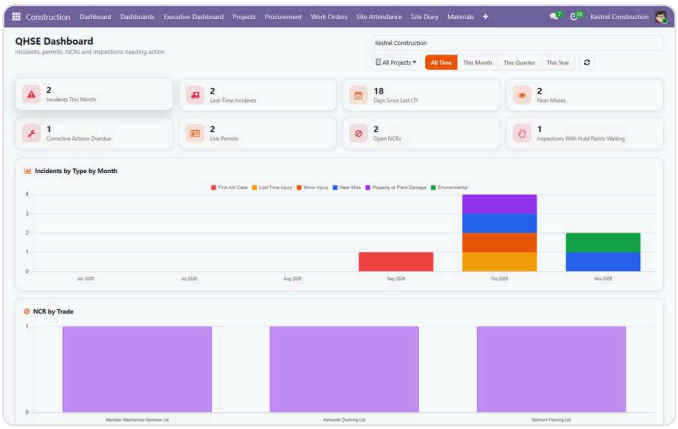

8 ENTERPRISE

The QHSE dashboard


Live permits, open hold points, NCRs and snags, incidents by type, LTIFR and days since the last lost-time injury.

The libraries are in Construction, Configuration: Permit Types (validity, ceiling, gas test, fire watch, isolation, the precaution checklist), Toolbox Talk Topics (key points, check questions, repeat interval) and Inspection and Test Plans (checks by work type).

PART 23 The client and subcontractor portal

ENTERPRISE

Clients see their contracts, certificates, variations and what they have paid. Subcontractors see their orders, valuations and payments. Both log in to the standard Odoo portal, on a phone or a computer, and see only their own records.

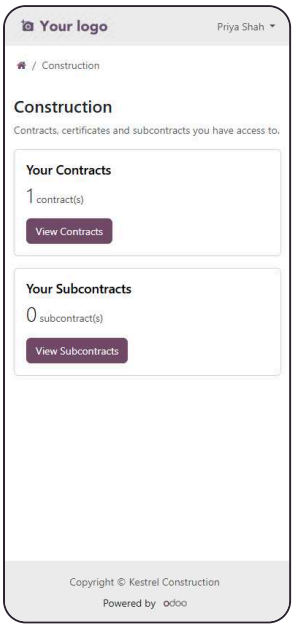


1 ENTERPRISE

My Construction

A portal user opens **/my/construction** from the portal home: Your Contracts and Your Subcontracts, each with a count and a button into the list.

Give access with Share with Client on the contract, or the standard Grant Portal Access on a contact.

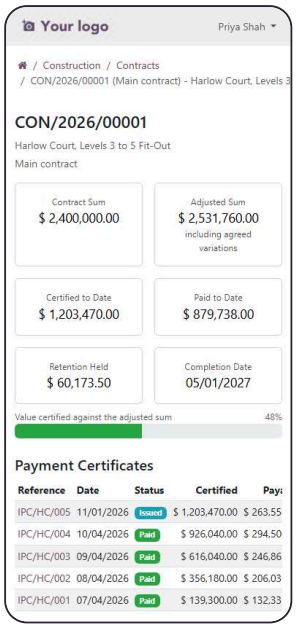

2 ENTERPRISE

A contract, seen by the client


Contract sum, adjusted sum including agreed variations, certified to date, paid to date, retention held, the completion date and a bar of value certified against the adjusted sum. Below, every payment certificate with its status, certified amount and payable, each opening to a page with a PDF download.



3 ENTERPRISE

Variations

Every variation on the client's contracts with its status and the value being asked for.

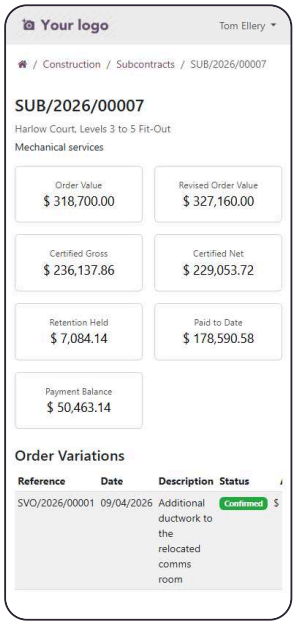

4 ENTERPRISE

A subcontract, seen by the subcontractor

Order value, revised order value, certified gross and net, retention held, paid to date and the payment balance, then the order variations and every valuation with its status.

Portal pages are reached only after an ownership check: a client sees contracts where they are the employer, a subcontractor sees orders where they are the subcontractor. Internal costs, budgets and margins never appear.

PART 24


Control tower, approvals and month-end controls

ENTERPRISE


The commercial office's view of everything that needs a decision, and the controls that stop money moving without one: approval by value, delegation, a month lock and an audit trail.

24.1 Control tower ENTERPRISE

Commercial, Control Tower	What it shows
Executive Dashboard	The portfolio on one screen (Part 26).
Alerts	Everything the alert rules have raised, worst first, by job.
Waiting on Me	Approvals the signed-in user can sign now, including under a delegation.
Cash Position	Certificates by job: certified, paid, outstanding.
Retention Held and Due	Retention by contract and due date.
Variation Exposure	Unsettled variations at carrying value.
Margin by Job	Margin from the signed CVRs.
Live Margin by Job	Every job's budget, committed, actual, margin at full commitment, today.




ENTERPRISE **Alerts**: rule, record, job, assigned to, severity, status.



ENTERPRISE **Live Margin by Job**.

24.2 Alert rules ENTERPRISE

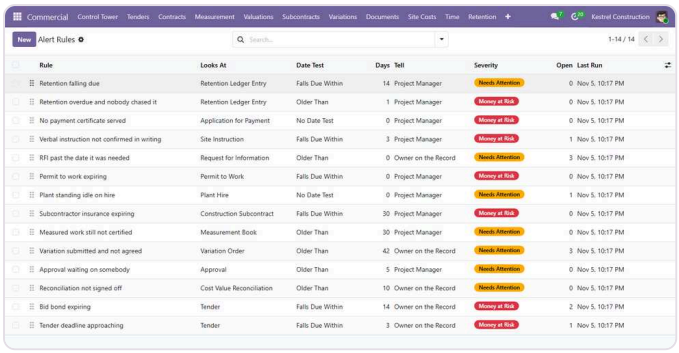

1 ENTERPRISE


An alert rule

Commercial, Configuration, Alert Rules. Which model, which records (a domain), a date test (falls due within or older than so many days), who to tell (project manager, the record owner, named people or a group), the one line summary, what to do, severity, repeat interval and a per-run ceiling.

What Does It Catch? previews the records before anyone trusts the rule; **Run It Now** tries it.

One daily job evaluates every rule, and a rule that fails does not stop the others. Each alert becomes an activity on the person told, and can be marked **Actioned** or **Dismissed** with an outcome.

24.3 Approvals ENTERPRISE

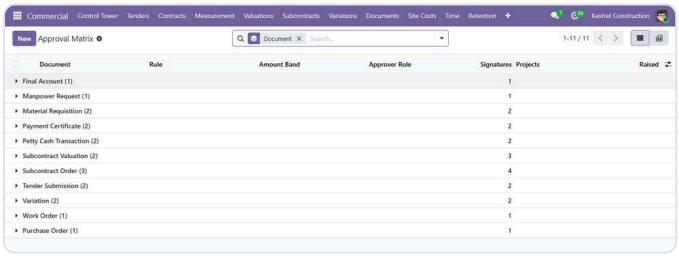


2 ENTERPRISE

The approval matrix

Commercial, Controls, Approval Matrix. One rule per document type and value band: over, up to, approved by named people or anyone in a group, signatures needed, projects it applies to, and why it exists.

Rules are configuration only until **Turn Enforcement On**. **Enforce the Whole Matrix** extends it beyond variations and subcontracts.

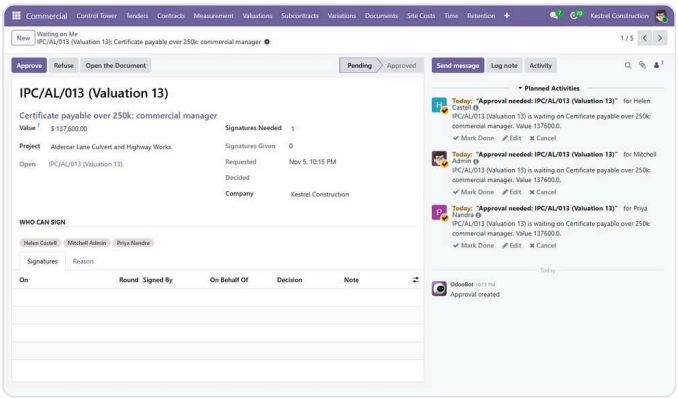


3 ENTERPRISE

An approval

The document, its value when the chain was raised, signatures needed and given, who can sign, and every signature by round. **Approve**, **Refuse** with a reason, **Send Back Round**.

If the document's value changes, the chain is raised again.

Documents the matrix can govern	
Variations (agree), subcontracts (confirm)	Always, once enforcement is on.
Certificates (issue), subcontract valuations (certify), work orders (release), manpower requests, petty cash, final accounts, tenders, requisitions	When the whole matrix is enforced.

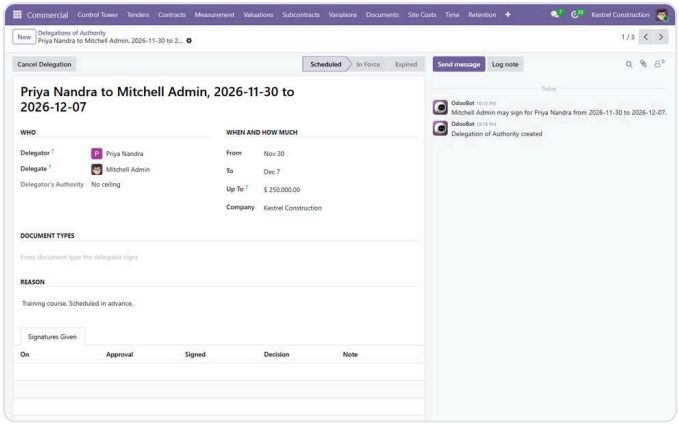


4 ENTERPRISE

Delegation of authority

Commercial, Controls, Delegations. Who lends their authority, to whom, from and to, for which document types and up to what value. Every signature given under it says on whose behalf.

24.4 Close the month ENTERPRISE

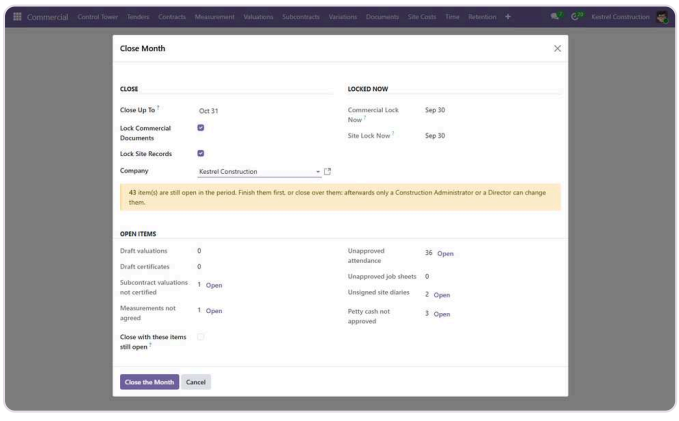


5 ENTERPRISE

Period Lock / Close Month

Pick the close-up-to date and whether to lock commercial documents, site records, or both. The dialog counts the valuations, certificates, measurements, attendance, job sheets, diaries and petty cash still open in the period. Tick to close over them if you must; they stay open.

Once locked, those records cannot be created, changed or deleted on or before the date.

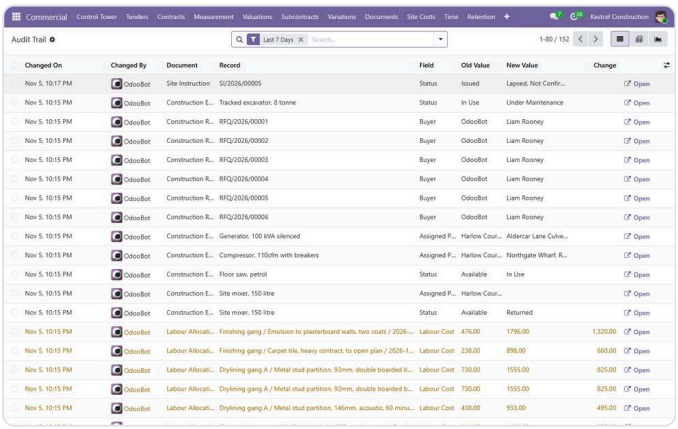


6 ENTERPRISE

Audit trail

Commercial, Controls, Audit Trail. Who changed which field on which document, from what to what, and the change in money for number fields. Filter on My Team.

24.5 Project templates ENTERPRISE



7 ENTERPRISE

A template

Commercial, Configuration, Project Templates. Job type, typical duration, form of contract, and tabs for phases (offset and duration in days from possession, never dates), bill sections, cost codes, a document register of drawings and submittals, an inspection plan, expected permits and the approval chain.

8 ENTERPRISE


Apply it

Apply a Template on a project (or during a tender award). The dialog asks for the possession date and which parts to create, and shows what it will create before anything is written.

PART 25 Roles and access control

ENTERPRISE


Who can see and change what. The Base module's three roles are enough for a small firm; Enterprise turns access into a ladder with specialist roles, hides cost from site roles in the database, and can keep users inside their own jobs.

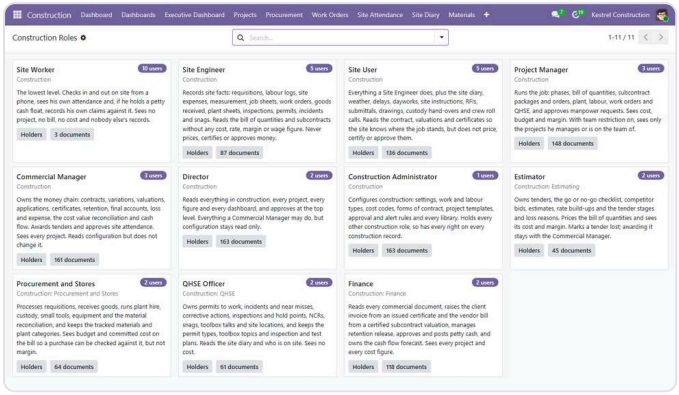

1 ENTERPRISE

Construction roles


Construction, Configuration, Access Control, Construction Roles. One card per role with a plain summary of what it does and how many construction documents it can open.

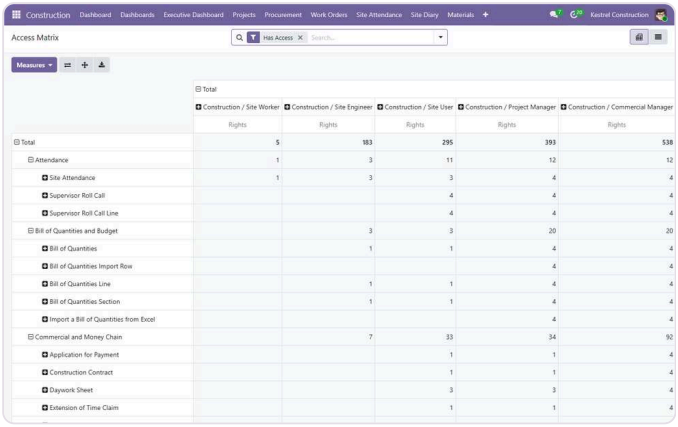

2 ENTERPRISE

The access matrix


Every role against every construction document: read, write, create, delete, and a level (no access, read only, edit, full). "Own row" says whether the right is the role's own or comes with a role it includes.



3 ENTERPRISE

Who has which role

Every user and every construction role they hold, given directly or through a higher role.

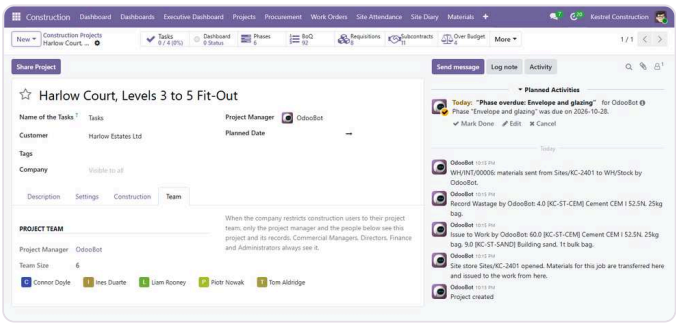

4 ENTERPRISE

The project team


The Team tab on a project. With **Restrict to Project Team** on in Settings, site, engineering, QHSE, procurement and estimating users see only the projects they manage or are on the team of. Commercial, director and finance see every job.

> Costs, rates, wages and margins carry field-level groups. A site engineer opening a bill item sees quantities but no rate; a procurement user sees budget and committed but not margin. This is enforced by the server, not only hidden on the screen.


PART 26 Dashboards

ENTERPRISE


One executive dashboard above everything, and one per role. Each is a live screen with tiles that open the records behind them.

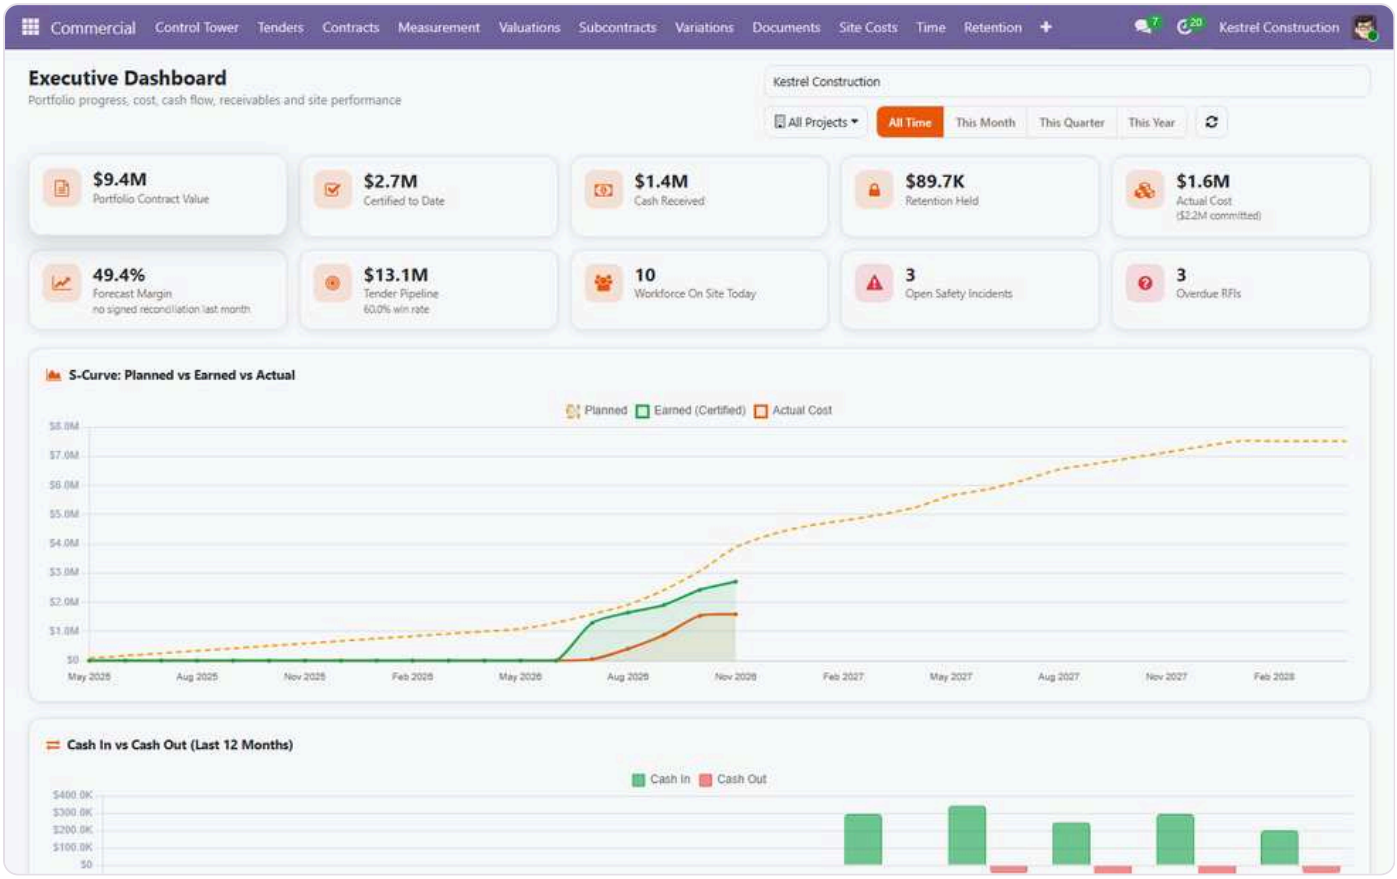


ENTERPRISE Executive Dashboard: portfolio value, certified and received, margin, an S-curve of planned, earned and actual, cash in and out, the tender pipeline, workforce on site and every job's status.

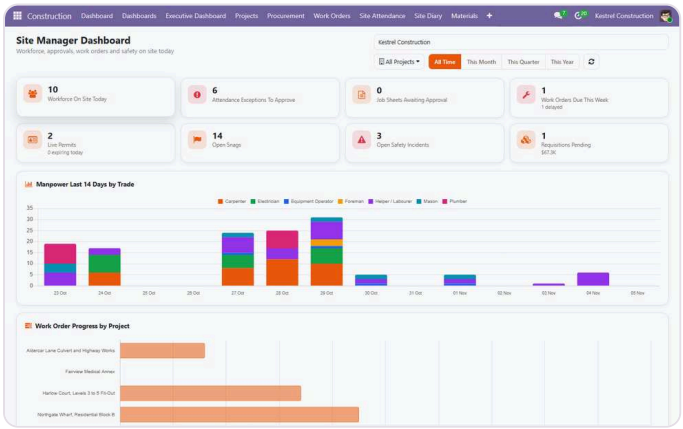


ENTERPRISE **Site Manager**: today on site, diaries to post, permits live, work orders, attendance to approve.

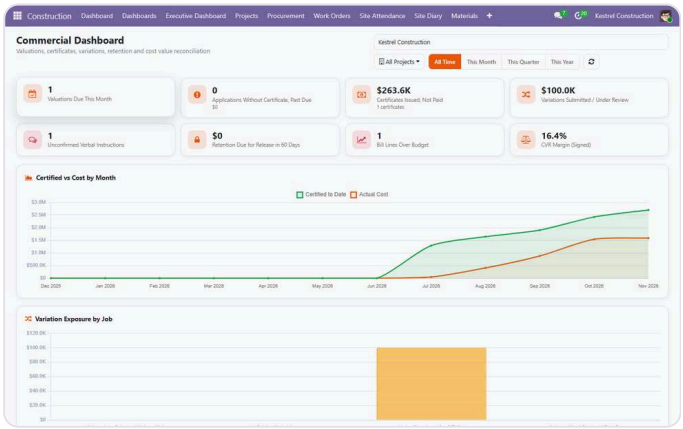

ENTERPRISE **Commercial**: valuations due, certificates, variations, retention, cost trend.

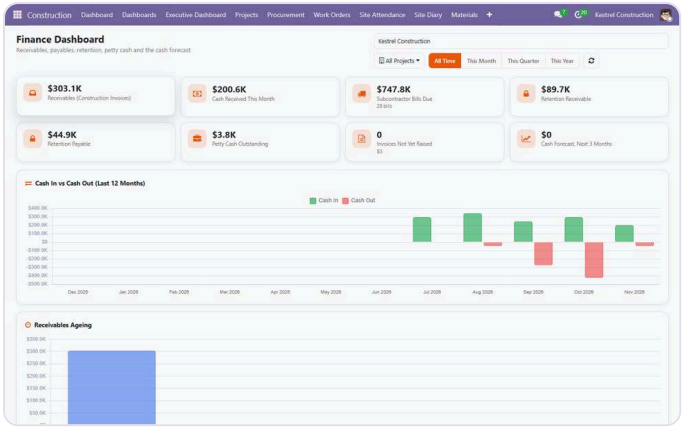

ENTERPRISE **Finance**: invoices from certificates, bills from valuations, cash in and out, petty cash.

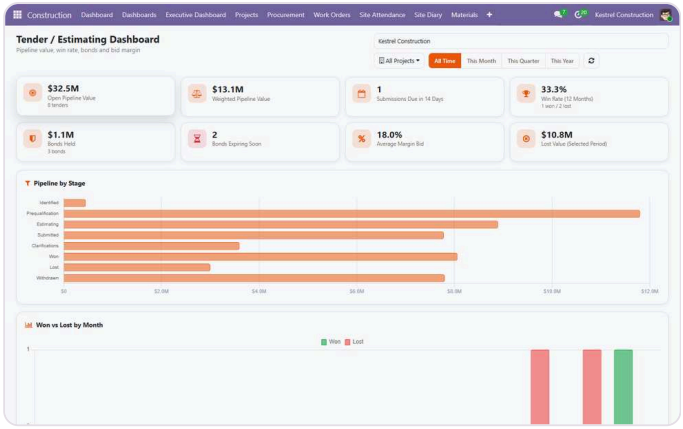

ENTERPRISE **Tender / Estimating**: pipeline, win rate, deadlines, bonds.

The QHSE and Procurement dashboards are shown in Parts 22 and 16. Every chart that draws cost over time takes material cost from one method, so a dashboard can never disagree with the budget about what material cost a job.

PART 27 Printed documents and Excel exports

Every print uses the company letterhead. The Print menu on each record lists the documents it can produce.

Print	From	Edition	Part
Bill of Quantities	Project	BASE	6
Project Progress Report	Project	BASE	9
Material Requisition	Requisition	BASE	7
Tender Submission Summary	Tender	ENTERPRISE	10
Construction Quotation	Sales quotation	ENTERPRISE	10
Measurement Sheet	Measurement	ENTERPRISE	11
Application for Payment	Application	ENTERPRISE	11
Payment Certificate	Certificate	ENTERPRISE	11
Running Account (RA) Bill	Certificate or application	ENTERPRISE	11
Variation Order	Variation	ENTERPRISE	12
Daywork Sheet	Daywork	ENTERPRISE	12
Final Account Statement	Final account	ENTERPRISE	13
Cost Value Reconciliation	Project	ENTERPRISE	15
Job Cost Sheet	Project or the wizard	ENTERPRISE	15
Quote Comparison	Request for quotation	ENTERPRISE	16
Work Order Job Card	Work order	ENTERPRISE	17
Custody Note	Custody	ENTERPRISE	20
Petty Cash Ledger	Float	ENTERPRISE	20

Excel ENTERPRISE

Export	From
Bill of quantities with sections	Bill, Export to Excel
Job Cost Sheet	Job Cost Sheet wizard, Export to Excel
Payment certificate	Certificate, Export to Excel
Cost value reconciliation	CVR, Export to Excel
Bill import template	Import wizard, Download Template



Your logo

Kestrel Construction
8000 Marina Blvd, Suite 300
Brisbane CA 94005
United States

Quotation
S00027

Client	Fairview Health Trust	Quotation Date	11/05/2026 10:15:23 PM
Project	Fairview Medical Annex	Our Reference	TND/2026/00013
Valid Until	12/05/2026	Total	$ 2,128,420.00

Priced Bill Summary

Section	Amount
1 Substructure and Frame	$ 327,600.00
2 MEP and Fit-Out	$ 1,523,200.00
Quotation Total	$ 2,128,420.00

Terms and Exclusions

Mobilisation advance: 10.0% of the contract sum, recovered pro-rata from certificates.

Retention: 5.0% held from each certified valuation.

Payment terms: 30 days from the date a certificate becomes due.

Defects liability period: 12 months from practical completion.

This quotation is valid until the date shown above. Prices exclude anything not listed in the priced bill summary. Construction invoicing runs through payment certificates against measured and certified quantity, not through this quotation.

For the Contractor

Date

ENTERPRISE Construction Quotation, from the client quotation.



Your logo

Al Bayan Contracting LLC
Office 1204, Bay Square Building 7, Business Bay
Dubai CA 94005
United Arab Emirates

Material Requisition

Reference: MRQ/2026/00003
Project: Marina Heights Residential Tower (G+12)
Phase: Superstructure Frame

Date: 09/29/2026
Required By: 10/04/2026
Status: Issued

#	Material	Description	Unit	Requested	Issued	Unit Cost	Subtotal
1	XLPE Cable 4C x 16 mm2 (m)	XLPE Cable 4C x 16 mm2 (m)	Units	1,200.0	1,200.0	$ 46.00	$ 55,200.00
2	Gypsum Board 12.5 mm sheet	Gypsum Board 12.5 mm sheet	Units	650.0	650.0	$ 27.00	$ 17,550.00

Total Cost **$ 72,750.00**

Requested By

Approved By

BASE Material Requisition.

PART 28 What runs by itself

Scheduled jobs that chase, flag and reverse without anyone remembering to. Each raises an activity on the person who has to act, and none repeats while its activity is still open.

Job	How often	What it does	Edition
Overdue Phase Reminders	Daily	A to-do on the project for each phase past its planned finish.	BASE
Pending Requisition Reminders	Daily	A to-do on each submitted requisition.	BASE
Evaluate alert rules	Daily	Runs every alert rule (Part 24).	ENTERPRISE
Valuation and Retention Reminders	Daily	Before each valuation date; retention fallen due.	ENTERPRISE
Chase uncertified measurements	Daily	Sheets measured and not certified.	ENTERPRISE
Applications With No Certificate	Daily	Applications past due with nothing certified.	ENTERPRISE
Retention Falling Due	Daily	Raises each moiety as it falls due, then chases it.	ENTERPRISE
Sync certificate payments from invoices	Daily	Backstop for payment status on certificates and subcontract valuations.	ENTERPRISE
Confirm Verbal Instructions	Daily	Warns before the confirmation window shuts, then records it lapsed.	ENTERPRISE
Chase Unsigned Daywork Sheets	Daily	Sheets ageing without a signature.	ENTERPRISE
Reverse Due and Superseded Accruals	Daily	Reverses accruals at their date and flags invoiced ones.	ENTERPRISE
Chase Delay Notices	Daily	Before the notice deadline.	ENTERPRISE
Chase Unposted Site Diaries	Daily	Yesterday's diary still open or missing.	ENTERPRISE
Flag Attendance Without Check-out	Hourly	Shifts open far too long.	ENTERPRISE
Expire Permits to Work	Every 15 minutes	Closes expired permits and warns about those about to expire.	ENTERPRISE
Toolbox Talk Reminder	Daily	A live job with no talk in a week.	ENTERPRISE
Chase Incident Reports and Actions	Daily	Statutory reports before their deadline, open actions.	ENTERPRISE
Chase Inspections and Hold Points	Daily	Tomorrow's inspections, stuck hold points.	ENTERPRISE
Chase Open NCRs, Chase Open Snags	Daily	Before their close-by or fix-by date and daily once overdue.	ENTERPRISE
Chase RFIs, submittals, transmittal responses	Daily	Before and after their due dates.	ENTERPRISE

Plant Off-Hire and Idle Check	Daily	Off-hire reminders, idle plant, hire charge refresh on the bill item.	ENTERPRISE
Gangs Below Norm	Daily	One activity per gang under norm over the last week.	ENTERPRISE
Preventive plant maintenance check	Daily	Service requests by running hours.	ENTERPRISE

PART 29 A 15 minute demo

A route through the product for someone seeing it for the first time. The first half runs on the live demo; the second half needs an Enterprise demo database.

MIN	SHOW	SAY
0	Construction, Dashboard	*Every job on one screen: contract value, cost so far, what is waiting for approval.*
2	Marina Heights, Construction tab	*A normal Odoo project with a construction layer: code, stage, supervisor, cost summary.*
4	Phases, then the Bill of Quantities	*The timeline and the budget. Every cost lands against a job and a phase.*
6	An approved requisition, then Issue Materials	*Asked for on site, approved by the manager, costed when issued.*
7	Labour Logs and a subcontract	*The gang sheet in one screen; let, billed and paid on the order.*
8	Reporting, Cost Analysis	*Where the money went, by job and category.*
9	Enterprise: Commercial, Tenders, Pipeline	*Win the job here; one award opens the project, bill and contract.*
10	Measurement Book, then a certificate	*Measured, valued, certified, claimed against certified with reasons.*
12	The RA Bill print	*The monthly bill the client signs, with retention and advance recovery.*
13	A signed CVR	*The honest margin this month: value against actual, accrued and committed.*
14	Executive Dashboard	*The director's screen: S-curve, cash, every job's status.*

PART 30

Questions people ask

Question	Answer
Does it need Odoo Enterprise?	No. Both modules run on Odoo 19 Community, and on Enterprise if you already have it. "Enterprise" is the name of our add-on, not of the Odoo edition.
Can I start with Base and add Enterprise later?	Yes. Install the add-on on top; existing projects, bills and costs stay, and every bill item gets a starting budget.
Does issuing materials move stock?	Not in Base. With Enterprise, set Material Flow to Inventory and requisitions become transfers to a site store, charged when issued to the work.
Is the dashboard margin a forecast?	No. In Base it is contract value less cost so far. For the true margin use the CVR, and Margin at Full Commitment on the project.
Can site engineers see costs?	In Base, yes, on the project cost summary. With Enterprise, rates, wages and margins are hidden from site roles by the server.
Does it print an RA bill?	Yes, from the certificate or the application, with previous, this bill and cumulative, deductions and the amount in words.
Can the client see their certificates online?	Yes, on the portal, with a PDF of each certificate. Subcontractors see their orders and valuations.
Can workers check in without an app?	Yes. The check-in page runs in the phone's browser and is tested against the site's geofence.
Can we import our bill from Excel?	Yes, on a draft bill, with a template and a row-by-row error check before anything is written.
Is it in Arabic?	Both modules ship an Arabic translation.

Want this for your contracting business?

We set it up with your jobs, bills of quantities, cost codes, forms of contract and approval limits, load your open jobs as they stand today, connect your accounts, and train the site team, the quantity surveyors and the office. Main contractors, subcontractors, fit-out firms and civil engineering contractors.

way4tech.com · info@way4tech.com

PART 31 Menu map and feature index

Every menu of both apps, and where each feature is explained.

Construction

Dashboard Base	Construction Control
Projects Base	Projects, Phases, Bill of Quantities, Bills of Quantities
Materials Base	Material Requisitions, Materials, Site Stores, Issue to Work
Resources Base	Equipment, Labour Logs, Subcontracts, Tools, Custody, Plant Maintenance
Site Expenses Base	Every site spend
Reporting Base	Cost Analysis, Labour Analysis, Bill Analysis
Site Diary Enterprise	Today, Diaries, Weather, Delays, Manpower, Plant
Site Attendance Enterprise	Check-In, Roll Call, All, To Approve, Exceptions, By Site
QHSE Enterprise	Permits, Board, Toolbox, Incidents, Inspections, Holds, NCRs, Snags, Locations
Work Orders Enterprise	Work Orders, Job Sheets, Manpower, Delayed, Generate, Schedule
Petty Cash Enterprise	Floats, Transactions, To Approve, Needing Top-Up
Procurement Enterprise	Requisitions, RFQs, Comparison, POs, Goods Received, Bills to Review, Stores, Transfers, Issue, Consumption
Dashboards Enterprise	Site, Commercial, Tender, QHSE, Procurement, Finance
Executive Dashboard Enterprise	The portfolio
Configuration Base	Settings, Work Types, Labour Types, Expense Categories
Configuration (Enterprise) Enterprise	Rate Library, Bill Templates, Cost Codes, Permit Types, Toolbox Topics, ITPs, Access Control

Commercial

Control Tower Enterprise	Executive Dashboard, Alerts, Waiting on Me, Cash, Retention, Exposure, Margin, Live Margin
Tenders Enterprise	Pipeline, Bid Bonds, Competitor Analysis, Opportunities, Quotations
Contracts Enterprise	Contracts
Measurement Enterprise	Measurement Book, Measured Quantities
Valuations Enterprise	Raise a Valuation, Interim Valuations, Applications, Certificates, Client Invoices
Subcontracts Enterprise	Packages, Valuations, Order Variations, Contra Charges, Subcontractor Bills
Variations Enterprise	Site Instructions, Variations, Exposure, Daywork Sheets, Provisional Sums, Approvals
Documents Enterprise	RFIs, Outstanding, Submittals, At Risk, Drawings, Revisions, Transmittals, Who Had What
Site Costs Enterprise	Plant Hire, Daily Plant Sheet, Goods Received, Material Reconciliation, Gangs, Labour Allocations
Time Enterprise	Programmes, Schedule, Delay Events, EOT Claims, Site Diaries
Retention Enterprise	Retention Ledger, Nobody Chased This, Snags Holding Retention
Final Account Enterprise	Final Accounts, Everything Holding a Job Open, Loss and Expense
Cost Value Reconciliation Enterprise	Reconciliations, Accruals, Accruals to Reverse, Cash Flow, Cost by Code
Reporting Enterprise	Budget vs Actual, Over Budget, Unconfirmed Instructions, Unsigned Dayworks, RFIs Holding Up Work, Idle Plant, Waste, Gangs Below Norm, Notices Due, Claimed vs Agreed, Losing Money, Cash Movements, Job Cost Sheet
Controls Enterprise	Approval Matrix, Waiting on Me, Delegations, Close Month, Audit Trail
Configuration Enterprise	Forms of Contract, Valuation Methods, document, plant, delay, weather and tender libraries, Templates, Approval and Alert Rules

Feature index

Access Matrix E Part 25
Accruals E Part 15
Accruals to Reverse E Part 15
Adverse Weather Criteria E Part 18
Alert Rules E Part 24
Alerts E Part 24
All Attendance E Part 19
Application for Payment E Part 11
Applications for Payment E Part 11
Approval Matrix E Part 24
Approval Rules E Part 24
Approvals E Part 24
Approvals at Risk E Part 24
Attendance by Site E Part 19
Audit Trail E Part 24
Bid Bonds E Part 10
Bill Analysis E Part 15
Bill of Quantities B Part 6
Bill Templates E Part 6
Bills of Quantities E Part 16
Bills to Review E Part 11
Budget vs Actual E Part 15
Cash Flow Forecast E Part 15
Cash Movements E Part 15
Cash Position E Part 24
Claimed Against Agreed E Part 13
Client Invoices E Part 11
Commercial E Part 26
Competitor Analysis E Part 10
Construction Quotation E Part 10
Construction Roles E Part 25
Consumption Analysis E Part 16
Contra Charges E Part 14
Contracts E Part 14
Cost Analysis B Part 9
Cost by Code E Part 15
Cost Codes E Part 15
Cost Value Reconciliation E Part 15
Crew Roll Call E Part 19
Custody Documents E Part 20
Custody Note E Part 20
Custody Register E Part 20
Daily Plant Sheet E Part 20
Dashboard B Part 9
Daywork Sheet E Part 12
Daywork Sheets E Part 12
Delay Causes E Part 18
Delay Events E Part 18
Delay Notices Due E Part 18
Delayed Work Orders E Part 17
Delays and Stoppages E Part 18
Delegations E Part 24
Downtime Analysis E Part 20
Drawing Disciplines E Part 21
Drawing Register E Part 21
Drawing Revisions E Part 21
Due for Service E Part 20
Equipment B Part 8
Everything Holding a Job Open E Part 13
Exceptions E Part 19
Executive Dashboard E Part 26
Expense Categories B Part 4
Exposure E Part 12
Extension of Time Claims E Part 18
Final Account Statement E Part 13
Final Accounts E Part 13
Finance E Part 26
Fleet Availability E Part 20
Floats E Part 20
Floats Needing Top-Up E Part 20
Forms of Contract E Part 14
Gangs E Part 17
Gangs Below Norm E Part 17
Generate Work Orders from BoQ E Part 17
Goods Received E Part 16
Hold Points Awaiting Release E Part 22
Hour Meter Readings E Part 20
Idle and Overdue Plant E Part 20
Incidents and Near Misses E Part 22
Inspection and Test Plans E Part 22

Inspections E Part 22
Interim Valuations E Part 11
Issue to Work E Part 16
Job Cost Sheet E Part 15
Job Sheets E Part 17
Jobs Losing Money E Part 15
Labour Allocations E Part 17
Labour Analysis B Part 9
Labour Logs B Part 8
Labour Types B Part 4
Lines Over Budget E Part 15
Live Margin by Job E Part 24
Locations E Part 22
Loss and Expense E Part 13
Maintenance Requests E Part 20
Manpower Histogram E Part 17
Manpower Requests E Part 17
Margin by Job E Part 24
Material Reconciliation E Part 16
Material Requisition B Part 7
Material Requisitions B Part 7
Materials B Part 7
Measured Quantities E Part 11
Measurement Book E Part 11
Measurement Sheet E Part 11
My Site Check-In E Part 19
Nobody Chased This E Part 13
Non-conformance Reports E Part 22
Opportunities E Part 10
Order Variations E Part 14
Outstanding Information E Part 21
Packages E Part 14
Payment Certificate E Part 11
Payment Certificates E Part 11
Period Lock / Close Month E Part 24
Permit Board E Part 22
Permit Types E Part 22
Permits to Work E Part 22
Petty Cash Ledger E Part 20
Phases B Part 6
Pipeline E Part 10
Plant Categories E Part 20
Plant Hire E Part 20
Plant Utilisation E Part 19
Procurement E Part 26
Programmes E Part 18
Project Progress Report B Part 9
Project Templates E Part 24
Projects B Part 5
Provisional Sums E Part 12
Purchase Orders E Part 16
Purposes of Issue E Part 21
QHSE E Part 26
Quotations E Part 10
Quote Comparison E Part 16
Raise a Valuation E Part 11
Rate Library E Part 6
Reconciliations E Part 15
Requests for Information E Part 21
Requests for Quotation E Part 10
Requisitions E Part 16
Retention Held and Due E Part 24
Retention Ledger E Part 13
Review Stamps E Part 21
RFI Categories E Part 21
RFIs Holding Up Work E Part 18
Running Account (RA) Bill E Part 11
Schedule (Gantt) E Part 18
Settings B Part 4
Site Diaries E Part 19
Site Expenses B Part 8
Site Instructions E Part 12
Site Manager E Part 26
Site Stores E Part 16
Site Transfers E Part 16
Snags E Part 22
Snags Holding Retention E Part 13
Subcontract Valuations E Part 14
Subcontractor Bills E Part 14
Subcontracts B Part 8
Submittal Types E Part 21
Submittals E Part 21

Tender / Estimating E Part 26
Tender Loss Reasons E Part 10
Tender Stages E Part 10
Tender Submission Summary E Part 10
To Approve E Part 19
Today E Part 19
Toolbox Talk Topics E Part 20
Toolbox Talks E Part 20
Tools E Part 20
Tracked Materials E Part 16
Transactions E Part 20
Transmittals E Part 21
Unconfirmed Verbal Instructions E Part 12
Unsigned Daywork Sheets E Part 12
Valuation Methods E Part 12
Variation Exposure E Part 24
Variation Order E Part 12
Variations E Part 12
Waiting on Me E Part 24
Waste by Material E Part 16
Weather Log E Part 19
Who Had What E Part 21
Who Has Which Role E Part 25
Work Order Job Card E Part 17
Work Orders E Part 17
Work Types B Part 4
